BETA UNIT

PLAN OF DEVELOPMENT

U.S. GEOLOGICAL SURVEY
RECEIVED
FEB 27 1978
LOS ANGELES

SHELL OIL COMPANY
UNIT OPERATOR
OCTOBER 1977

PLAN OF DEVELOPMENT

OF

THE BETA UNIT

Including

Parcels Covered By Leases

OCS-P 0296
OCS-P 0300
OCS-P 0301
OCS-P 0306
and
Unleased Tract 255

GEOLOGICAL SURVEY
RECEIVED
FEB 27 1978
LOS ANGELES

PREPARED AND SUBMITTED
BY
SHELL OIL COMPANY
UNIT OPERATOR
OCTOBER 1977

PLAN OF DEVELOPMENT

TABLE OF CONTENTS

I. INTRODUCTION

II. GEOLOGIC SETTING

III. FIELD HISTORY AND RESERVOIR EVALUATION

IV. PLATFORM STRUCTURE AND SITE

V. DRILLING FACILITIES

VI. PLATFORM FACILITIES

VII. SUBSEA PIPELINES AND ONSHORE FACILITIES

VIII. APPENDIX

SECTION I

INTRODUCTION

Shell Oil Company is to be the initial operator for the proposed Beta Unit. Other potential participants are Aminoil USA, Inc., Champlin Oil Company, Chanslor-Western Oil and Development Company, Chevron USA, Inc., Getty Oil Company, Hamilton Brothers Oil Company, Occidental Petroleum Company, and Union Oil Company of California. The Unit is located in Federal waters in the San Pedro Bay about nine miles off the Huntington Beach coast. It is to include 28,800 surface acres on five parcels covered by OCS Sale 35 Leases P-0296, P-0300, P-0301, P-0306 and the unleased Tract 255.

In accordance with Title 30, Code of Federal Regulation, 250.34, OCS Order Number 8, Pacific Region and the proposed OCS Order Number 15, this Plan of Development for the Beta Unit is submitted for approval. It includes the following: the geologic setting, field history and reservoir evaluation, platforms, drilling plans and facilities, production plans and facilities, pipelines and shore facilities and an appendix. Oil spill contingency plans are included in the appendix.

This plan covers the initial development program which includes:

1) Fabrication and installation of a drilling platform jacket and decks in 265 feet of water (Platform Ellen).

2) Fabrication and installation of a companion production platform and decks in 255 feet of water (Platform Elly) connected to the drilling Platform Ellen by a 200-foot bridge.

3) Fabrication and installation on the production Platform Elly facilities necessary

   a) to test, collect, separate, heat, treat, dehydrate, measure and transport the production

   b) to clean, treat, pressure and inject both the produced water and source water for waterflooding operations

   c) to generate the necessary power for artificial lift, injection, compression, transport, etc.

4) Construction and installation of two API type drilling rigs on the drilling Platform Ellen

5) Installation of a clean oil line to shore with sufficient onshore facilities to measure and distribute the oil to the various local refineries.

The plan envisions that an additional drilling platform in 700 feet of water will be required to develop the accumulation. The production Platform Elly will have the potential capacity to process the foreseeable production from the field.

From the drilling Platform Ellen, we plan the capability of drilling up to 80 wells including service and waterflood injectors, at angles up to 70°.

The exploration program indicates that the accumulation contains oil in seven separate producing intervals, A through G. Gas-oil ratios range from 160 to 230 cubic feet per barrel. Oil gravities range from 10-12° API in the A and G zones to 20-22° API in the upper D zone. Oil production from the drilling Platform Ellen is expected to peak at a rate of about 16,000 B/D in 1982 if the development program is not delayed. The estimated peak rate from both the 265 and 700-foot water depth drilling platforms will be 26,000 B/D of 14-16° API oil in 1984 if our development plan proceeds according to schedule.

That schedule is shown on page 1-3.

BETA FIELD DEVELOPMENT PLAN

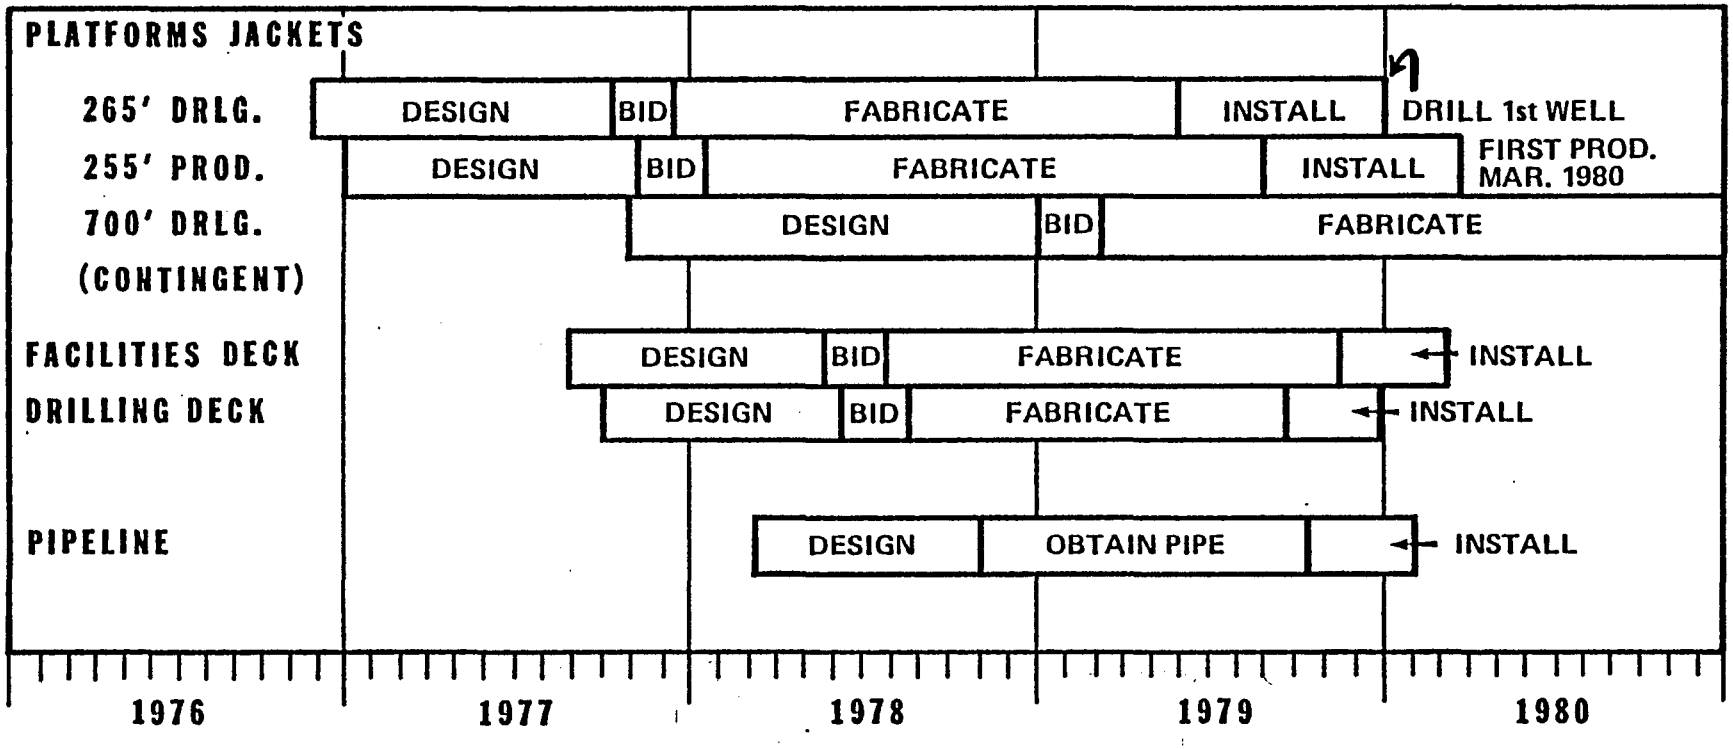

9/20/77

ZF 2714 10/77

SECTION II

Not for Public Release

GEOLOGIC SETTING

TABLE OF CONTENTS

		Page
2.1	Introduction	2-1
2.2	Area Geology	2-1
2.3	Attachments	

Figure No. 2-1	Index map of Southern California
Figure No. 2-2	Location map of San Pedro Bay and Vicinity
Figure No. 2-3	Structure Map (Upper Miocene Layer)
Figure No. 2-4	Cross section through shallow water platform site area
Figure No. 2-5	Quarternary Stratigraphy

SECTION III

Not for Public Release

FIELD HISTORY AND RESERVOIR EVALUATION

TABLE OF CONTENTS

		Page
3.1	Drilling History of OCS Tracts 254, 261 and 262 (Leases OCS-P-0296, P-0300, and P-0301)	3-1
3.2	Reservoir Description	3-1
3.3	Well Test Data	3-2
3.4	Reservoir Fluid Properties	3-2
3.5	Development Plans	3-3
3.6	Anticipated Production	3-3
3.7	Attachments	

Figure 3-1 Structure Map, Top of "D" Sand
Figure 3-2 X-Section B-B
Figure 3-3 Gravity Curves
Figure 3-4 Gravity Curves
Figure 3-5 Oil Viscosity vs. Gravity Correlation
Figure 3-6 Fluid Properties
Figure 3-7 Well Locations and Productive Limits Map
Table 3-1 Pre-Lease Sale Drilling Activity
Table 3-2 Beta Pre-development Drilling Activity
Table 3-3 Production Test Data Well P-0301-1
Table 3-4 Production Test Data Well P-0301-2
Table 3-5 Production Test Data Well P-0301-3
Table 3-6 Production Test Data Well P-0300-2
Table 3-7 Production Test Data Well P-0294 wells
Table 3-8 Well Test Analysis Summary

SECTION IV

PLATFORM SITE AND STRUCTURES

TABLE OF CONTENTS

	Page
4.1 Introduction	4-1
4.2 Geotechnical Considerations	4-1
4.2.1 Bathymetry	
4.2.2 Soil Conditions	
4.2.3 Near-Surface Faulting	
4.2.4 Slope Stability	
4.2.5 Hydrocarbon Seeps	
4.2.6 Subsidence	
4.2.7 Hydrology	
4.3 Oceanographic Design Criteria	4-4
4.4 Earthquake Design Criteria	4-5
4.5 Corrosion Control	4-5
4.6 Shipping Lanes	4-6
4.7 Platform Visibility	4-6
4.8 Cultural Resources	4-6
4.9 Platform Analysis	4-7
4.10 Fabrication and Installation	4-7
4.11 Platform Removal	4-8
4.12 Attachments	
Figure 4-1 Drilling Platform	
Figure 4-2 Production Platform	
Figure 4-3 Geotechnical Considerations	
Figure 4-4 Photograph showing visibility from Huntington Beach of the proposed platforms on a clear day	

SECTION IV

PLATFORM SITE AND STRUCTURES

4.1 Introduction

The Beta Field will initially be developed with a drilling platform and a companion production platform. The drilling platform, as shown in Figure 4-1, will be a standard 8-leg jacket located in 265 feet of water. The platform will have two deck levels, each about 108 feet by 175 feet, with space for 80 wells and two drilling rigs. The production platform, shown in Figure 4-2, will be a 12-leg jacket in 255 feet of water. Located on two deck levels, each about 200 feet by 140 feet, will be enough space for handling all expected production at Beta. A personnel and pipeline bridge about 200 feet long will link the two platforms.

Both platforms were designed in accordance with the latest drafts of USGS OCS Order No. 8 and API RP 2A to safely withstand the loads caused by severe storm waves or earthquakes or during launching and installation. The platforms' main legs are framed with diagonal and horizontal bracing which provides a high level of redundancy and adds substantially to the structural integrity. The structures will be secured to the ocean bottom with piles driven through and welded to the legs of the jackets. Because the platforms will be near the Palos Verdes and Newport-Inglewood faults and close to the San Pedro shelf edge, we have paid special attention to seismic design criteria and soil stability analysis. Further details on these topics, oceanographic criteria, platform analyses, fabrication and installation are summarized below. More details are included in the reports on the geological and geophysical site evaluations, soil borings, and oceanographic conditions which are listed as Appendices 8.1 through 8.5.

4.2 Geotechnical Considerations

The drilling and production platforms are sited in areas which are safe from potential hazards such as near-surface faults and areas of possible soil instability. The location of the platforms with respect to these geotechnical considerations is shown in Figure 4-3.

4.2.1 Bathymetry

The seafloor in the area of the platform site is essentially featureless and slopes to the southeast at about 2 degrees. (Figure 4-3). Further details on bathymetry in the area are discussed in a report by MESA, Inc. (Appendix 8.1)

4.2.2 Soil Conditions

Three soil borings have been drilled in the vicinity of the site as shown on Figure 4-3. Borings 261-1 and 261-2 were drilled to depths of 463 feet and 61 feet respectively and Boring 262-1 was drilled to a depth of 500 feet. Detailed logs of these borings and the results of basic soil mechanics tests are given in the reports by Woodward-Clyde Consultants (Appendices 8.2 and 8.3). Additional information on the stratigraphy and depositional history is included in Appendix 8.1.

Briefly, the soils in the vicinity of the proposed platform site are marine Holocene and fluvial-marine Late Pleistocene clastic sediments. At Boring 261-1, the Holocene section is about 40 feet thick and consists of clayey silt and silty clay layers and a basal silty sand layer. The underlying Late Pleistocene units consist of sand and gravel channel-fill to a depth of about 80 feet and then predominantly clayey silts to the depth explored. In Boring 261-1, there is a lower gravel layer from a depth of 225 feet to 250 feet within the clayey silts.

A final site investigation will be conducted at the proposed platform site in the near future. Static and cyclic loading tests have been conducted on soil samples obtained in the preliminary borings. Similar tests will be conducted on samples obtained in the final soil borings. These final borings and laboratory tests will be used to finalize the foundation design including pile length, wall thickness and driveability.

4.2.3 Near-surface Faulting

In order to guide the final siting of the platforms in the optimum location relative to both near-surface faulting and any areas of potential instability, a detailed geophysical study was conducted over an area of 8.5 square miles which includes the platform site. This survey was run by General Oceanographics, Inc., using precision bathymetric profiling, Uniboom, sparker, side scan sonar and magnetometer equipment on a 500-foot square grid over most of the area. Within this area a 2-square mile segment was surveyed using the Sonia subbottom profiler on a 250-foot square grid. A portion of the interpreted geophysical data in Appendix 8.1 is reproduced as Figure 4-3.

The platform site is located near the Palos Verdes fault zone and a fault zone which is located along the San Gabriel submarine canyon. Two minor faults are located

between these major fault zones and a zone of minor transverse faults appears to be located in the vicinity of the disturbed area downslope from the platform site. The relationship of these near-surface faults to deeper faults and folds in the vicinity of the platform sites has been discussed in Section 2.2. A report by Damei and Moore, Geoseismic Investigation of the Palos Verdes Fault Zone, (Appendix 8.5) assesses the seismic activity along the Palos Verdes and Newport-Inglewood Faults.

4.2.4 Slope Stability

On the basis of the surveys described in Section 4.2.3, we conclude (Appendix 8.1) that the survey area and the adjacent shelf-basin slope are stable. There is no evidence of slumping or downslope movement in the strata at the platform site. From this investigation, there is no reason to anticipate liquefaction or other instability at the site.

South and southwest of the site, two small areas have been identified as possibly having past instability. These are shown as "disturbed areas" on Figure 4-3. The area 2000 feet to the southwest of the platform site appears to be a slide associated with fault F3 but is also subject to alternative interpretations. The area 1200 feet downslope from the platform site corresponds to a topographic bulge, and there is a lack of continuity of reflectors in this area. The feature is located immediately below the Late Pleistocene shelf break and may be related to either depositional processes or slumping related to the shelf break or to movement along a series of minor transverse faults. In the San Gabriel submarine canyon, over 4000 feet east of the platform site, the walls are generally stable at slopes of as much as 30 degrees.

4.2.5 Hydrocarbon Seeps

In a review of all available fathometer, water column bubble detector and high resolution geophysical profiles and side scan sonar records, MESA², Inc. identified and mapped only three questionable seeps within 1000 feet of the shallow water site (Figure 4-3). These seeps are not considered to be hazards because they are not associated with faults, seafloor disruption or anomalous reflections on geophysical records.

No gas was encountered in the shallow section during the drilling of six exploratory wells and three soil borings in the area. Additionally, higher resolution and more

closely spaced geophysical data indicates that most of the zones which are mapped as possible gas by BBN-Geomarine Services Company in a report (refer to Section 4.8) on potential shallow drilling hazards are instead zones that reflect contrasting lithologies.

4.2.6 Subsidence

The potential for surface subsidence due to reservoir fluid withdrawal is negligible. A pressure maintenance program using water injection will begin soon after the start of production and continue throughout the life of the field. Little or no reduction in pore pressure is anticipated; accordingly, no compensating settlement of overburden is expected.

4.2.7 Hydrology

Electric logs indicate that exploratory wells penetrated no fresh water sands. However, if fresh water sands are encountered during development drilling, they will be isolated from deeper zones containing salt water or hydrocarbons by setting and cementing casing before drilling below their base.

4.3 Oceanographic Design Criteria

The platforms have been designed for severe storms having less than a one percent chance of exceedance in a given year. The design wave, wind, currents, and tide criteria for the site are as follows:

Wave	
Maximum Height (Crest-Trough)	45 feet
Period of Maximum Wave	9 to 15 seconds
Wind (5 second average; assumed in the wave direction; measured at +30 ft. elevation)	64 knots
Current (assumed in the wave direction)	
Surface	2.8 fps
Mid-depth	1.6 fps
Bottom	0.6 fps
Tide (including storm surge)	6.0 feet (above MLLW)

These oceanographic design criteria were derived from a study by Evans Hamilton, Inc. (Appendix 8.4). Normal oceanographic/ meteorological conditions were found to be favorable for operations.

4.4 Earthquake Design Criteria

The location of the Beta Field within an area of recognized seismicity requires that all structures be designed for an earthquake environment. The platforms have been designed for a two-level design requirement as outlined in API RP 2A. For the first level earthquake criteria, the platforms will resist shaking having a low probability of occurrence without damage. All platform structural members would remain elastic.
For the Beta Field, this criteria is defined by Zone 4, Soil Type C in 1977 API RP 2A. Peak horizontal acceleration is 0.25g. The probability that the platforms will experience this earthquake activity is about 0.005 per year - a 200 year recurrence interval.

Furthermore, the platforms can safely withstand the second level criteria, associated with a rare intense earthquake, without collapse. In this unlikely event, some members would suffer inelastic deformation but the platforms possess the necessary ductility and redundancy to prevent collapse. Ground motions are twice those of the first level criteria. At the Beta Field, the probability of an earthquake exceeding this criteria is less than 0.001 per year - a recurrence interval greater than 1000 years.

4.5 Corrosion Control

The platform will be protected from corrosion by coatings in the splash zone and above, and by cathodic protection below mean water level.

The protective coating system is an established concept and employs standard materials used in accordance with conventional corrosion protection practices. It has been used successfully for over ten years in the Gulf of Mexico. Two types of protective coatings are used:

1. Galvanizing applied to grating, ladders, cages and other difficult to paint hardware.

2. Painting the exterior surfaces of the structures will be multi-coated from the minus 8-foot elevation to the top of the structure with an inorganic zinc-vinyl system.

A conventional sacrificial anode system will provide the corrosion protection for the below-water portion of the platforms. Aluminum anodes will be uniformly located throughout the structures as a function of the structures' surface area and projected life.

4.6 Shipping Lanes

While the proposed platform development plan is within the Gulf of Santa Catalina Traffic Separation Scheme, it is clear of both traffic lanes and their buffer zones. Navigational aids will be installed and maintained as required by the Coast Guard. The structures will have a beneficial effect by acting as aids to navigation.

The contingent deep-water platform, in about 700 feet of water, is within the Buffer Zone. However, since the Traffic Separation Scheme will not be permanently fixed until substantial exploratory drilling has been completed, and since just a slight shift of the scheme would put the platform location within the Separation Zone, we believe that the contingent platform will not hinder shipping. As plans for this platform are finalized, we will keep the appropriate agencies informed of our siting constraints.

4.7 Platform Visibility

Lease stipulations require that these platforms be camouflaged by appropriate painting. We suggest that the Supervisor, in consultation with the Coast Guard and the Operator, determine the appropriate color.

Figure 4 is the view from the bluff at Huntington Beach looking toward the platform site. In the foreground is Aminoil's Platform Emmy about 1.3 miles offshore. The exploratory drilling rig just to the left of the center of the picture is near the platform site. The other drilling rig, further to the left is near the contingent deep water platform site. Visibility conditions equal to or better than this probably occur less than 10 percent of the time. Therefore, the platforms should not be visible from shore 90 percent of the time.

4.8 Cultural Resources

An assessment of cultural resources is included in a report by BBN-Geomarine Services Company entitled "Geophysical Interpretation and Assessment of Cultural Resources and Potential Shallow Drilling Hazards for a Part of Offshore California Tracts 035-261 and 035-262 San Pedro Bay, dated April 1976. This report has been previously submitted to the Oil and Gas Supervisor, Pacific Area, U. S. Geological Survey. An interpretation of additional magnetometer records is included in Appendix 8.1. No magnetic anomalies or seafloor objects were identified in the area of the platform sites by either study.

4.9 Platform Analysis

The structures have been designed for the described combinations of environmental conditions, operational loads, gravity, buoyancy, and pressures associated with fabrication, transportation, installation, and use in their proposed offshore location. Analytically determined member stresses are limited to the allowable stresses and other design limitations set forth in API RP 2A.

The design wave condition was analyzed utilizing a Shell-developed three dimensional computer program. The design wave was stepped through the structure and the wave position causing the largest base shear was determined. The structural model was then analyzed using the joint loads corresponding to the largest base shear. The pile-soil system was modeled using the static nonlinear load-deflection characteristics of the soil.

The earthquake analyses were performed utilizing two dynamic response computer programs. The platforms were designed utilizing scaled recorded time histories, artificial time histories and the response spectra as given in API RP 2A for Zone 4 and soil type C. The elastic level earthquake (.25 g peak acceleration) was analyzed using a Shell-developed three dimensional finite element program capable of performing both time history and response spectrum analyses. The inelastic analyses were performed using a two dimensional inelastic frame analysis program specifically developed for this application. Scaled time histories of ground motion were input and the platforms checked for the required ductility. These analyses included non-linear modeling of the structure-foundation systems.

Load-out, launch and installation of the platforms were also analyzed and all members designed for these forces. The platforms are designed to be stable under launch and during installation before the piling are fully installed.

4.10 Fabrication and Installation

The jacket type platform is a proven concept for offshore structures. The principal components of this type of platform are the deck, the jacket, and the piling. To implement this project, a contractor or contractors will fabricate and assemble these components, and barge them from the assembly yard to the offshore site for the installation. Sites for construction and assembly will be determined when contracts are awarded. The jackets, after being transported to the site on a launch barge will be launched and then lowered to the ocean floor by a derrick barge assisted by controlled flooding of the jacket. After the jacket is secured by piling, the deck

sections and equipment will be set in place on the jacket. Jacket installation is currently scheduled for 1979.

4.11 Platform Removal

Following the depletion of all producing zones developed from the platforms, the site will be cleared in accordance with permit requirements.

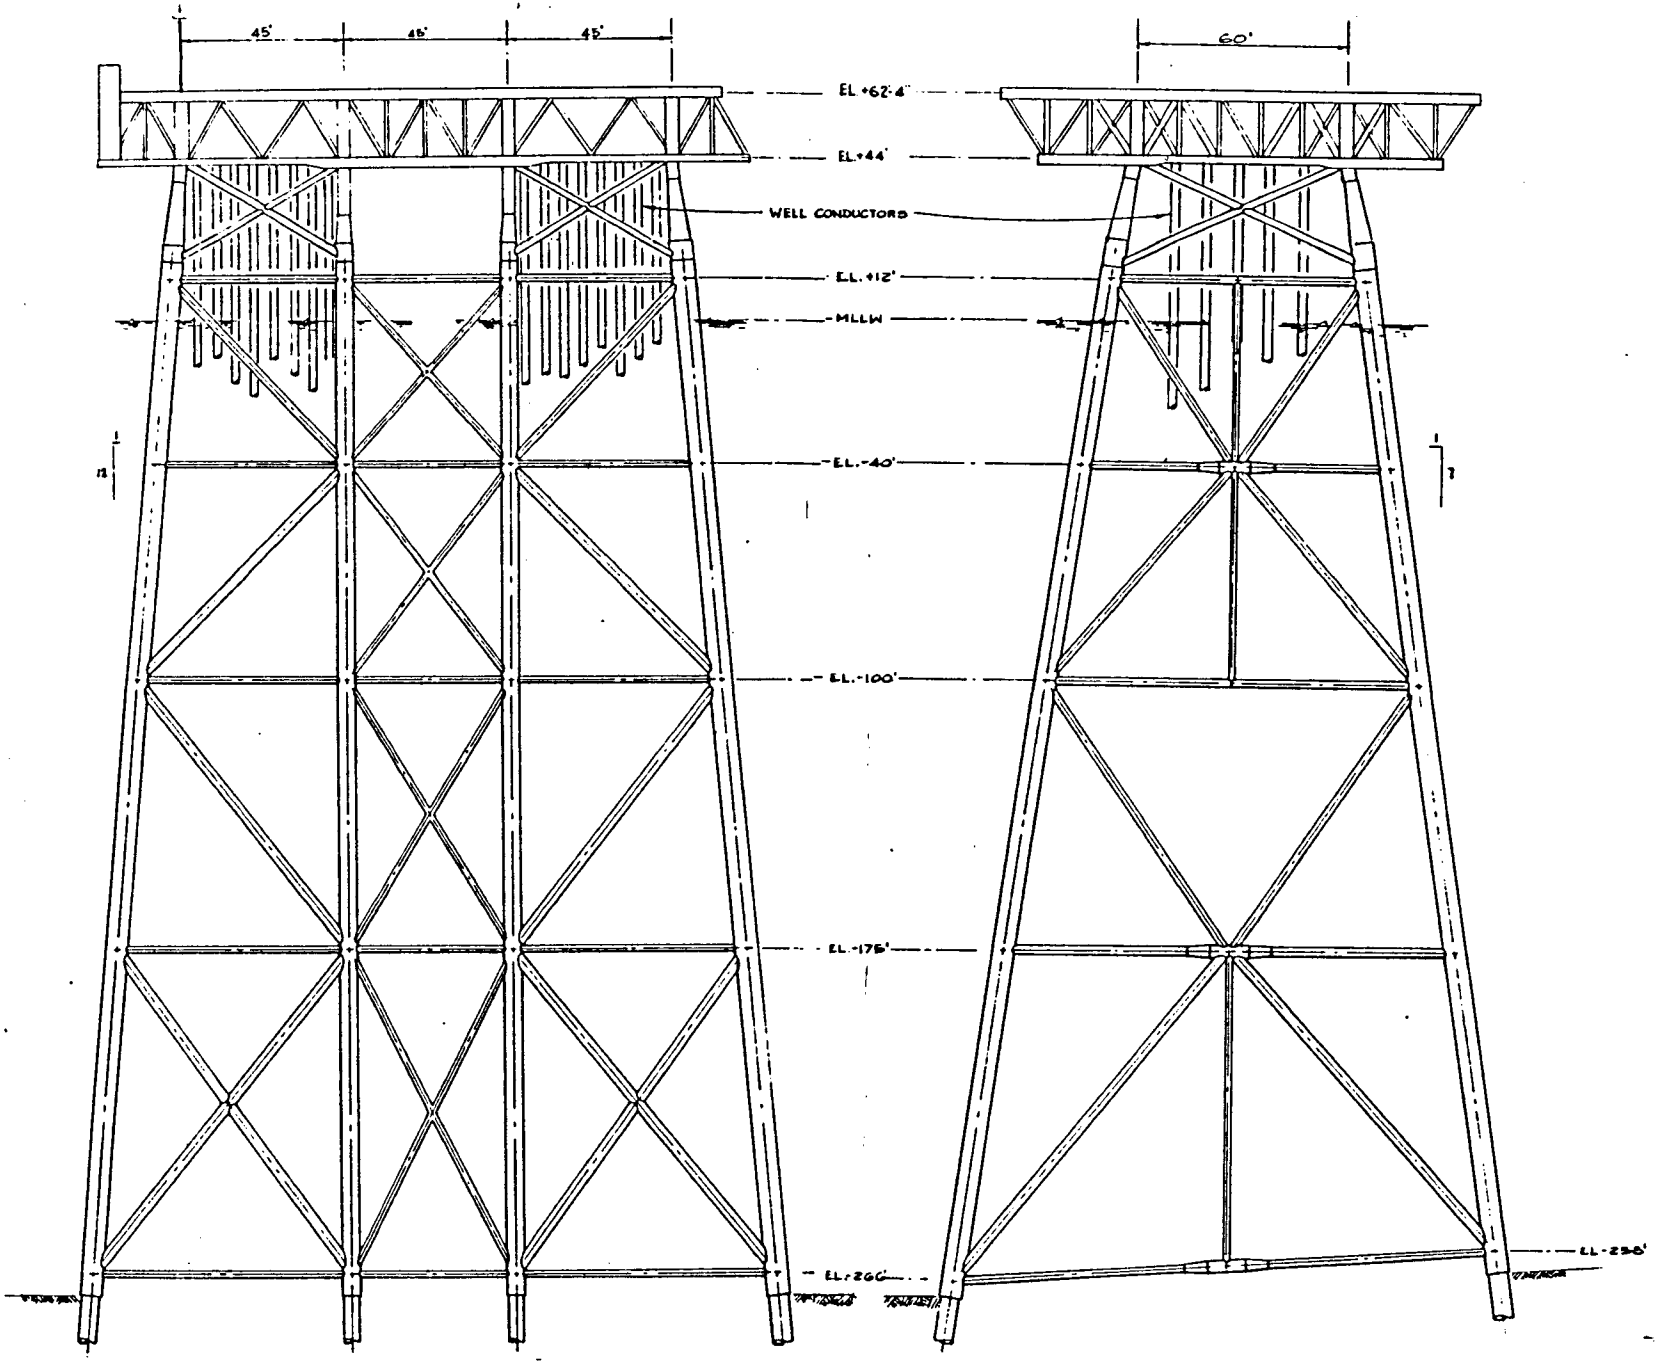

DRILLING PLATFORM
SAN PEDRO BLOCK 261

FIGURE 4-1

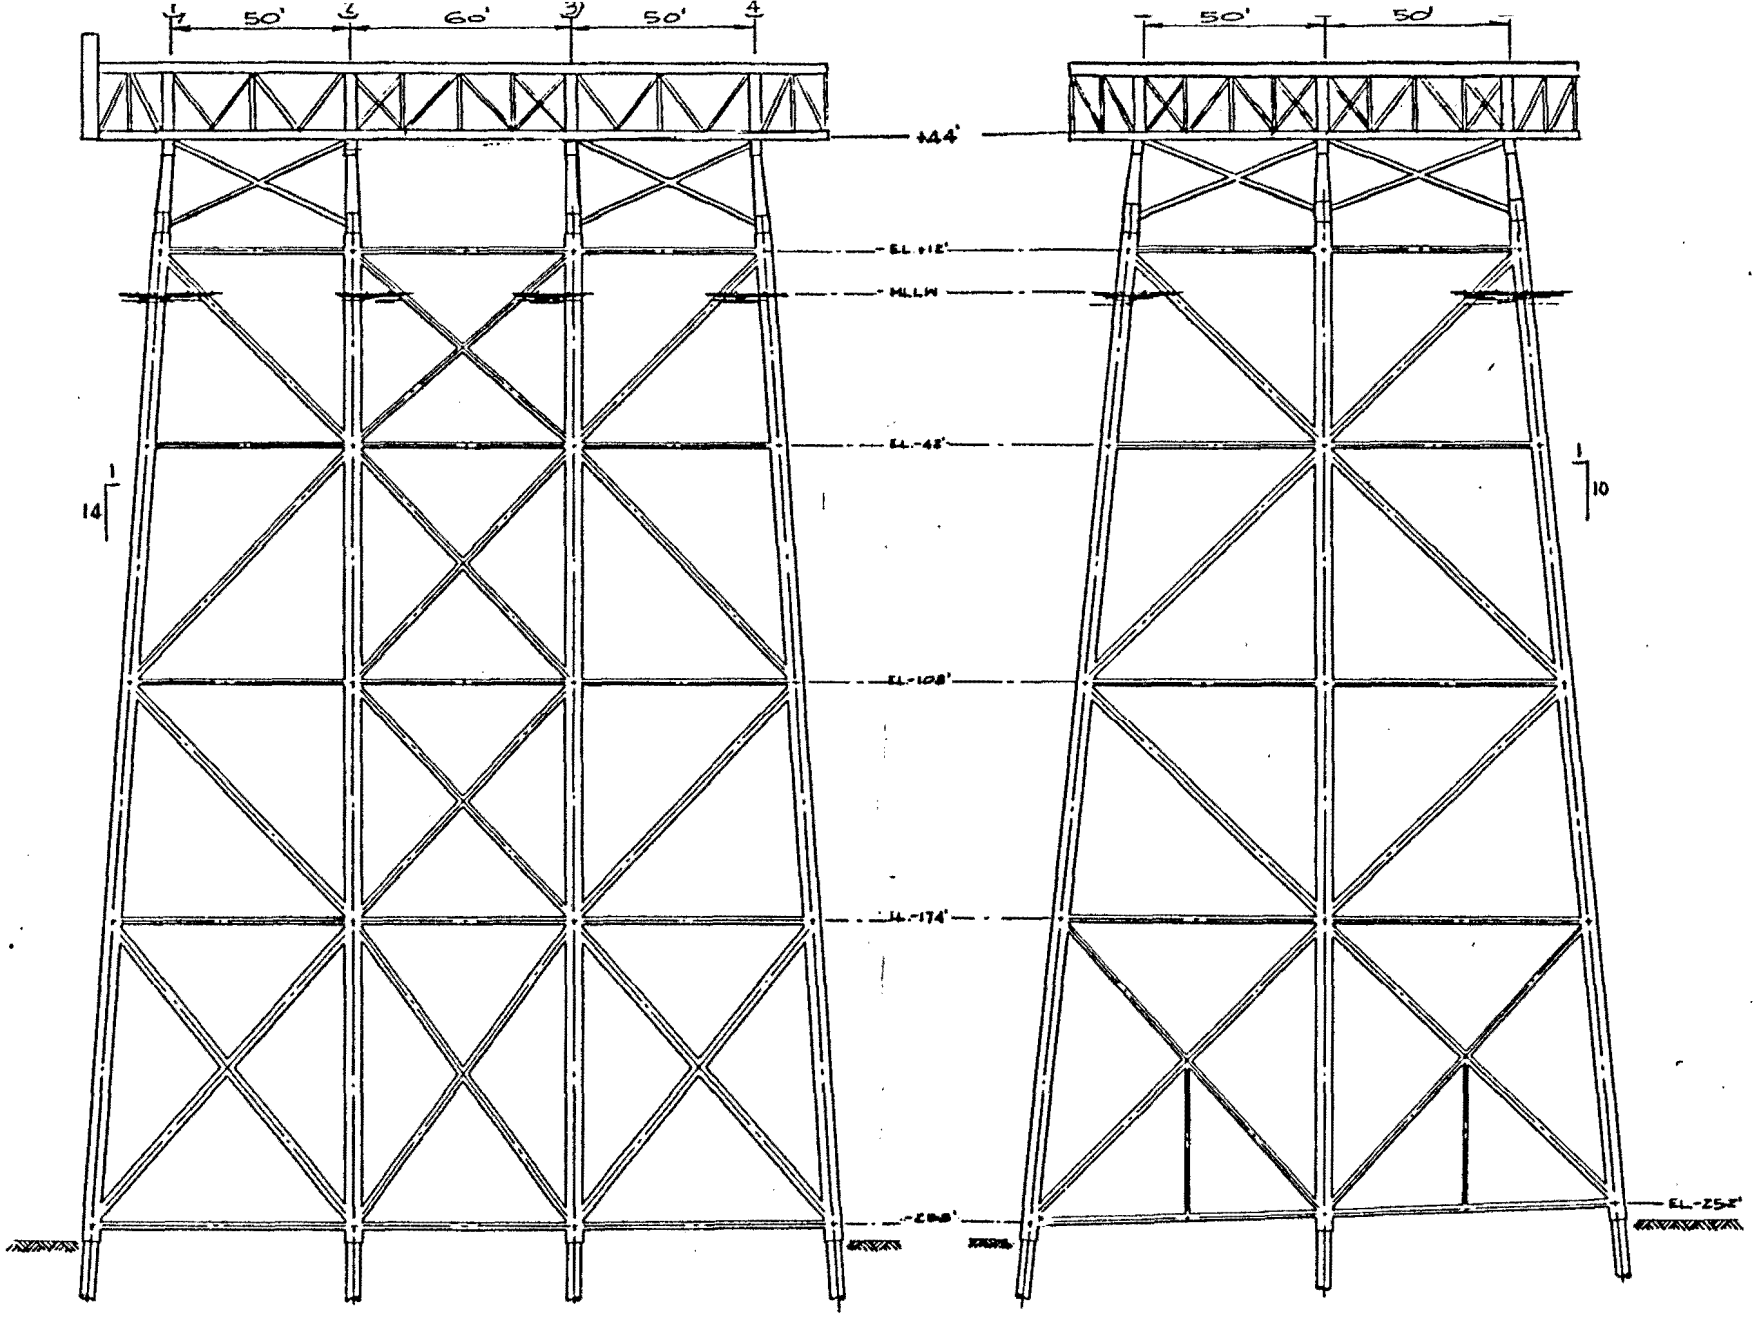

PRODUCTION PLATFORM
SAN PEDRO BLOCK 261

FIGURE 4-2

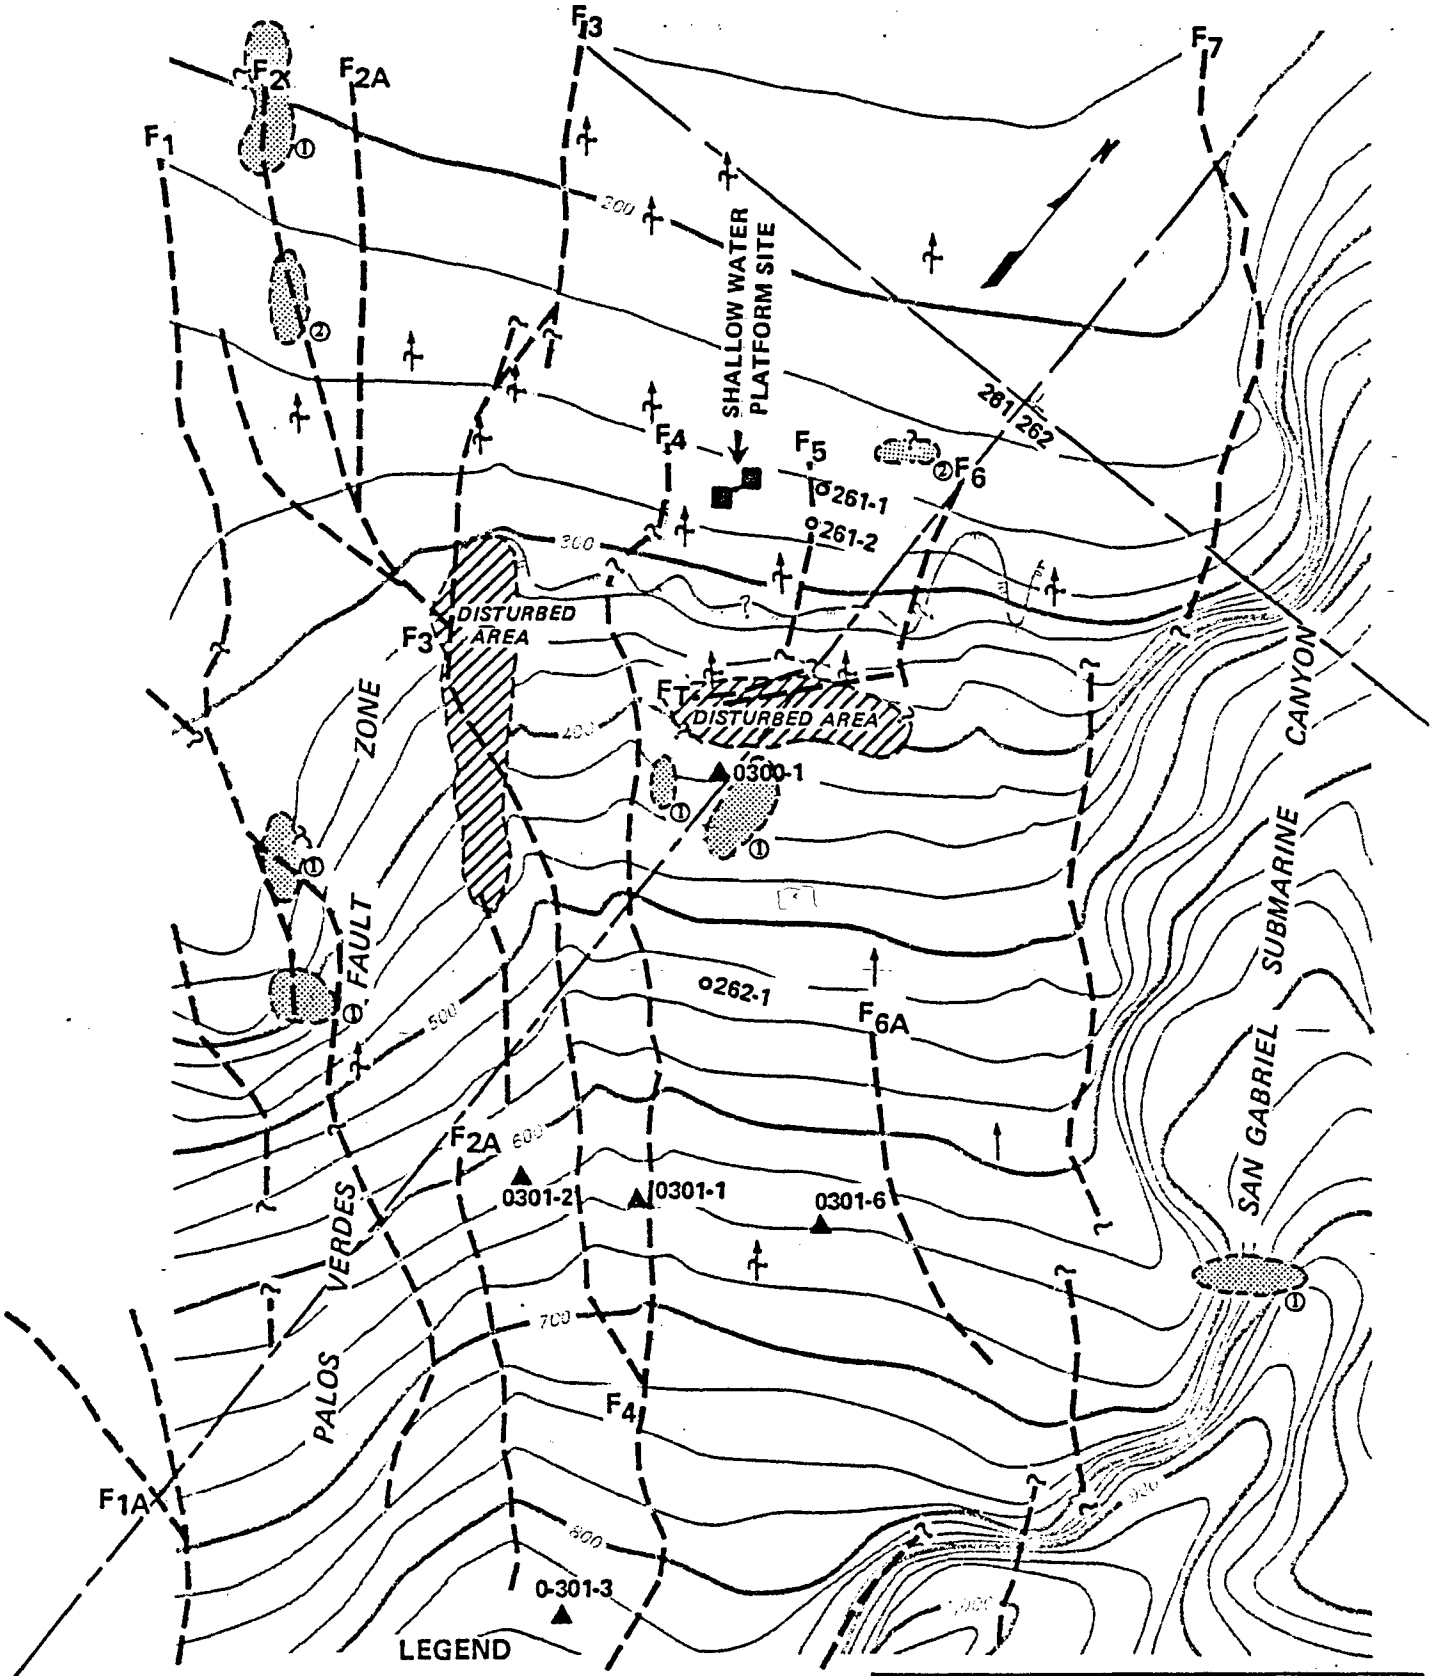

FAULTS MAPPED NEAR SURFACE

PALEO SHELF BREAK

TOPOGRAPHIC AND/OR STRUCTURAL ANOMALY

GAS AND OIL(?) SEEP

GAS AND OIL(?) SEEP AREA

① DEFINITE

② PROBABLE

? QESTIONABLE

▲ EXPLORATION WELLS

o SOIL BORING

CONTOURS ARE WATER DEPTH IN FEET

SHELL OIL COMPANY	WESTERN E & P REGION WESTERN DIVISION	PRODUCTION DEPARTMENT

GEOTECHNICAL CONSIDERATIONS

OCS NO. P-0300,P-0301

TRACT NO. 35-261,262

BLOCK NO. 33 N-37W,36W

0' 1000' 2000'

By: RCS	Date: 11-1-77	File: ZF-2752
For:	FIGURE 4-3	Encl.:

Figure 4

SECTION V

DRILLING FACILITIES

TABLE OF CONTENTS

		Page
5.1	Introduction	5-1
5.2	Drilling Equipment	5-1
5.2.1	Rig Components	
5.2.2	Substructures	
5.2.3	Drilling Mud System	
5.2.4	Cementing Unit	
5.2.5	General Layout	
5.3	Drilling Operations	5-3
5.3.1	Casing Program	
5.3.2	Well Completions	
5.3.3	Wellhead Equipment	
5.3.4	Blowout Preventer Equipment	
5.3.5	Drilling Platform Drainage	
5.3.6	Safety	
5.3.7	Fire Prevention and Suppression	
5.3.8	Crew and Supply Transport	
5.4	Attachments	

Figure 5-1 - Top Deck Equipment Layout, Drilling Platform
Figure 5-2 - Lower Deck Equipment Layout Drilling Platform
Figure 5-3 - Proposed Casing Program
Figure 5-4 - Cased Hole Type Completion
Figure 5-5 - Open Hole Type Completion
Figure 5-6 - Combination Type Completion

SECTION V

DRILLING FACILITIES

5.1 Introduction

The 265-foot water depth drilling platform will have slots for a maximum of 80 wells. Two drilling rigs and associated crews and services will be required to drill the wells presently planned.

Preliminary drilling equipment layouts are shown as drawings at the end of this section. The rigs will be platform-type rigs. After the initial drilling phase is completed, one rig will be removed. The rig left on the platform will be designed to move from one end to the other as required for well servicing, work-overs and redrills. The deep-water platform will be designed to accomodate two rigs. One of the rigs will be a platform-type and designed to be left on the platform to handle well work after the primary drilling phase is completed.

Drilling operations, testing and training, pollution prevention systems and safety systems will be in accordance with OCS and EPA regulations and industry standards.

5.2 Drilling Equipment

5.2.1 Rig Components

Two platform-type derricks, 147 feet high for 12,000 foot drilling and 750,000 pound hook-load capacities, will be used. The derricks will be designed in accordance with A.P.I. Standards.

Drawworks - 1000 H.P. electrically powered.

Rotary Table - Independently powered.

The hook, traveling block, and crown block will be of 350+ ton load rated capacity to match the derrick.

The drill string will be 4½", Grade E drill pipe.

5.2.2 Substructures

A drilling skidbase is to be provided to support the derrick, drawworks subbase, and connecting stairways.

Each substructure will be supported on a skidbase, which will rest on two elevated skidbeams. The skidbase will be equipped with a hydraulic jacking system to facilitate

movement along the well rows. The substructure will also be equipped with hydraulic jacks for lateral skidding. Mechanical restraint equipment will prevent substructure movement as desired.

5.2.3 Drilling Mud System

A separate mud system will be provided for each drilling rig.

Each rig will be equipped with two mud pumps (800 HP each), a mud slugging tank (100 bbl±), a circulating tank (250 bbl±), and a reserve mud tank (300 bbl±). In addition, a completion fluid system of 1200 barrels will be required. The completion fluid will be used for all underreaming or perforating through the pay interval and for gravel packing operations.

A low solids, gas free mud will be maintained using high speed shale shakers, desanders, desilters, and degassers. The shale shakers will be equipped with cuttings recovery systems to handle any oil-contaminated cuttings for disposal. Cuttings that cannot be adequately cleaned will be diverted to a waste cuttings holding tank, to be hauled ashore for disposal.

Mud volumes will be closely monitored using a pit volume totalizer system, an incremental flowrate indicator, and a precision fill-up measurement system. These warning systems will have visual and audible alarm signals at the driller's console. Bulk material handling system will be provided with 1000 cu. ft. storage capacity for barite. Additional mud and completion fluid additives (chemicals, lost circulation material, gravel, etc.,) will be palletized.

5.2.4 Cementing Unit

For use on both rigs, a diesel powered dual cementing unit and four 1000 cubic foot bulk storage tanks will be provided for well cementing operations. In addition, a single cementing unit when combined with a blender will be used for completion work.

5.2.5 General Layout

The drilling rig will be located on the upper deck. This will include the mud package, power package, skid base, substructure and derrick. The living quarters, offices and heliport will be located above the power package. Above the mud package will be the pipe racks and the rig crane.

On the lower deck will be the cementing units, gravel packing equipment and storage for all liquid and dry material.

5.3 Drilling Operations

5.3.1 Casing Program

Casing setting depths and cementing will be in accordance with the USGS Pacific Area OCS Order No. 2 and/or field rules. The attached casing programs show the USGS exploratory requirements and proposed field rules. Our plan for field rules is based on data from our exploratory drilling, shallow hazard surveys and the soil borings taken to date. Additional soil borings are currently underway.

We have not seen evidence of shallow gas in our exploratory drilling and the shallow seismic data does not indicate the presence of shallow gas. With this data we propose the following casing and drilling program:

1. 24-inch drive pipe be set 200+ feet below the mud line.

2. The conductor casing string be eliminated.

3. The surface casing be set from 1200 to 1500 feet below the mud line.

4. An additional casing string will be set on top of the pay or at T.D. The setting depth of this string will be determined by the well completion program.

5. A total depth of 5000 feet subsea (4735 feet below the mud line). This is the anticipated T.D. of wells drilled on the down dip side of the structure.

The soil borings currently underway will help in determining the depth to which the 24-inch drive pipe can be driven. The 200 feet below the mud line is proposed as a minimum depth for the drive pipe. The additional data will be presented when it becomes available.

5.3.2 Well Completions

The reservoir consists of an assemblage of sands, shales and silts. The thicker shales divide the reservoir into seven zones. Because the sands are unconsolidated, sand control is required and it will be achieved by gravel packing a slotted liner (or screen) inside cemented, jet perforated casing or in underreamed open hole.

Several zones will be simultaneously opened into a common wellbore and interzonal isolation will be needed in some cases to provide for the control of fluids either entering or leaving the wellbore and to allow for the optimum exploitation and conservation of the reserves.

The attached figures, 5-4, 5-5 and 5-6 show schematically the mechanical configurations which will allow both gravel packing and interzonal isolation. It is not possible to select a single completion type at the present time and it is now expected that all of the completion types shown may be used.

5.3.3 Wellhead Equipment

Either unitized or conventional flanged wellheads will be used during the drilling phase. The wellhead assemblies will be suitable for free flow and submersible or hydraulic pumping.

5.3.4 Blowout Preventer Equipment

Low and high pressure blowout preventer systems will be used as required by OCS Order No. 2 and/or field rules. These systems will be hydraulically operated and will include remote control.

The low pressure system will consist of a 21 3/4-inch, 2000 psi annular-type blowout preventer with diverter system installed for drilling below the 24-inch conductor casing string. After 16-inch or 13 3/8-inch surface casing is landed and cemented, the low pressure BOP stack will be removed. A 3000 psi W.P. BOP stack will be installed on the surface casing head. The BOP equipment will include an annular preventer, a blind ram and one pipe ram if approved in field rules.

Both systems will have the appropriate choke manifold, kill and bleed lines, and fill-up lines as required by OCS Order No. 2 and/or field rules.

5.3.5 Drilling Platform Drainage

The drilling platform will be divided into two drainage systems for separate handling. Drainage from the top deck, from drip pans in the rig substructure and from the rig floor will gravitate to a "waste tank" located on the lower deck. Drainage from the lower deck areas will drain to a sump tank below the lower deck, from which the liquids will be pumped into the waste tank. Wash water from the cuttings washer will also gravitate to the waste tank. Oily waste water from the waste tank will be sent to

the production platform for treatment. Washed cuttings and oil free sediments from the waste tank will gravitate to the skim pile for disposal.

5.3.6 Safety

Appropriate OCS and OSHA Safety regulations will be followed.

5.3.7 Fire Prevention and Suppression

In addition to the platform systems described in the Production Facilities section, portable fire extinguishers will be provided for the rig floor and BOP areas.

5.3.8 Crew and Supply Transport

Drilling crews will work regular 8-hour shifts and will be transported between shore and platform by boat. Day shifts are expected to consist of 25 people and night shifts 18 people. Supply boats will transport supplies as required.

Weather should have little effect on boats or crew and supply boat operations, but emergency facilities and supplies will be provided to allow at least one week of normal operations under storm conditions.

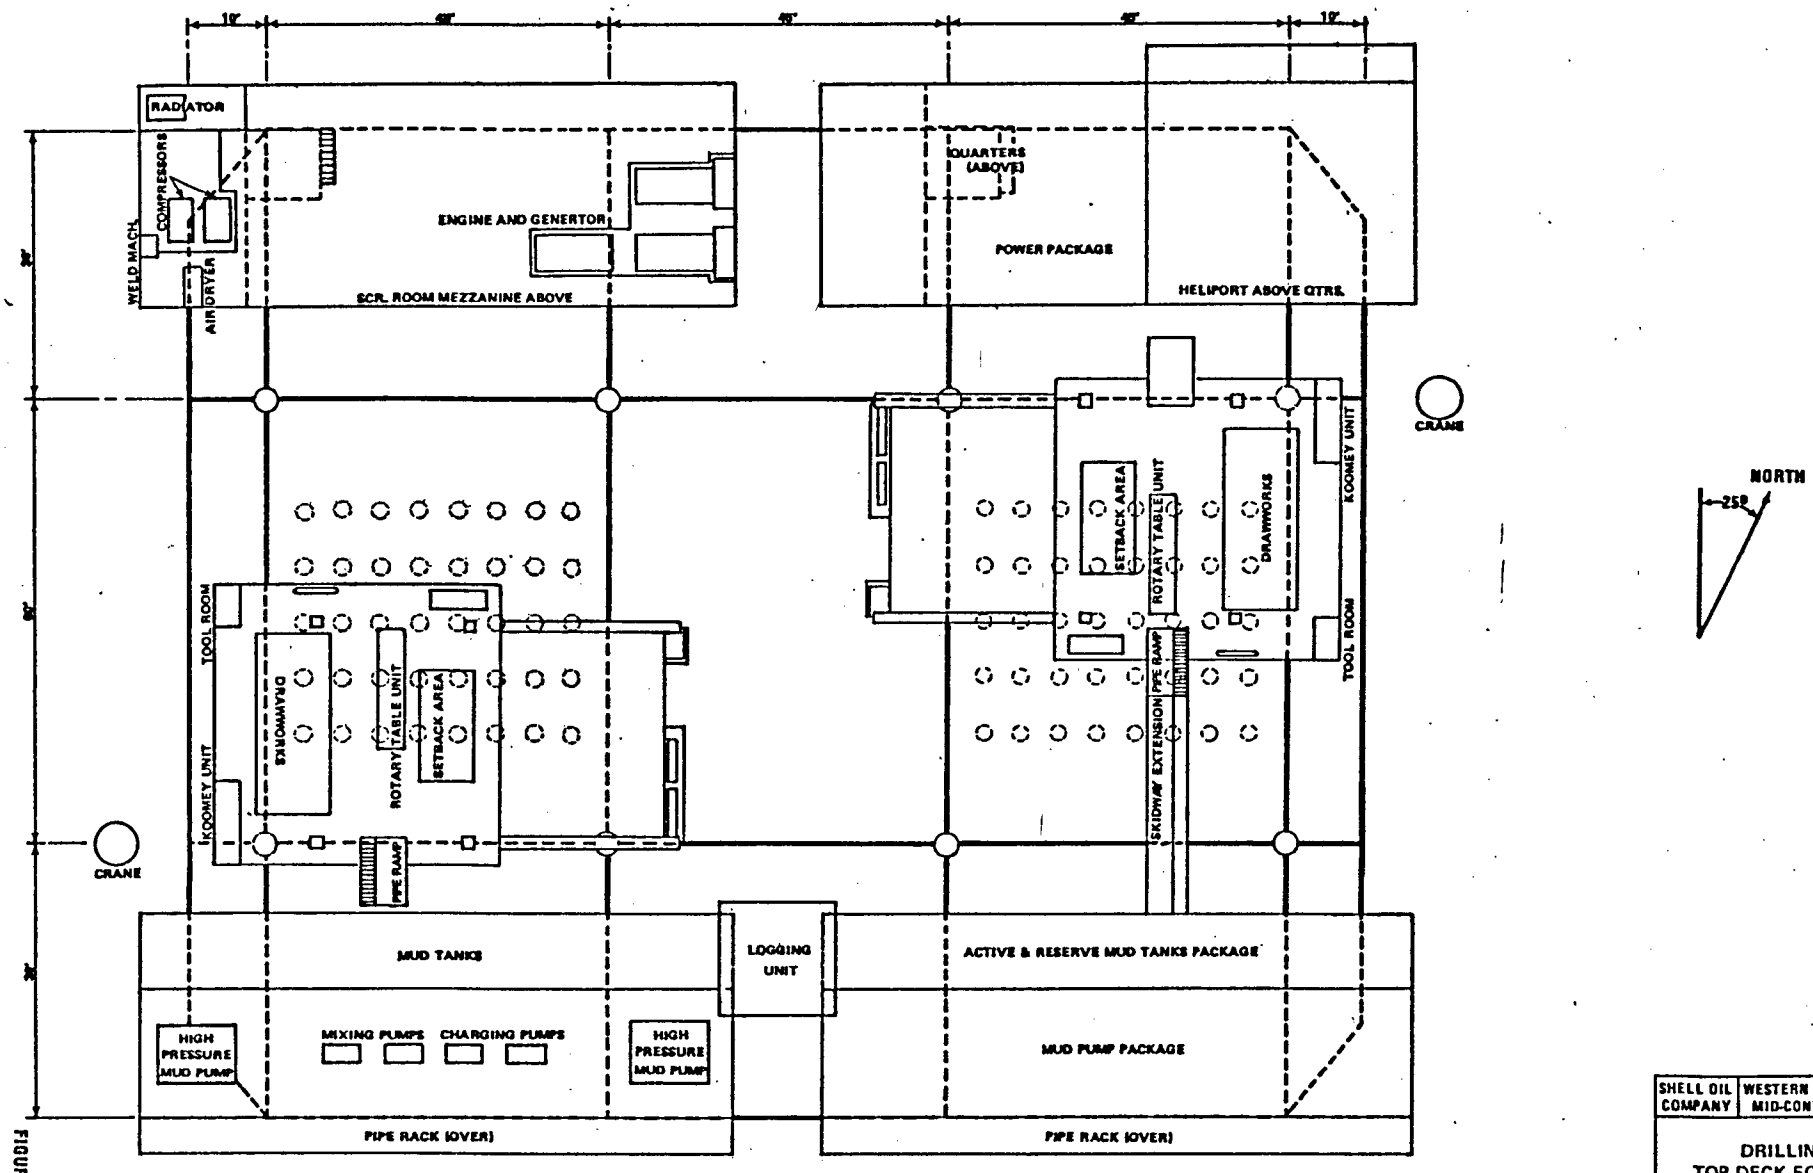

FIGURE 5-1

SHELL OIL COMPANY	WESTERN E & P REGION MID-CONTINENT DIV.	PRODUCTION DEPARTMENT

DRILLING PLATFORM
TOP DECK EQUIPMENT LAYOUT
BETA UNIT, SAN PEDRO BAY

By: J. SYDOW	Date: 8/31/77	File: UF-318
For:		Encl.:

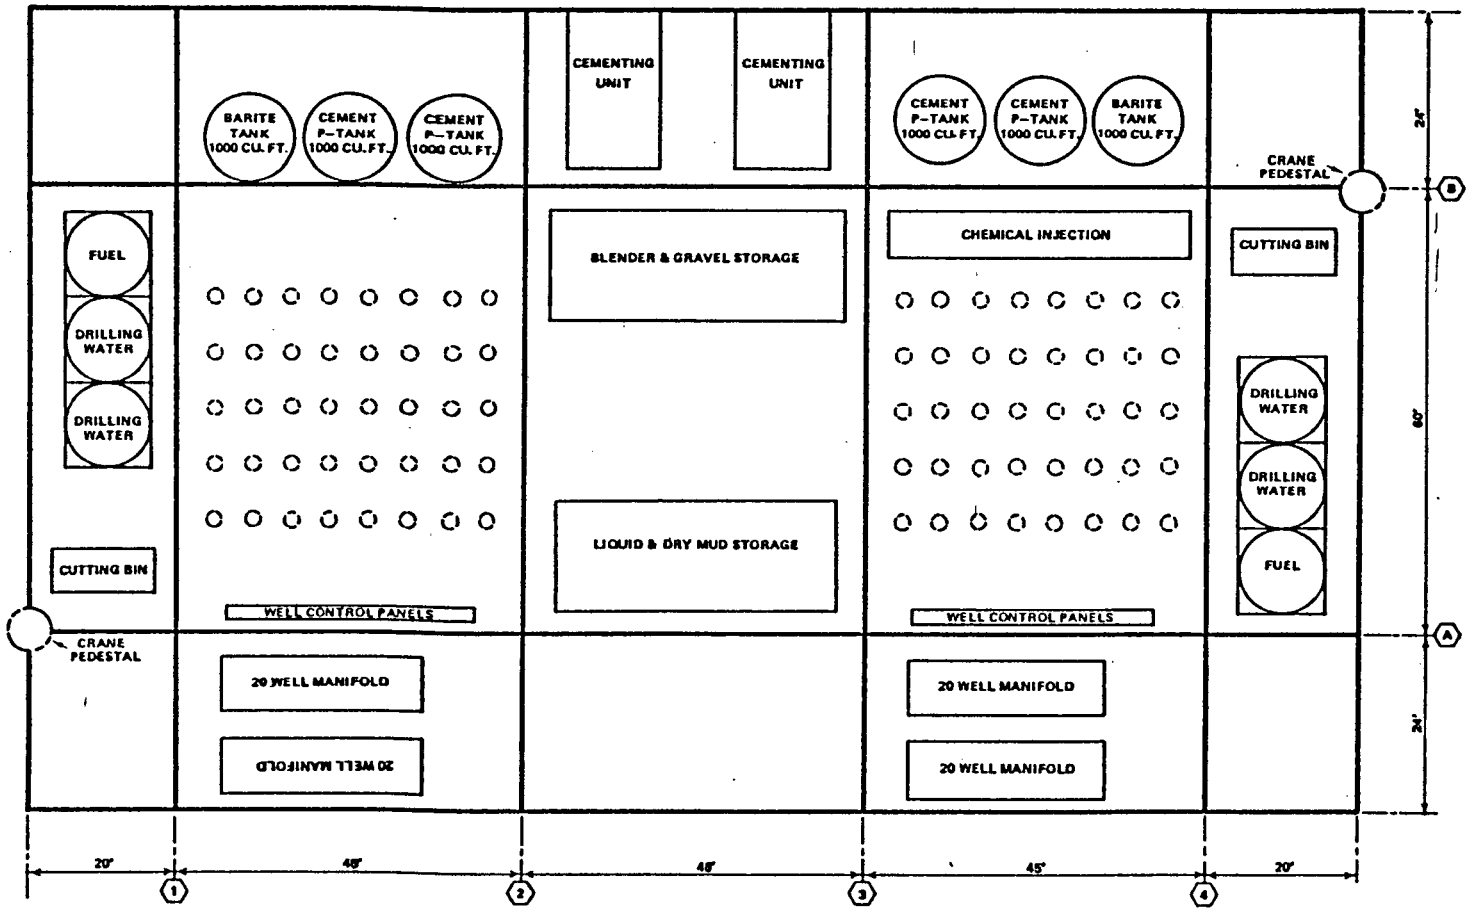



SHELL OIL COMPANY	WESTERN E & P REGION WESTERN DIVISION	PRODUCTION DEPARTMENT

DRILLING PLATFORM
LOWER DECK EQUIPMENT LAYOUT
BETA UNIT, SAN PEDRO BAY

By: J. SYDOW	Date: 8/31/77	File: UP-317
For:		Encl.:

FIGURE 6-2

DRILLING PROGNOSIS
BETA PLATFORM

PROPOSED CASING PROGRAM
#1. PRESENT USGS REQUIREMENTS
#2 PROPOSED FIELD RULES

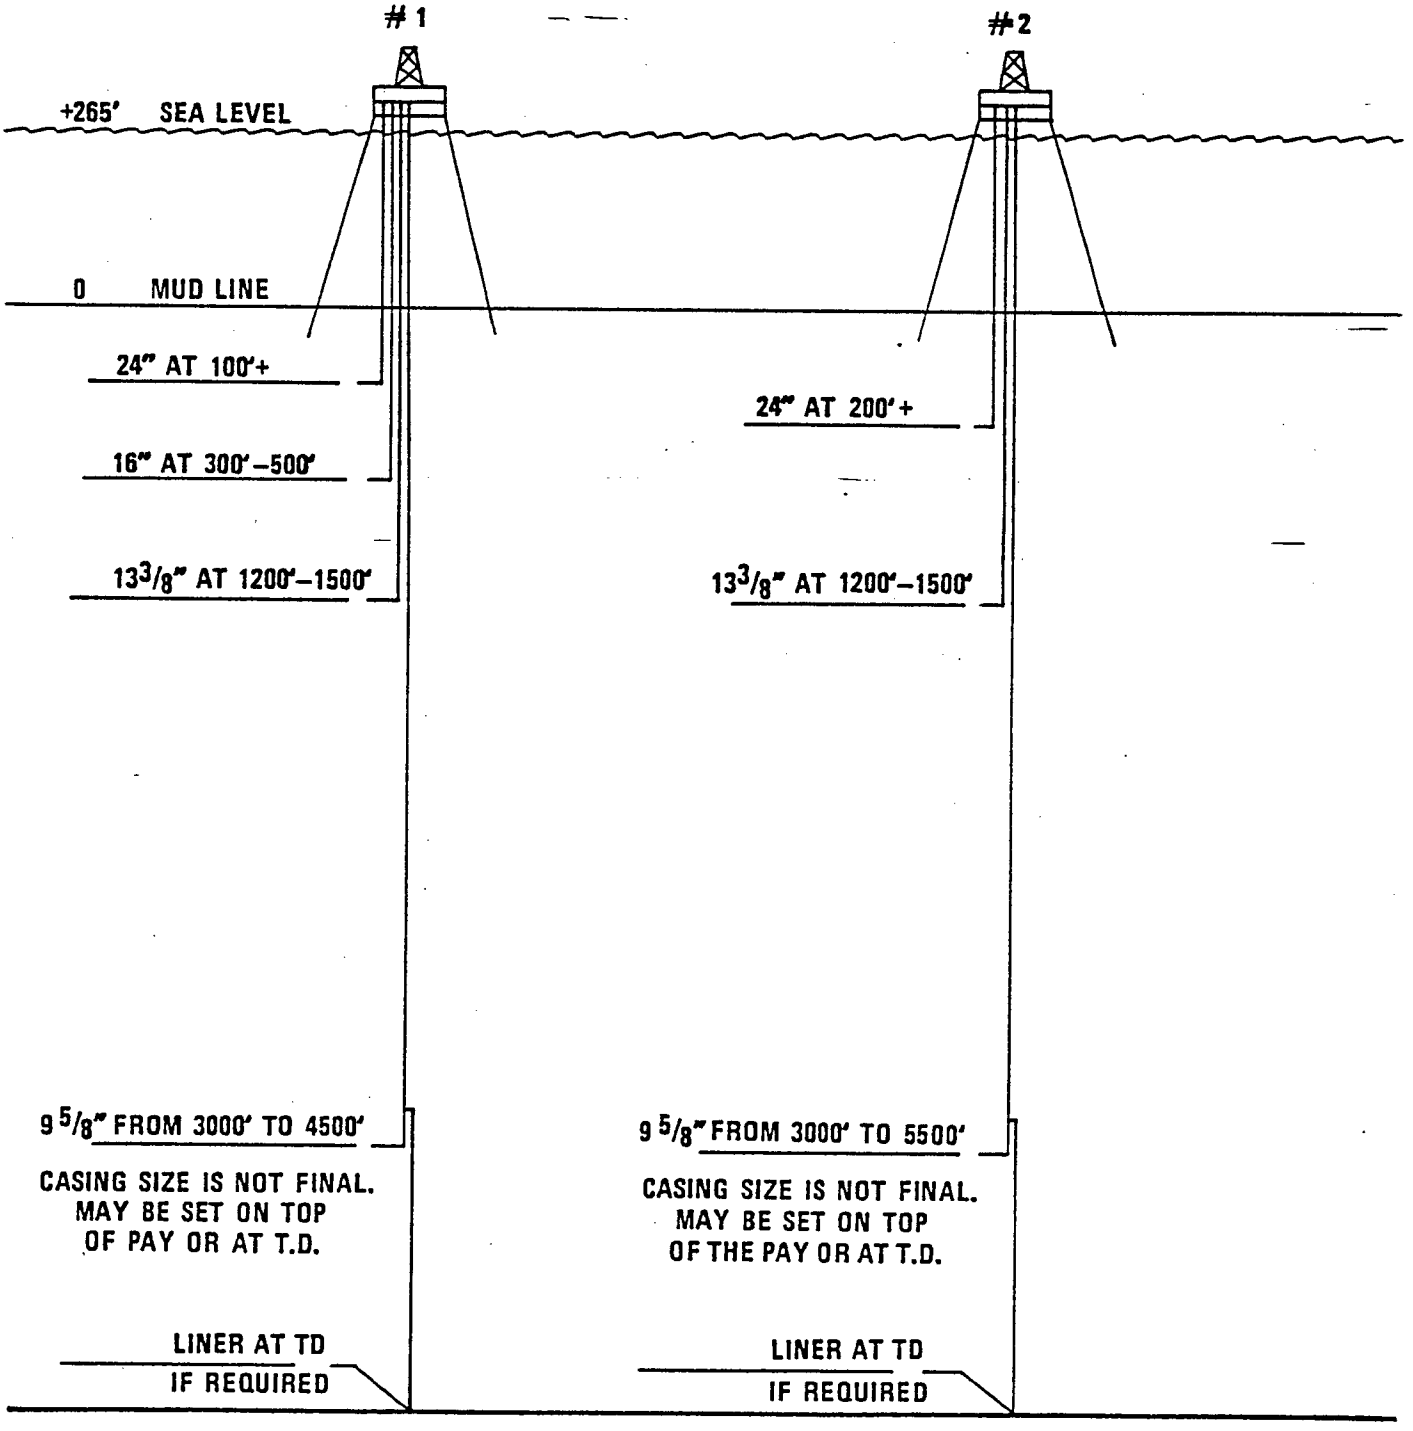

ZF 2564 D

FIGURE 5–3

SCHEMATIC OF CASED–HOLE TYPE COMPLETION

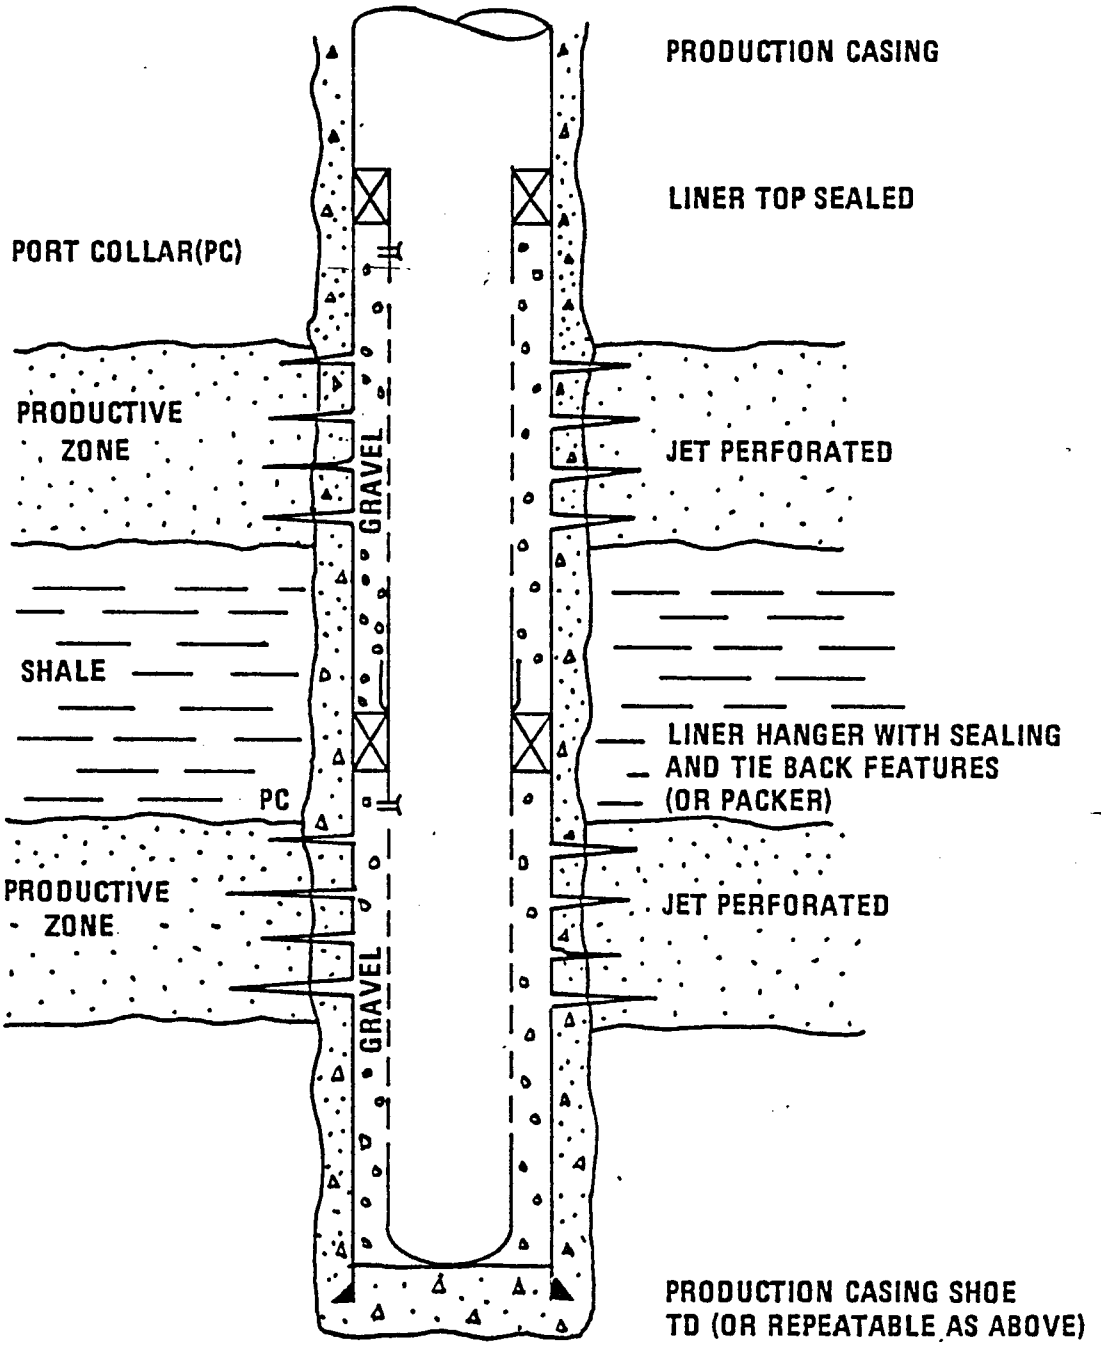

SIMPLIFIED PROCEDURE

1. DRILL THROUGH PRODUCTIVE INTERVAL – RUN LOGS
2. RUN AND CEMENT CASING
3. JET PERFORATE COMPLETION ZONES – WASH PERFORATIONS
4. RUN LOWER LINER AND GRAVEL PACK
5. RUN OPEN LINER(S) AND GRAVEL PACK
   (ALTERNATIVE TO STEPS 4 & 5 – RUN ENTIRE LINER, SET PACKERS – GRAVEL PACK THROUGH PORT COLLARS FROM BOTTOM UP)
6. WASH AND REPACK AS REQUIRED

FIGURE 5–4

ZF 2748A

SCHEMATIC OF OPEN–HOLE TYPE COMPLETION

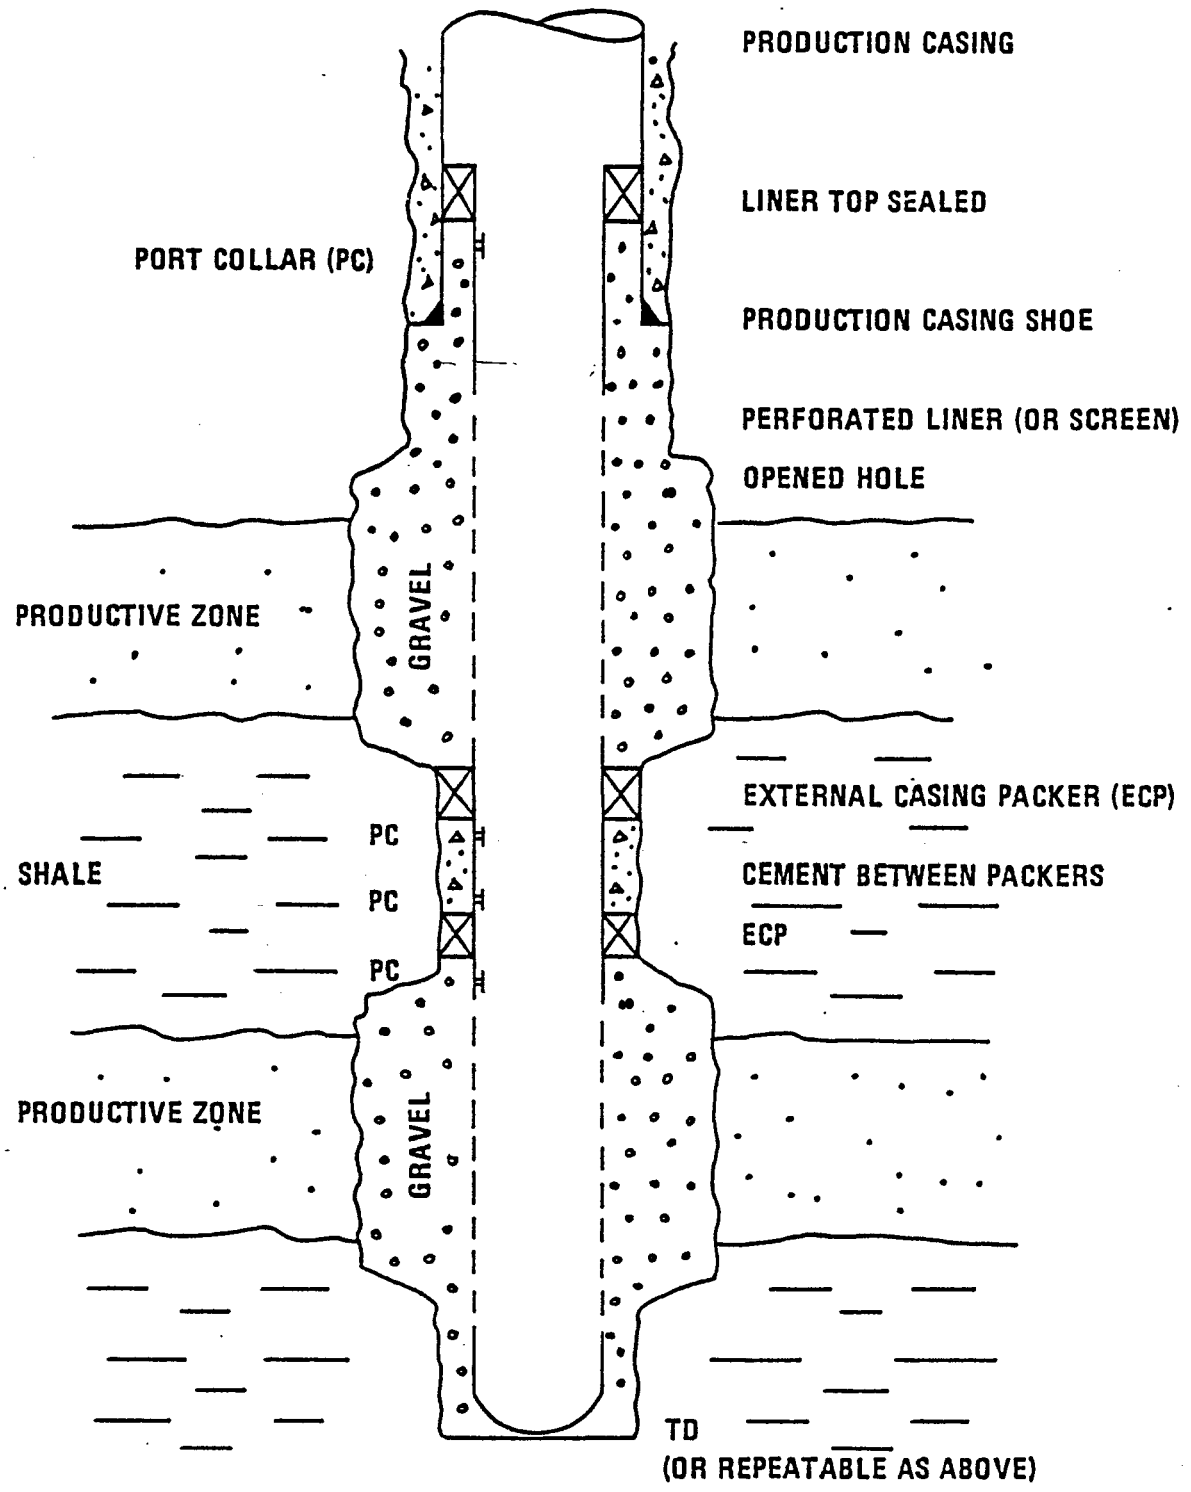

SIMPLIFIED PROCEDURE

1. SET PRODUCTION CASING
2. DRILL THROUGH PRODUCTIVE INTERVAL–LOG
3. OPEN HOLE THROUGH PRODUCTIVE ZONES–RUN LINER, SET OPEN HOLE PACKERS
4. GRAVEL PACK PRODUCTIVE ZONES (FROM BOTTOM UP) THROUGH PORT COLLARS
5. CEMENT BETWEEN ZONES (FROM BOTTOM UP) THROUGH PORT COLLARS
6. WASH AND REPACK AS REQUIRED

ZF 2748B

FIGURE 5–5

SCHEMATIC OF COMBINATION TYPE COMPLETION

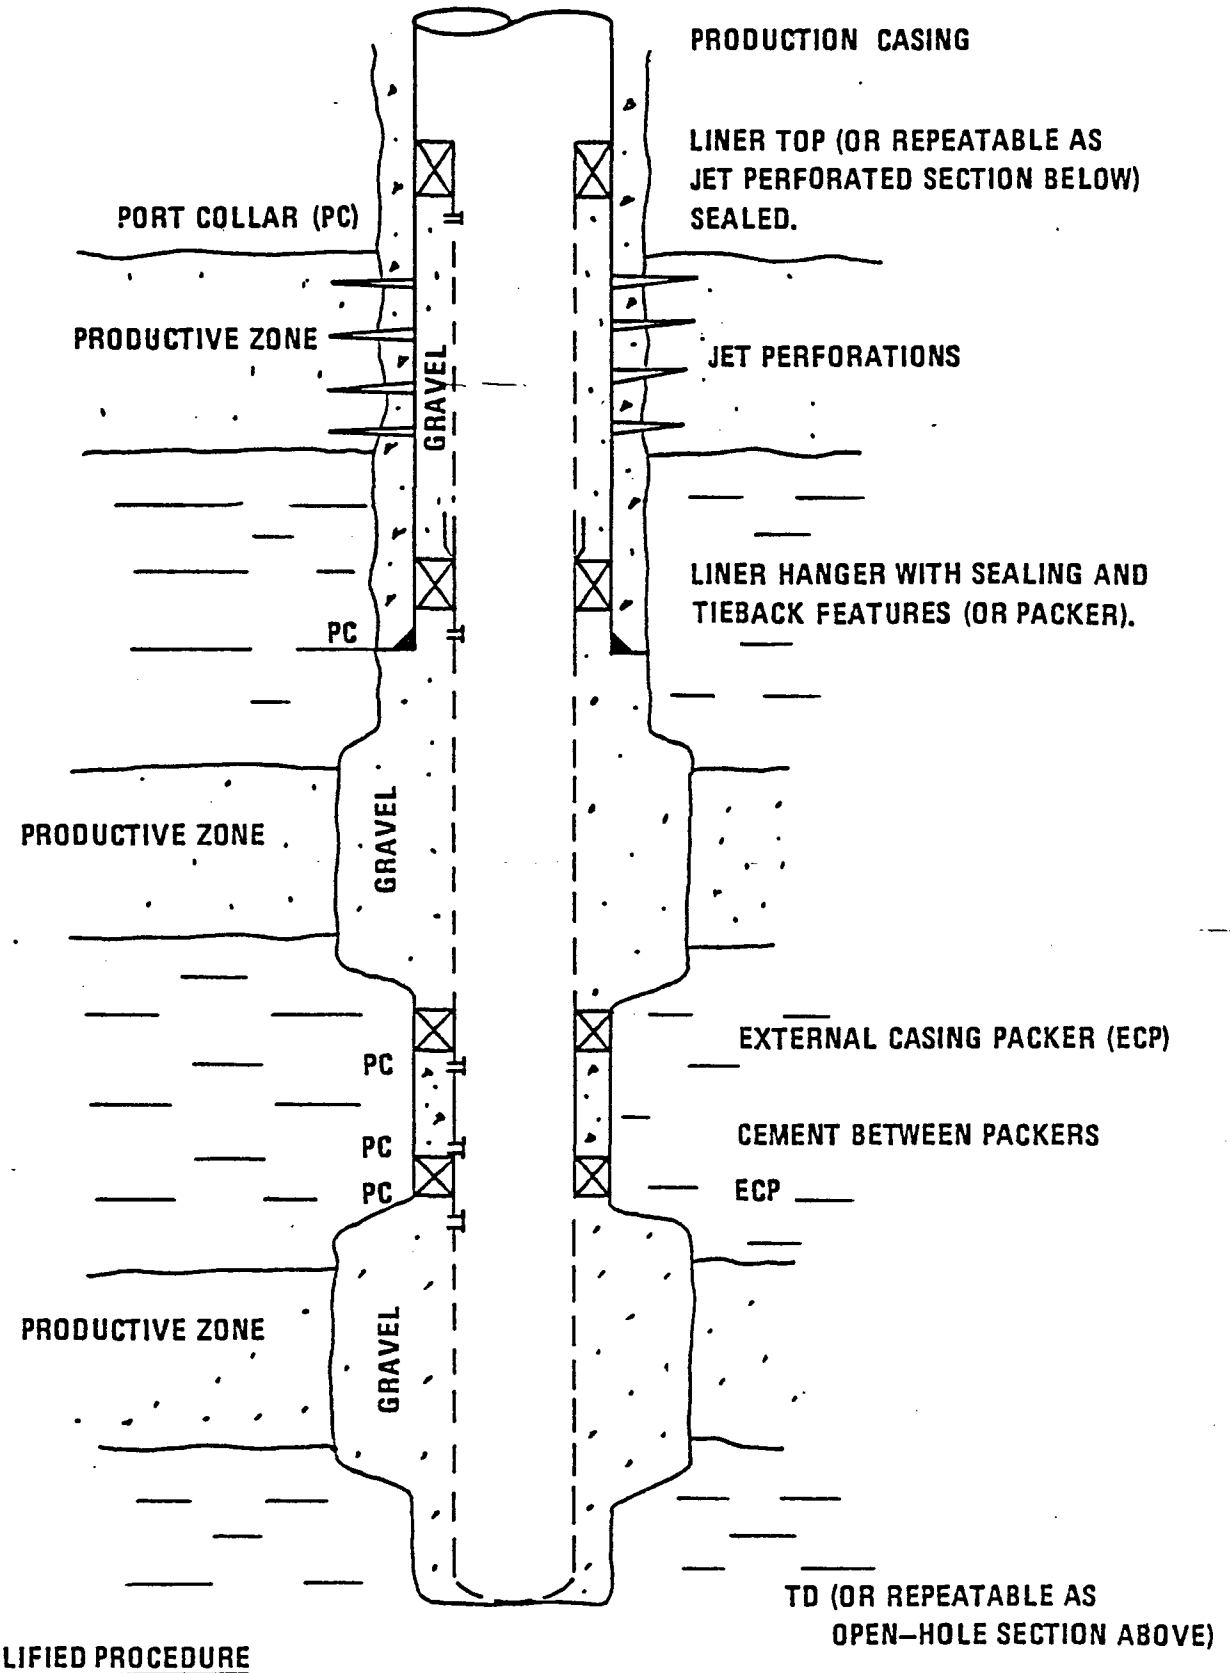

SIMPLIFIED PROCEDURE

1. FOR OPEN–HOLE SECTION, SAME AS OPEN HOLE TYPE COMPLETION
2. FOR CASED–HOLE SECTION, SAME AS CASED HOLE TYPE COMPLETION

FIGURE 5– 6

ZF 2748C

SECTION VI

PLATFORM FACILITIES

TABLE OF CONTENTS

		Page
6.1	Introduction	6-1
6.2	Production Process Facilities	6-1
6.2.1	Design Criteria	
6.2.2	Wellheads, Flowlines, and Manifolds	
6.2.3	Artificial Lift	
6.2.4	Oil Processing and Shipping	
6.2.5	Produced Water Cleanup and Injection	
6.2.6	Produced Sand/Solids Handling	
6.2.7	Gas Processing and Compression	
6.2.8	Condensate Handling	
6.2.9	Well Test/Well Cleanup Facilities	
6.2.10	Source Water Treatment and Injection	
6.2.11	Relief and Vent Systems	
6.3	Utility Systems	6-5
6.3.1	Electric Power Generation	
6.3.2	Emergency Power Generator	
6.3.3	Fuel Gas System/Auxiliary Fuel	
6.3.4	Process Heating System	
6.3.5	Potable Water/Sewage Treatment	
6.3.6	Instrument Air System	
6.3.7	Power Water System for Artificial Lift	
6.3.8	Deck Drainage/Sump System	
6.4	Support Facilities	6-7
6.4.1	Personnel Quarters	
6.4.2	Fire Suppression System	
6.4.3	Navigation Aids	
6.4.4	Emergency Shutdown System (ESD) and Automatic Shut-in of Wells	
6.4.5	Safety and Escape Equipment	
6.5	Measures to Minimize Environmental Impact	6-8
6.5.1	Gas Turbine Emissions	
6.5.2	Hydrocarbon Emissions	
6.5.3	Discharges to the Ocean	

6.6 Attachments

Drawing No. Z9-499d	265 Ft. Water Depth Platform Complex - Prospect Beta
Drawing No. Z9-499c	Simplified Process Flow-Platform Production Facilities, Prospect Beta
Drawing No. Z9-499a	Simplified Process Flow-Remote Platform Production Facilities - Prospect Beta
Drawing No. C6-1714	Equipment Layout - Lower Deck, 12-Leg Facilities Platform - Prospect Beta
Drawing No. C6-1715	Equipment Layout - Upper Deck, 12-Leg Facilities Platform - Prospect Beta
Drawing No. C6-1716	Process Flow Sheet - Sheet 1, Beta Prospect
Drawing No. C6-1717	Process Flow Sheet - Sheet 2, Beta Prospect
Drawing No. Z9-501	Production/Injection Forecast - Beta Prospect
Drawing No. ZF-2627	Wellhead Arrangement
Drawing No. Z9-499b	Single Train Oil Dehydration - Prospect Beta
Drawing No. Z9-499	Simplified Process - Produced Water Treatment - Prospect Beta
Drawing No. Z9-500	Forecast of NO_x Emission Addition/Reduction Program

SECTION VI

PLATFORM FACILITIES

6.1 Introduction

This section describes the various facilities and equipment to be installed. The majority of this equipment will be installed on a separate production facility platform located adjacent to the 265 foot water depth drilling platform. Drawing Z9-499d is a plot plan of the two platform complex. These facilities will serve not only this drilling platform, but also any future remote drilling platform(s).

The facilities will consist of production process facilities for treating oil, produced water, source water, and produced gas, utility systems, and support facilities. These are intended to make the field operation as self-sufficient as possible. Drawing Z9-499a is a simplified flow diagram of the facilities.

By having a centrally located facilities platform, other future remote platforms would require only a minimum of facilities. Drawing Z9-499a is a simplified flow diagram of the facilities required for the remote platform(s).

Reservoir pressure maintenance will be accomplished by injecting the produced water and by injecting a source water. Perhaps a suitable subsurface aquifer will be found to supply the source water. However, since the presence of this aquifer is unconfirmed, the facility design will assume a "worst case", i.e., use of sea water for the source water. Because of the considerable uncertainty as to the volume of produced water which will need to be processed, considerable flexibility is incorporated in the design to accommodate up to about 100,000 B/D of produced water initially.

6.2 Production Process Facilities

Drawings No. C6-1716 and C6-1717 depict the process flow for the production facilities platform and for the adjacent drilling platform. Drawings C6-1714 and C6-1715 depict the equipment layout on the facility platform lower deck and upper deck, respectively.

6.2.1 Design Criteria

The design criteria are based 1) upon observations from the eight exploratory wells drilled on the two tracts and 2) pressure maintenance by waterflooding.

a) Maximum bottomhole pressure = 1600 psig
b) Bottomhole temperature = 140° - 160°F
c) Oil Gravity = 12° API to 20° API
d) Gas/Oil Ratio (GOR) = 200 Scf/bbl
e) Maximum Water Injection Pressure at surface = 2000 psig
f) Maximum shut-in wellhead tubing pressure = 2000 psig (with pump)
g) Production/Injection Forecast - See Drawing Z9-501

6.2.2 Wellheads, Flowlines, and Manifolds

A typical wellhead configuration for a submersible pumped well is shown in Drawing ZF-2627. The 80 well slots are divided into two groups of 40. Each group of forty slots consists of five rows of eight slots each. Initially, 60 well conductors will be installed with the remaining 20 well slots reserved for future use.

All wells will be equipped initially with downhole hydraulically controlled safety valves in accordance with OCS Order No. 5.

Flowlines for the 60 wells will connect to a manifold system. Flow from the wells will normally be routed to a bulk production header. Well test will be accomplished by selectively routing individual wells into either of two well test/cleanup headers.

Although all wells will be produced initially, within a year some wells will be converted to water injectors. Provisions are included in the manifold arrangement for readily converting any given well from producer to injector.

6.2.3 Artificial Lift

It is anticipated that artificial lift will be required for all wells initially or soon after completion. Initial provisions for submersible electric pumping will be provided. Plans include provision for hydraulic pumping in the future if required. The hydraulic power water system surface facilities are described in Section 6.3.7.

6.2.4 Oil Processing and Shipping

Three separate trains of oil dehydration equipment are provided. Drawing Z9-499b is a simplified flow diagram of one of these trains. Two of the trains will be installed initially; the third will be added when need is recognized.

The produced crude oil and water are directed through one of the three parallel trains. The stream is first heated to about 140°F in two heat exchangers. Three phase separation occurs in the free water knockout vessel. The vessel operates at 50 psig. Gas is separated and sent into the gas compression system. An oil/water emulsion phase is separated and sent to the treater for the final step of oil dehydration. Free water is separated and sent to the produced water treating system.

Before entering the treater, the emulsion is heated in two heat exchangers to approximately 220°F. In the treater, the remaining water is removed and the clean oil flows to the clean oil storage tank.

From this tank, the oil is metered for sales through the LACT and pumped into the pipeline.

6.2.5 Produced Water Cleanup and Injection

Prior to injection of the produced water, it must be treated to remove suspended solids and oil. The treatment process is shown in simplified form in Drawing Z9-499. Treatment consists of a skim tank for removal of oil by gravity separation. Water is then passed through an induced gas flotation cell. The third stage of treatment is filtration through downflow mixed media (anthracite plus sand) filters.

The filtered water is accumulated in a surge tank. From the tank, the water is pumped through cartridge-type polishing filters. Gas turbine driven injection pumps then boost the water to the required injection pressure.

Under normal operations, all produced water will be injected. However, there will be times when it will be necessary to discharge produced water overboard. The water so discharged will be sufficiently cleaned to meet the EPA requirements for discharge into the ocean.

6.2.6 Produced Sand/Solids Handling

It is anticipated that some sand and clay will be produced in conjunction with the oil and water. Facilities are provided to collect these materials and to dewater them. The EPA requirements allow overboard discharge of these solids provided no free oil is present. Since it is not known at this time whether that criteria can be met, provisions are included for collection of the solids and for barging them to shore for disposal.

6.2.7 Gas Processing and Compression

Gas is collected from various points in the production handling system. A prime source of gas is from the casing-tubing annulus. In order to minimize the back-pressure on the producing formation, it is necessary that these gases be removed. A casing gas gathering system is provided for this purpose.

Additional gas breakout occurs in the free water knockout, in the treater, and in the stock tank. Provisions are included for collecting all of these gases and compressing them for use as fuel gas for the various gas turbines on the platform. All well tests have indicated that the gas contains no measurable quantity of hydrogen sulfide (H_2S).

Virtually all of the natural gas produced will be consumed onboard the platform as fuel. However, at peak production rates, gas production may slightly exceed fuel gas requirements. To provide for this contingency, a compressor is provided to boost the pressure to about 2000 psig for injection into the reservoir.

No gas pipeline to shore is provided since it is not anticipated that excess gas for sales would be available in quantities sufficient to justify its installation.

6.2.8 Condensate Handling

Condensate from the natural gas collection and compression system is blended back into the crude oil system.

6.2.9 Well Test/Well Cleanup Facilities

Well tests will be performed by selectively routing the well to be tested to one of two well test vessels. Gas, water and oil metering from these vessels will allow accurate well tests to be performed.

The vessels serve a second function. That function is as a "well cleanup scrubber" for newly completed wells. This would allow segregation of the production from that well until drilling muds, etc. are purged from the well.

6.2.10 Source Water Treatment and Injection

Equipment is provided to treat seawater as a supplemental source of injection water. Treatment consists of filtration to remove suspended solids and deaeration to

remove oxygen. Gas turbine driven pumps boost the pressure for injection.

6.2.11 Relief and Vent Systems

Overpressure protection for the various pressure vessels is provided by appropriately sized pressure relief valves. These valves discharge into a collection system which routes the vapor through a "Vent Scrubber" to prevent liquid carryover prior to venting. Two separate collection systems and scrubbers are provided. One provides protection for the low pressure vessels (less than 5 psig) and the second provides protection for the high pressure vessels.

6.3 Utility Systems

In order for platform operations to be as self-sufficient as possible, the following utility systems are provided:

6.3.1 Electric Power Generation

Space is provided for up to six (6) 2400 KW generators. The generators will be driven by gas turbines capable of utilizing either natural gas or diesel as fuel. These generators will provide power for artificial lift, for various process and production needs as well as providing power for one of the two drilling rigs on the adjacent drilling platform.

If additional remote drilling platforms are installed, it is intended that these generators would supply power via submarine electric cable for electrical loads on those platforms.

6.3.2 Emergency Power Generation

A separate diesel driven generator of approximately 500 KW capacity will provide backup power to certain critical loads such as lighting, navigation aids, instrument air compressors, quarters, etc.

6.3.3 Fuel Gas System/Auxiliary Fuel

All of the prime movers on the platform will utilize produced natural gas as the primary fuel. However, all will be equipped to utilize diesel as an auxiliary fuel at times when the gas production is insufficient to meet all of the fuel needs.

On board storage for about 1000 bbls. of diesel is provided. Connections at the boat landing level will allow taking aboard diesel fuel from work boats, barges, etc.

6.3.4 Process Heating System

Process heat requirments are fulfilled by means of a closed circulating—system utilizing low pressure (15 psig) steam as the heat media. The source of the heat will be waste heat recovery units on the gas turbines.

6.3.5 Potable Water/Sewage Treatment

Provision is made for supplying water from shore by means of a supply boat.

Sanitary sewage will be treated through a packaged sewage treatment unit. The effluent from the unit will comply with the EPA requirements.

6.3.6 Instrument Air System

Air for operation of pneumatic instruments will be supplied by a system consisting of compressors and air dryers.

6.3.7 Power Water System for Artificial Lift

A closed power water system will be provided for driving downhole hydraulic pumps. The system will be designed for 3000 B/D at 3000 psig. Make up water for the system will be treated produced water.

6.3.8 Deck Drainage/Sump System

In order to prevent spills of oil or other pollutant materials from reaching the ocean, both the drilling platform and the production platform will be equipped with drainage collection systems in all areas where spills are likely to occur. These "drip pans" collect the spilled material and route it to a water sump. Oil is collected in an oil sump and pumped back into the oil handling system. Water is collected in a drain water surge tank and pumped back into the produced water cleanup system. Under normal operations (i.e., routine cleanup and washdown of small spills) no discharge of either oil or water into the ocean will occur.

Should the capacity of the pumping system be exceeded (e.g., during a heavy rainstorm or when firewater is being

used), the excess water which can not be pumped back into the produced water system will discharge into an emergency sump or skim pile. In the unlikely event that any oil carries over into the skim pile, provisions are included to recover the oil.

6.4 Support Facilities

6.4.1 Personnel Quarters

Personnel Quarters will be sized to accommodate those people who would routinely be quartered on the platform. Sleeping accommodations, kitchen and lunchroom; locker room, and restroom-washroom facilities will be provided.

6.4.2 Fire Suppression System

The design of the fire supression system will include the following:

a) a fixed automatic water spray system in the wellhead areas as required by OCS Order No. 8
b) a looped fire water system with two (2) fire water pumps on the facilities platform and two (2) fire water pumps on the drilling platform. These pumps will be located remotely from one another so that the likelihood of damage to more than one is remote
c) dry chemical extinguishers
d) foam generation equipment

6.4.3 Navigation Aids

A navigational aid system which complies with the U. S. Coast Guard's regulation will be provided.

6.4.4 Emergency Shutdown System (ESD) and Automatic Shut-in of Wells

All wells, including those artifically lifted, will be initially equipped with surface controlled subsurface safety devices. These devices will be installed in the well below the mudline and held open by the application (from the surface of the platform) of hydraulic and pneumatic pressure. Any accidental or deliberate bleeding off of the pressure will cause these devices to close and thereby stop any flow from the well, from either the tubing or the casing annulus, from below the device.

The pneumatic system holding open these and other safety shut-in devices on the platform equipment is spread throughout the platform. Monitors of critical functions

and manual bleed-off valves at ESD stations will cause the system pressure to bleed off if an abnormal condition is detected. Accidental breaking of the system piping will also cause the system to bleed off and shut-in the wells.

6.4.5 Safety and Escape Equipment

Escape systems and life jackets will be provided on each of the platforms. The quarters building will be located near the bridge to provide a ready means of egress from the drilling platform.

6.5 Measures to Minimize Environmental Impact

Although no specific rules governing emissions apply to platforms offshore, it is planned to take appropriate steps to insure that no significant adverse effects will result from the installation and operation of these production facilities. Discharges to the ocean will comply with regulatory requirements.

6.5.1 Gas Turbine Emissions

The gas turbines which are used as the prime movers for the electric power generators and for the water injection pumps are the primary source of emissions. Although subject to change, the current plan calls for installing a total of eight (8) gas turbines with a total rating of about 20,000 horsepower. All of the turbines will be located on the 255-foot water depth production platform and will be sized to handle anticipated production from both the 265-foot water depth drilling platform and the future deep water platform. All turbines will be dual fuel (i.e., they will be equipped to burn either produced natural gas or diesel as fuel).

In order to minimize the environmental impact of these sources, the following steps will be taken:

a) Special turbines designed for low emissions of NO_x will be purchased.

b) Shell will shut down the Ventura gas plant and plans to shut down a number of natural gas engines in its Ventura Field. These will, in effect, offset the emissions of NO_x from the proposed gas turbine installation. A forecast of both the emission decrease at Ventura and the emission increase as a result of the proposed installation is shown in Drawing Z9-500.

c) Sulfur content of the fuel gas and the diesel fuel will comply with the equivalent regulations which apply onshore (i.e., fuel gas will contain less than 50 grains total sulfur as H_2S per 100 standard cubic feet and diesel fuel will contain a maximum of 0.25% sulfur by weight.)

6.5.2 Hydrocarbon Emissions

The offshore processing facilities will be designed to minimize hydrocarbon emissions. All vessels and tanks will be equipped with vapor recovery.

Although plans for onshore facilities are not definite at this time, they will be minimal. If tankage is required, it will be equipped with vapor recovery so that no emissions onshore will occur.

6.5.3 Discharges to the Ocean

The pollutant concentrations in ocean discharges will be within the limits prescribed by EPA in their Interim Final NPDES Effluent Guidelines with one exception; deck drainage will achieve "discharge of no free oil to the surface waters". This deck drainage requirement was stipulated by EPA and the industry in API versus EPA, Ninth Circuit Court of Appeals, 76-3588. The limitations prescribed are listed below:

Far Offshore Category

Water Source	Oil & Grease (mg/l) Maximum for Any One Day	Oil & Grease (mg/l) Average Daily Values for thirty consecutive days	Residual Chlorine (mg/l)
Produced Water	72	48	NA
Deck Drainage Drill Cuttings Produced Sand	No discharge of free oil to the surface waters		NA
Sanitary Waste	NA	NA	1.0 Minimum
Domestic Waste	NA	NA	NA

NA - Not Applicable.

265 FT. WATER DEPTH PLATFORM COMPLEX PROSPECT BETA

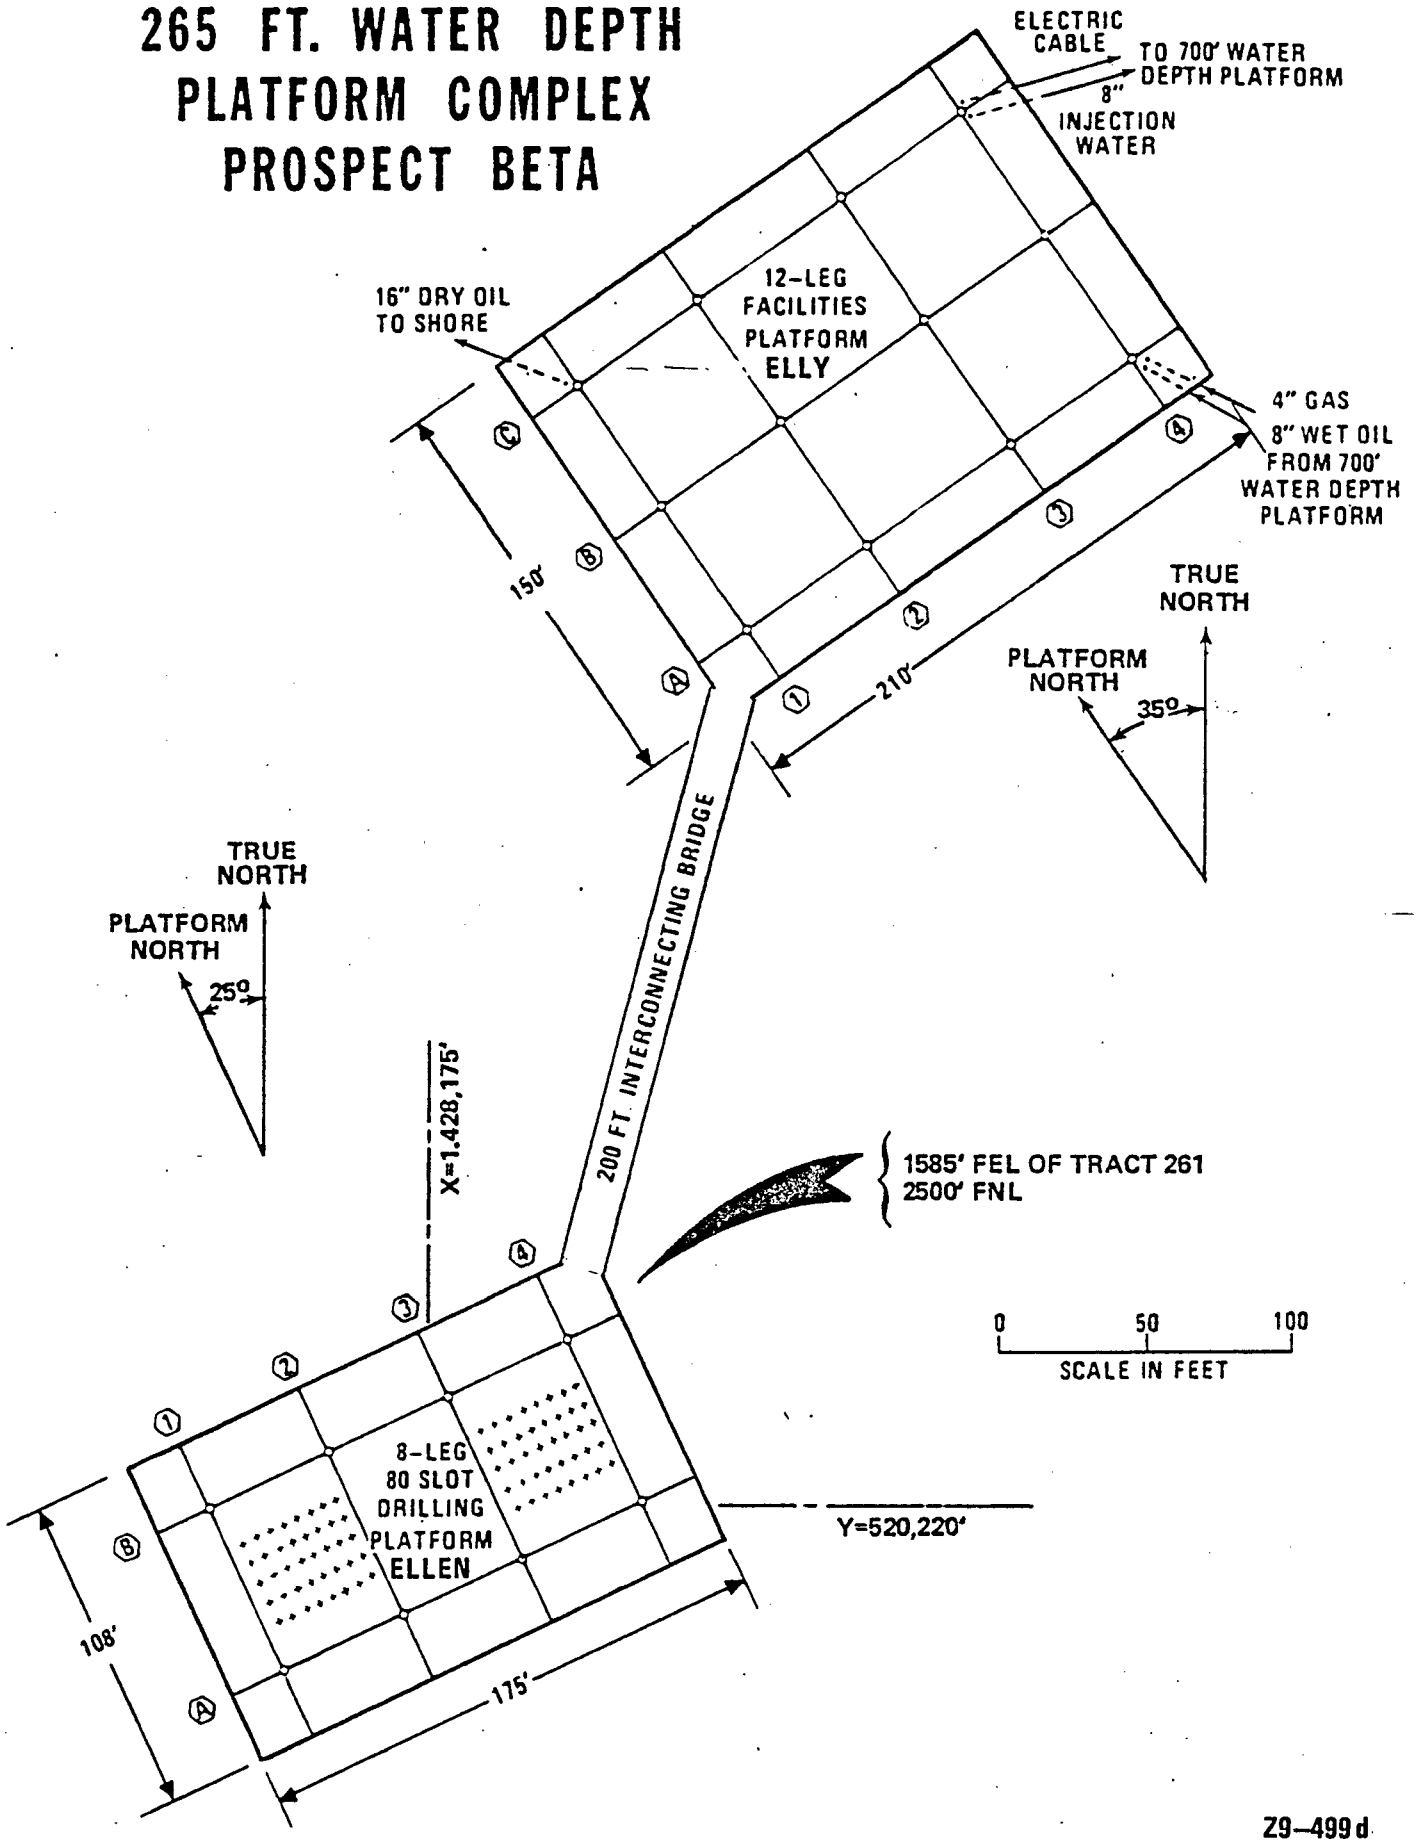

Z9-499d

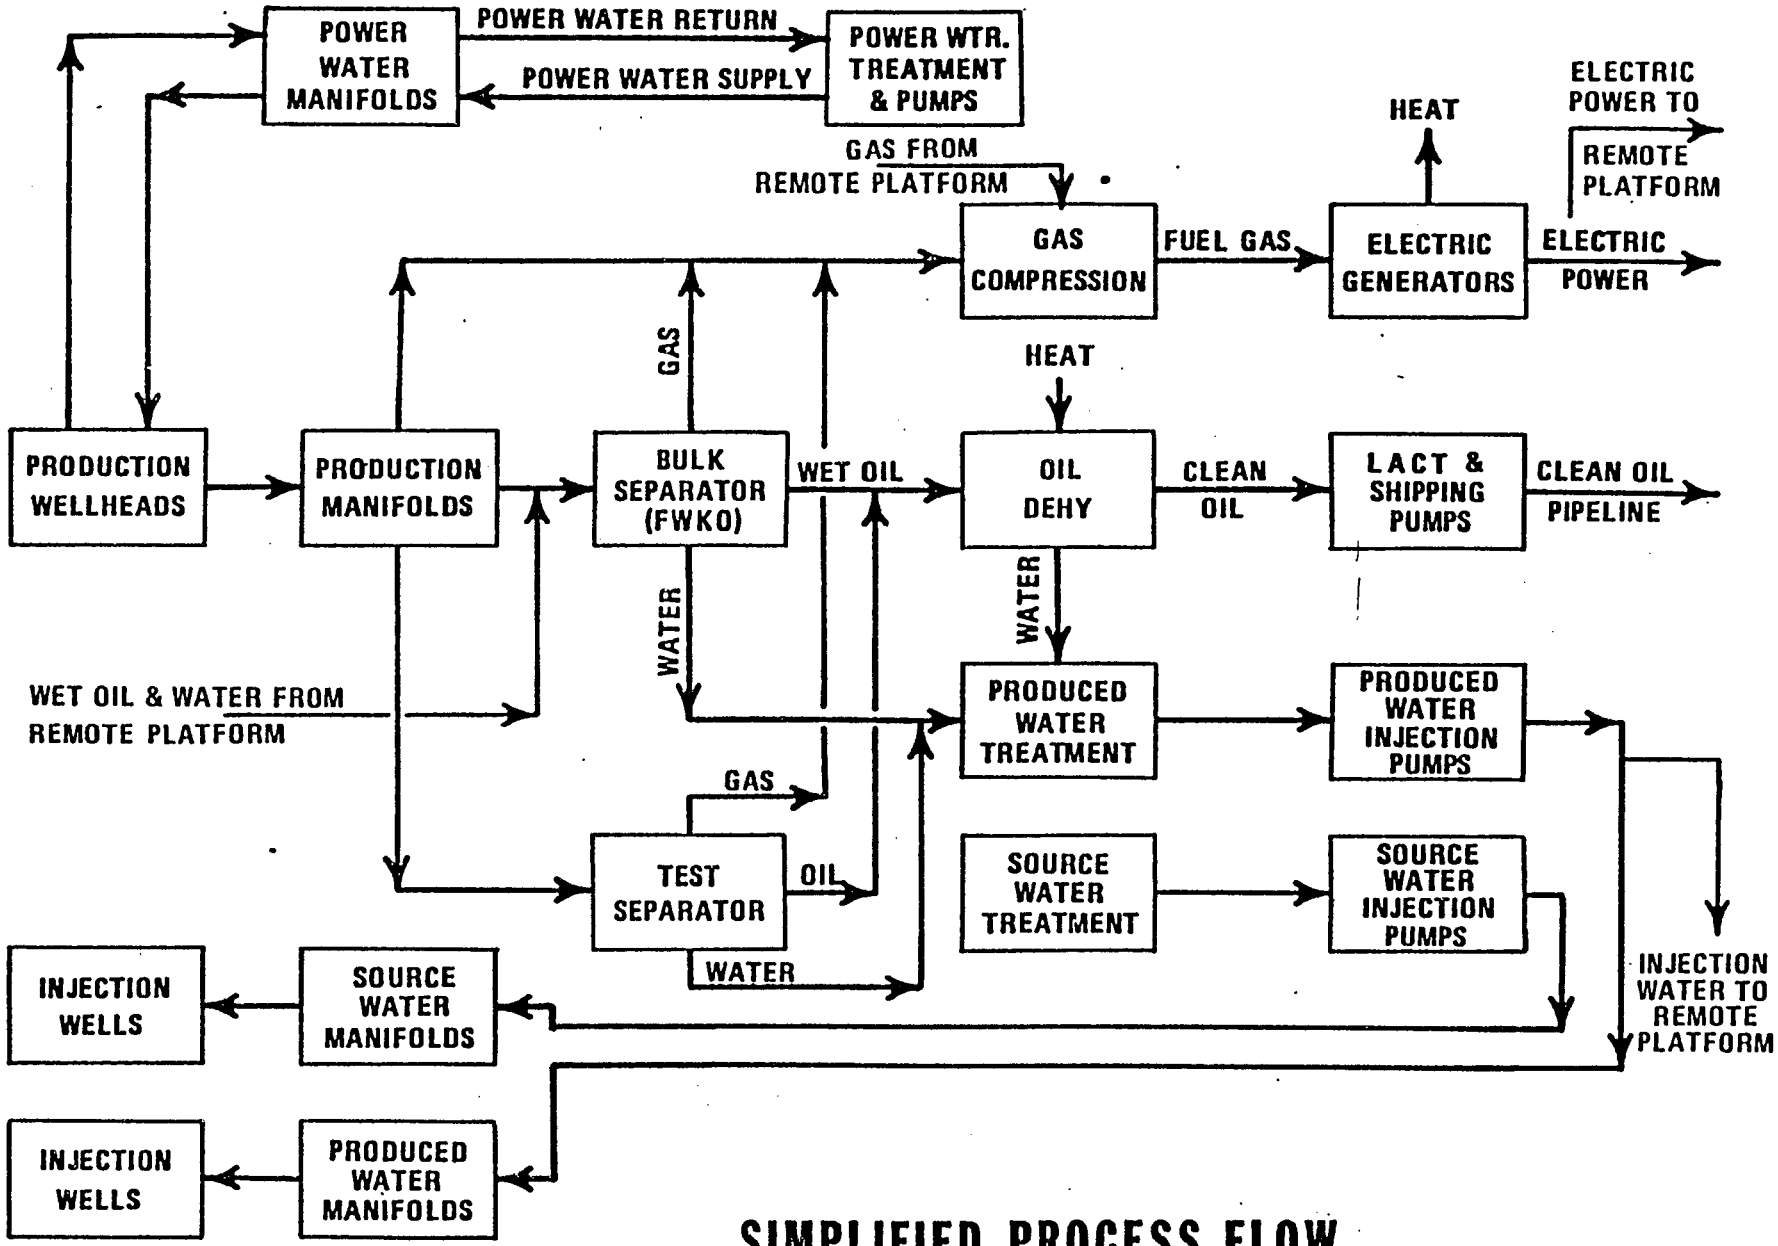

SIMPLIFIED PROCESS FLOW
PLATFORM PRODUCTION FACILITIES
PROSPECT BETA

ETB 8/2/77
Z9-499c

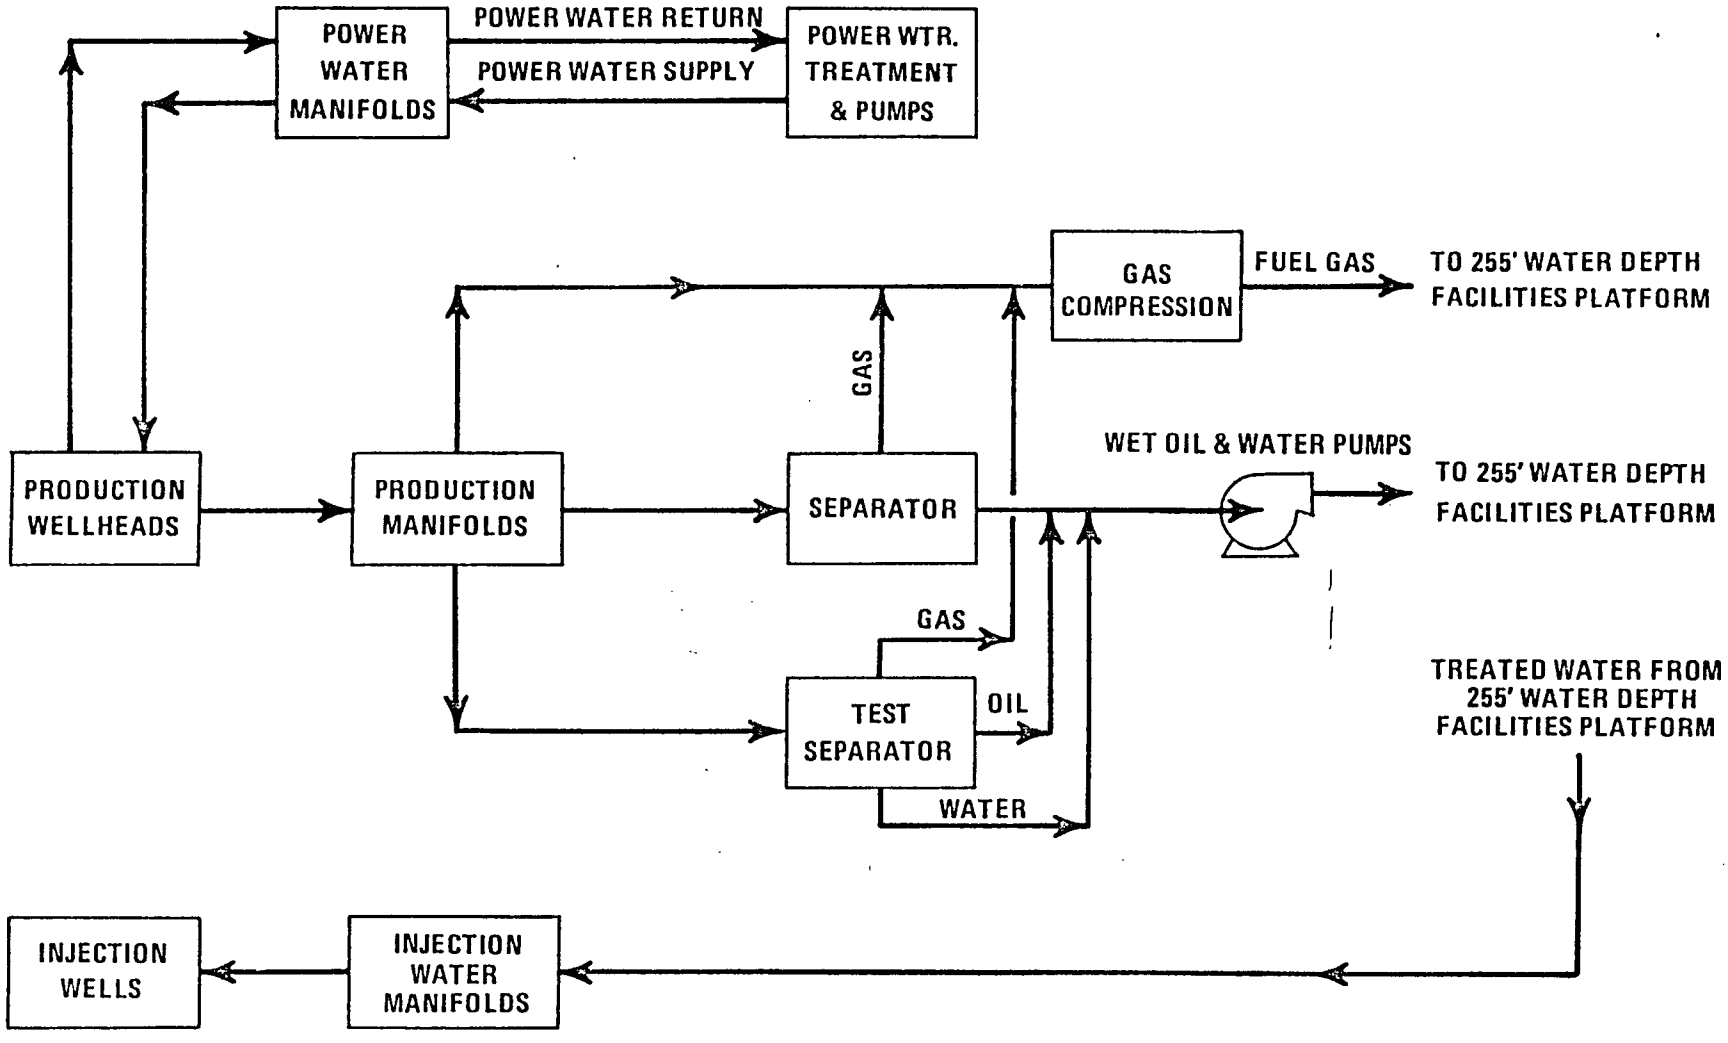

SIMPLIFIED PROCESS FLOW
REMOTE PLATFORM PRODUCTION FACILITIES
PROSPECT BETA

ETB 8/1/77
Z9-499a

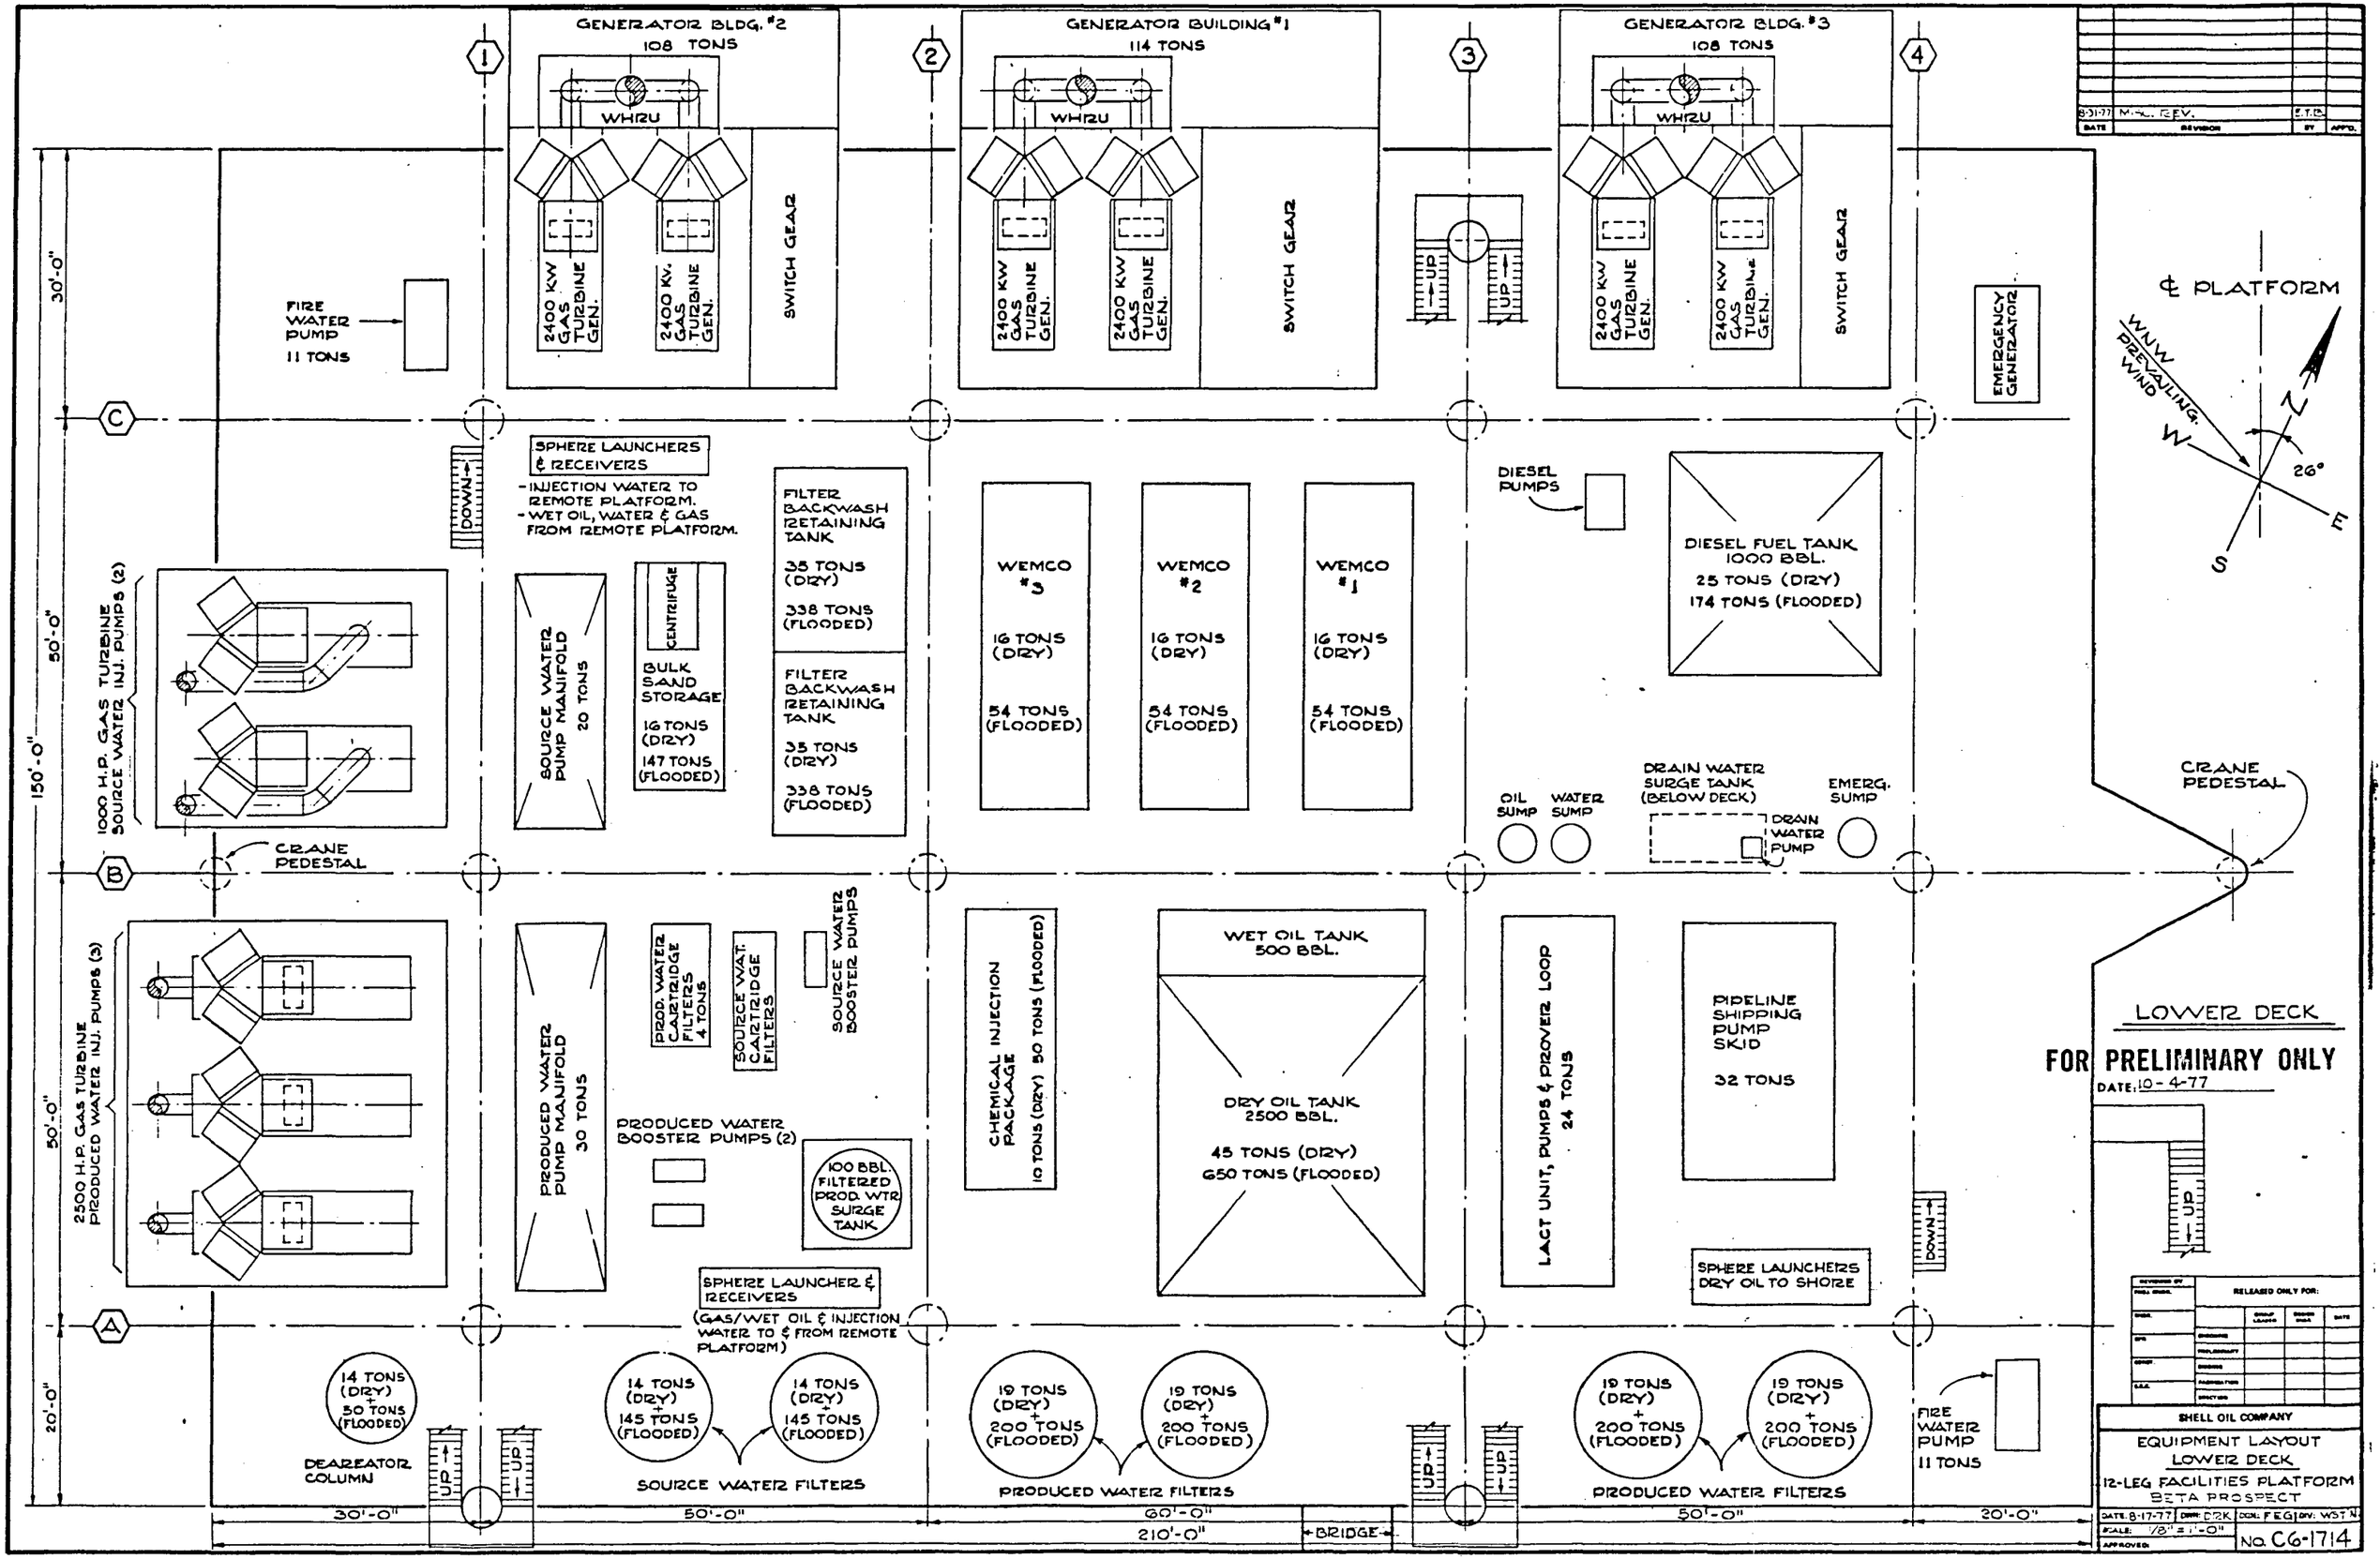
GENERATOR BLDG. #2
108 TONS
WHRU
2400 KW GAS TURBINE GEN.
2400 KW GAS TURBINE GEN.
SWITCH GEAR
GENERATOR BUILDING #1
114 TONS
WHRU
2400 KW GAS TURBINE GEN.
2400 KW GAS TURBINE GEN.
SWITCH GEAR
GENERATOR BLDG. #3
108 TONS
WHRU
2400 KW GAS TURBINE GEN.
2400 KW GAS TURBINE GEN.
SWITCH GEAR
EMERGENCY GENERATOR
FIRE WATER PUMP
11 TONS
UP
DOWN
SPHERE LAUNCHERS & RECEIVERS
- INJECTION WATER TO REMOTE PLATFORM.
- WET OIL, WATER & GAS FROM REMOTE PLATFORM.
FILTER BACKWASH RETAINING TANK
35 TONS (DRY)
338 TONS (FLOODED)
FILTER BACKWASH RETAINING TANK
35 TONS (DRY)
338 TONS (FLOODED)
WEMCO #3
16 TONS (DRY)
54 TONS (FLOODED)
WEMCO #2
16 TONS (DRY)
54 TONS (FLOODED)
WEMCO #1
16 TONS (DRY)
54 TONS (FLOODED)
DIESEL PUMPS
DIESEL FUEL TANK
1000 BBL.
25 TONS (DRY)
174 TONS (FLOODED)
1000 H.P. GAS TURBINE SOURCE WATER INJ. PUMPS (2)
SOURCE WATER PUMP MANIFOLD
20 TONS
CENTRIFUGE
BULK SAND STORAGE
16 TONS (DRY)
147 TONS (FLOODED)
CRANE PEDESTAL
OIL SUMP
WATER SUMP
DRAIN WATER SURGE TANK (BELOW DECK)
DRAIN WATER PUMP
EMERG. SUMP
CRANE PEDESTAL
2500 H.P. GAS TURBINE PRODUCED WATER INJ. PUMPS (3)
PRODUCED WATER PUMP MANIFOLD
30 TONS
PROD. WATER CARTRIDGE FILTERS
4 TONS
SOURCE WAT. CARTRIDGE FILTERS
SOURCE WATER BOOSTER PUMPS
PRODUCED WATER BOOSTER PUMPS (2)
100 BBL. FILTERED PROD. WTR. SURGE TANK
CHEMICAL INJECTION PACKAGE
10 TONS (DRY) 50 TONS (FLOODED)
WET OIL TANK
500 BBL.
DRY OIL TANK
2500 BBL.
45 TONS (DRY)
650 TONS (FLOODED)
LACT UNIT, PUMPS & PROVER LOOP
24 TONS
PIPELINE SHIPPING PUMP SKID
32 TONS
SPHERE LAUNCHERS DRY OIL TO SHORE
SPHERE LAUNCHER & RECEIVERS
(GAS/WET OIL & INJECTION WATER TO & FROM REMOTE PLATFORM)
14 TONS (DRY) + 50 TONS (FLOODED)
DEAERATOR COLUMN
14 TONS (DRY) + 145 TONS (FLOODED)
14 TONS (DRY) + 145 TONS (FLOODED)
SOURCE WATER FILTERS
19 TONS (DRY) + 200 TONS (FLOODED)
19 TONS (DRY) + 200 TONS (FLOODED)
PRODUCED WATER FILTERS
19 TONS (DRY) + 200 TONS (FLOODED)
19 TONS (DRY) + 200 TONS (FLOODED)
PRODUCED WATER FILTERS
FIRE WATER PUMP
11 TONS
30'-0"
50'-0"
150'-0"
50'-0"
20'-0"
30'-0"
50'-0"
60'-0"
50'-0"
20'-0"
210'-0"
BRIDGE
℄ PLATFORM
WNW PREVAILING WIND
N
W
E
S
26°
LOWER DECK
FOR PRELIMINARY ONLY
DATE: 10-4-77
8-31-77 MISC. REV.
DATE REVISION BY APPD.
SHELL OIL COMPANY
EQUIPMENT LAYOUT
LOWER DECK
12-LEG FACILITIES PLATFORM
BETA PROSPECT
DATE: 8-17-77 DRWN: D.R.K. DCN: F.E.G. DRV. WST N.
SCALE: 1/8" = 1'-0"
APPROVED:
No. C6-1714

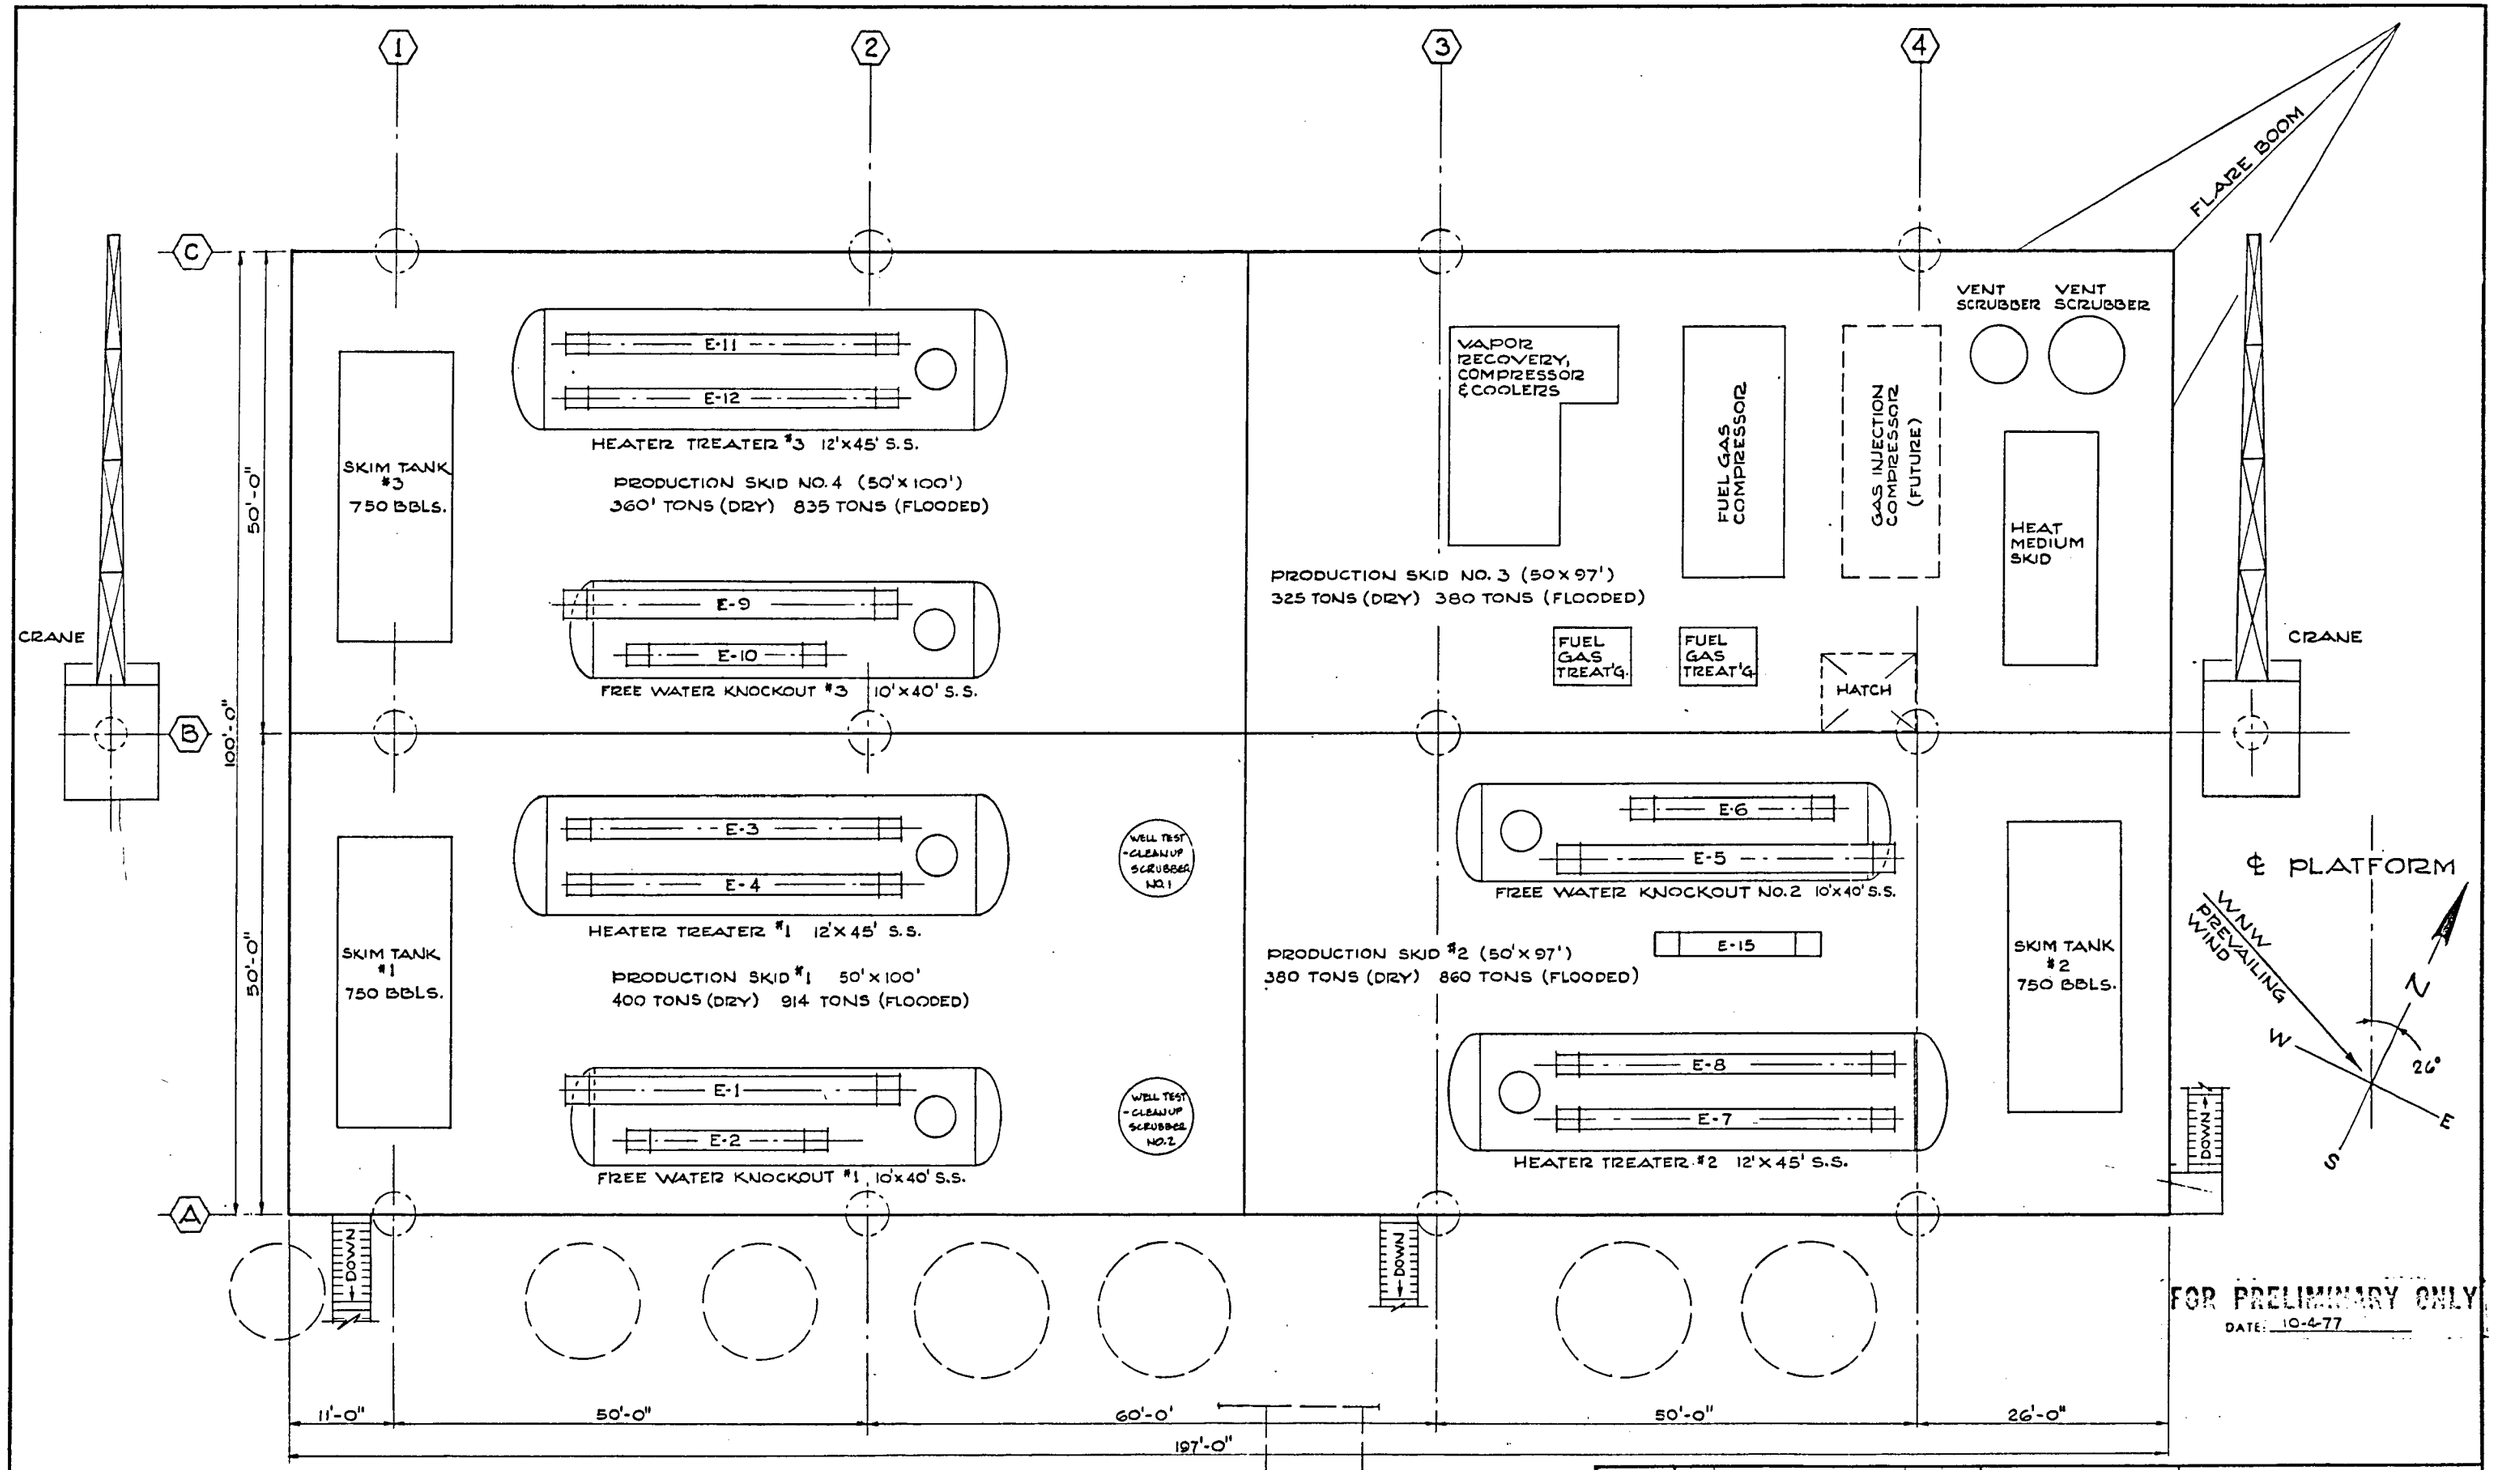

REVIEWED BY:	DATE	REVISION	BY	APP'D.
PROJ. ENGR.				
ENGR.				
OPR.				
CONST.				
S.E.C.	8-31-77	RELOCATED E-15 & MISC.	ETB	

RELEASED ONLY FOR:	GROUP LEADER	DESIGN ENGR.	DATE
CHECKING			
PRELIMINARY			
BIDDING			
FABRICATION			
ERECTION			

SHELL OIL COMPANY

EQUIPMENT LAYOUT
UPPER DECK
12-LEG FACILITIES PLATFORM
BETA PROSPECT

DATE: 8-17-77 | DWN. DRK | DGN. FEG | DIV. WESTERN
SCALE: 1/8" = 1'-0" | No. C6-1715
APP'D.

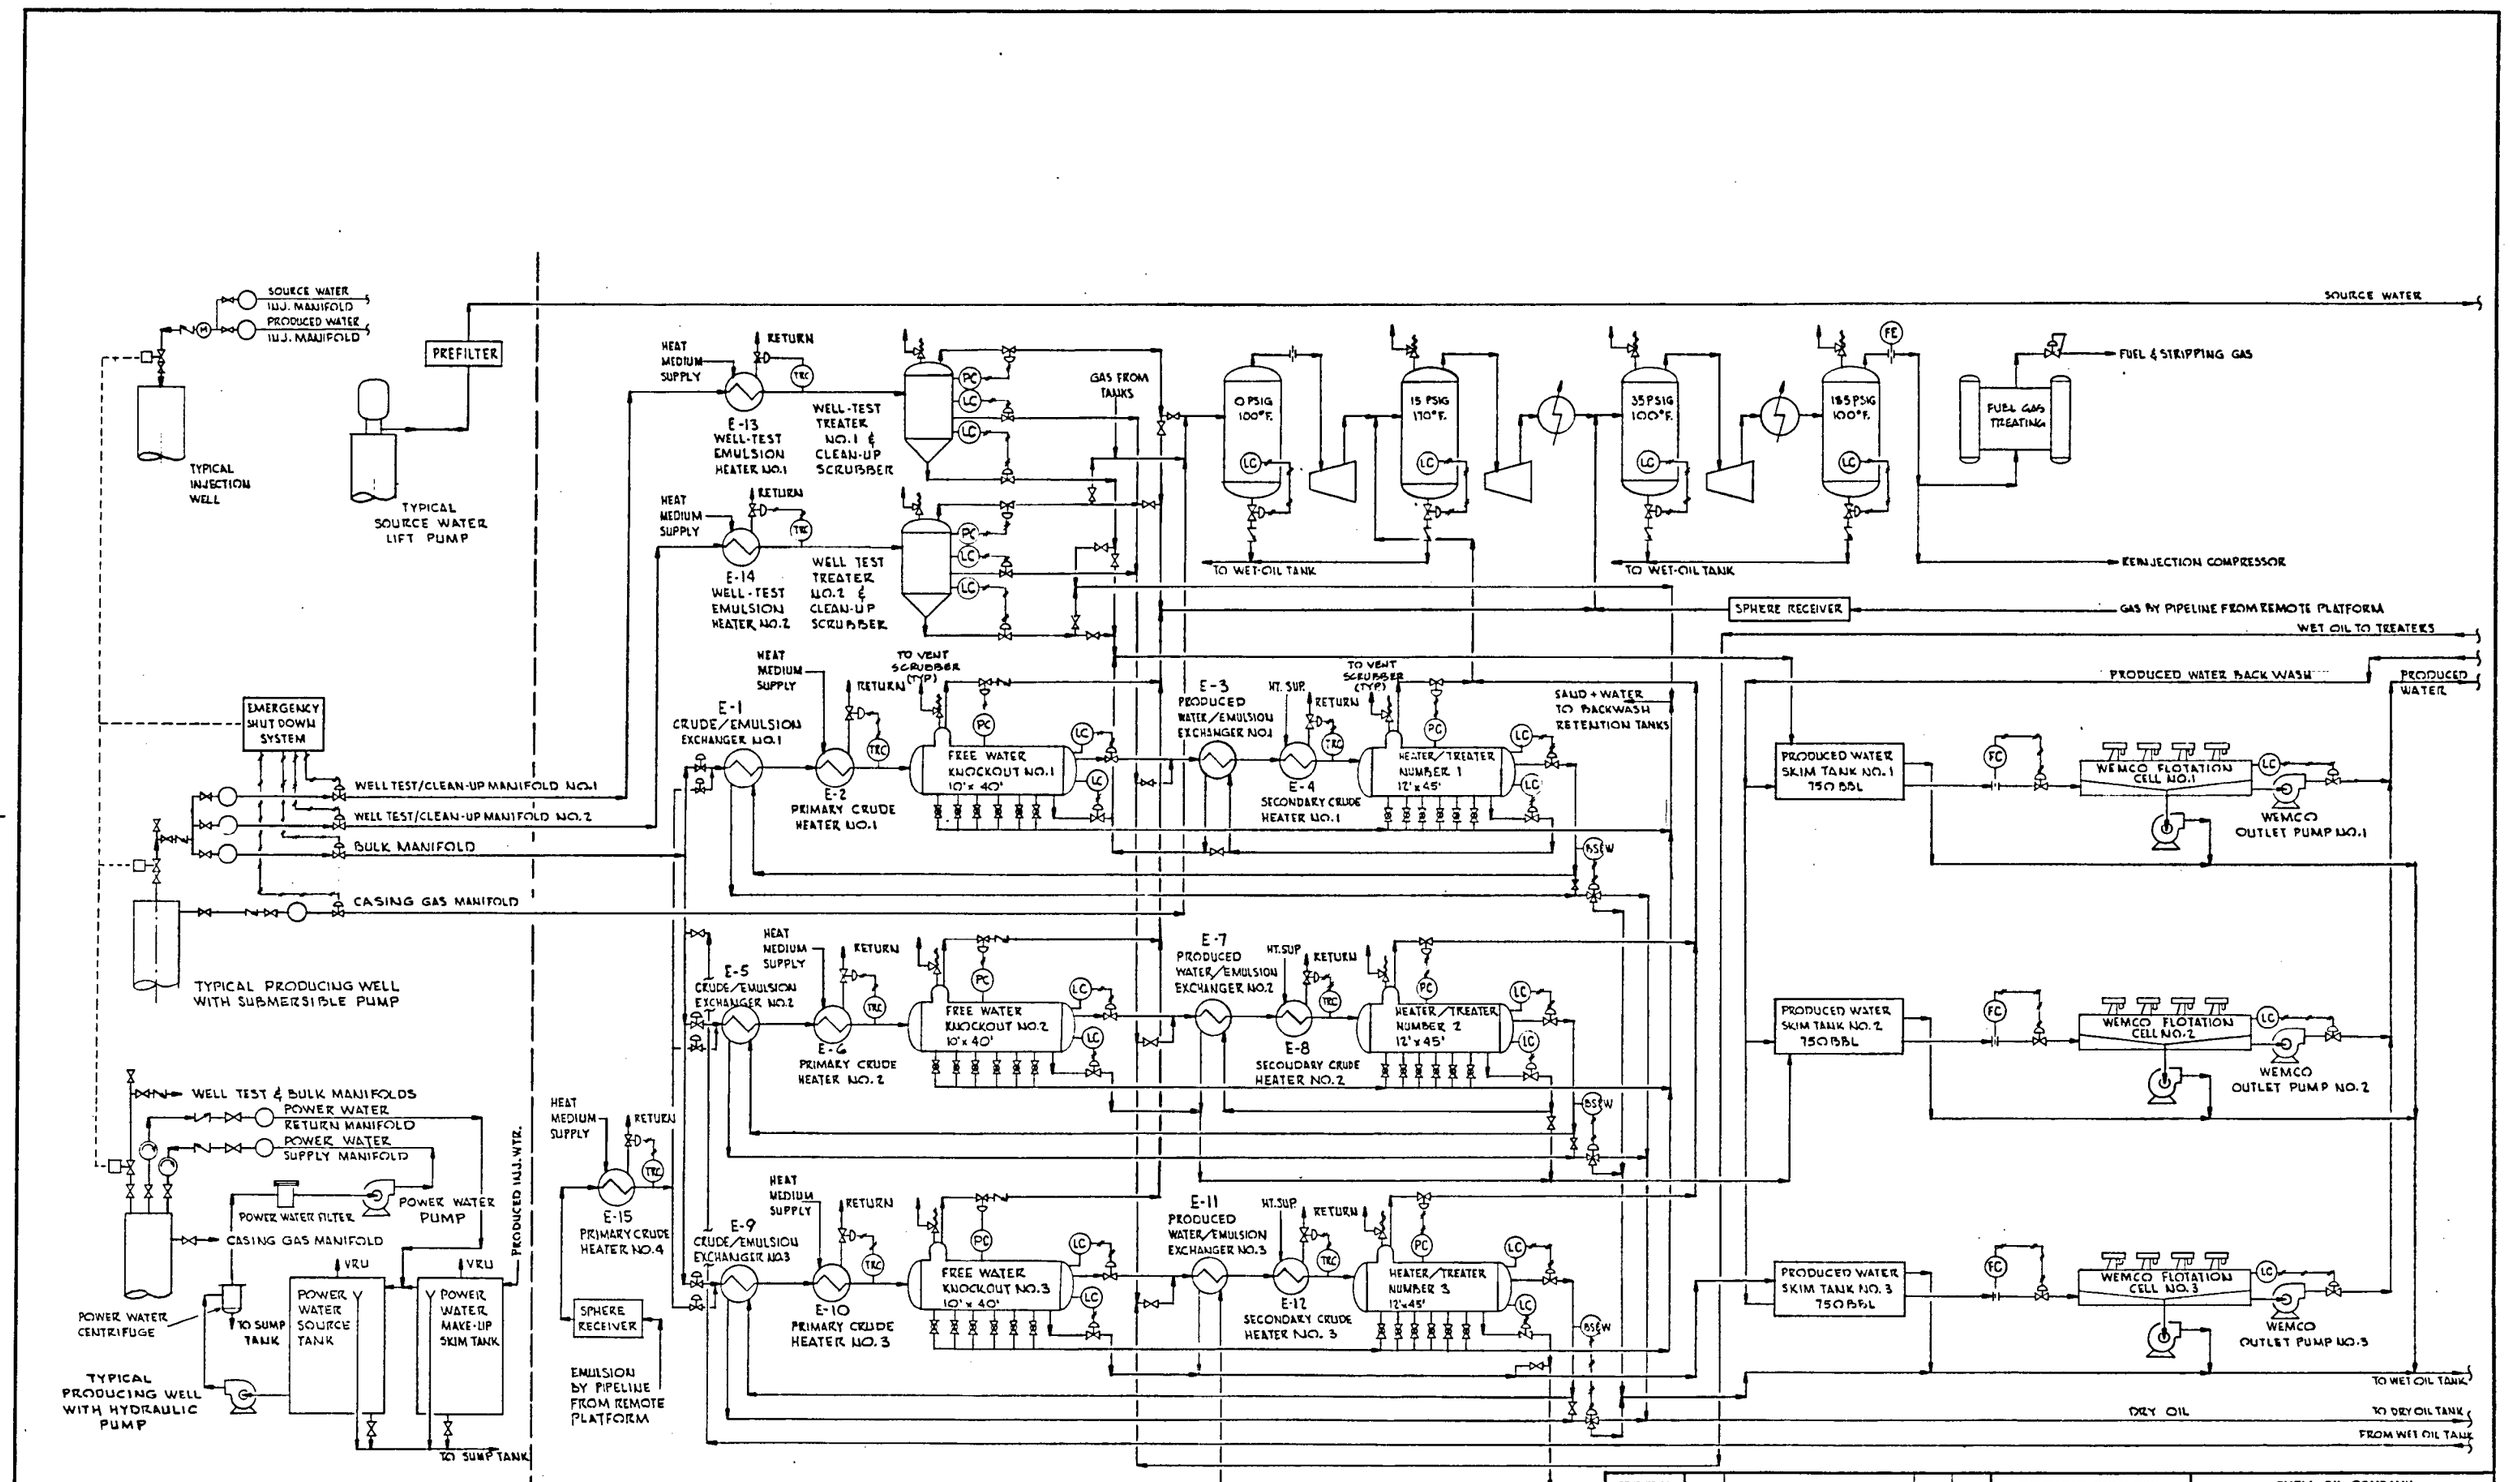

FOR PRELIMINARY ONLY

DATE: 10-4-77

REVIEWED BY:	DATE	REVISION	BY	APP'D
PROJ. ENGR.				
ENGR.				
OPR.				
CONST.				
S.E.C.	8-31-77	DELETED BULK MANIFOLD NO.2	STS	

RELEASED ONLY FOR:

	GROUP LEADER	DESIGN ENGR.	DATE
CHECKING			
PRELIMINARY			
BIDDING			
FABRICATION			
ERECTION			

SHELL OIL COMPANY

PROCESS FLOW SHEET
SHEET 1
SHALLOW WATER COMPLEX
BETA PROSPECT

DATE: 8/9/76 | DWN. A.R. | DGN. F.E.G. | DIV. WESTERN
SCALE: NONE | APP'D | No. CG-1716

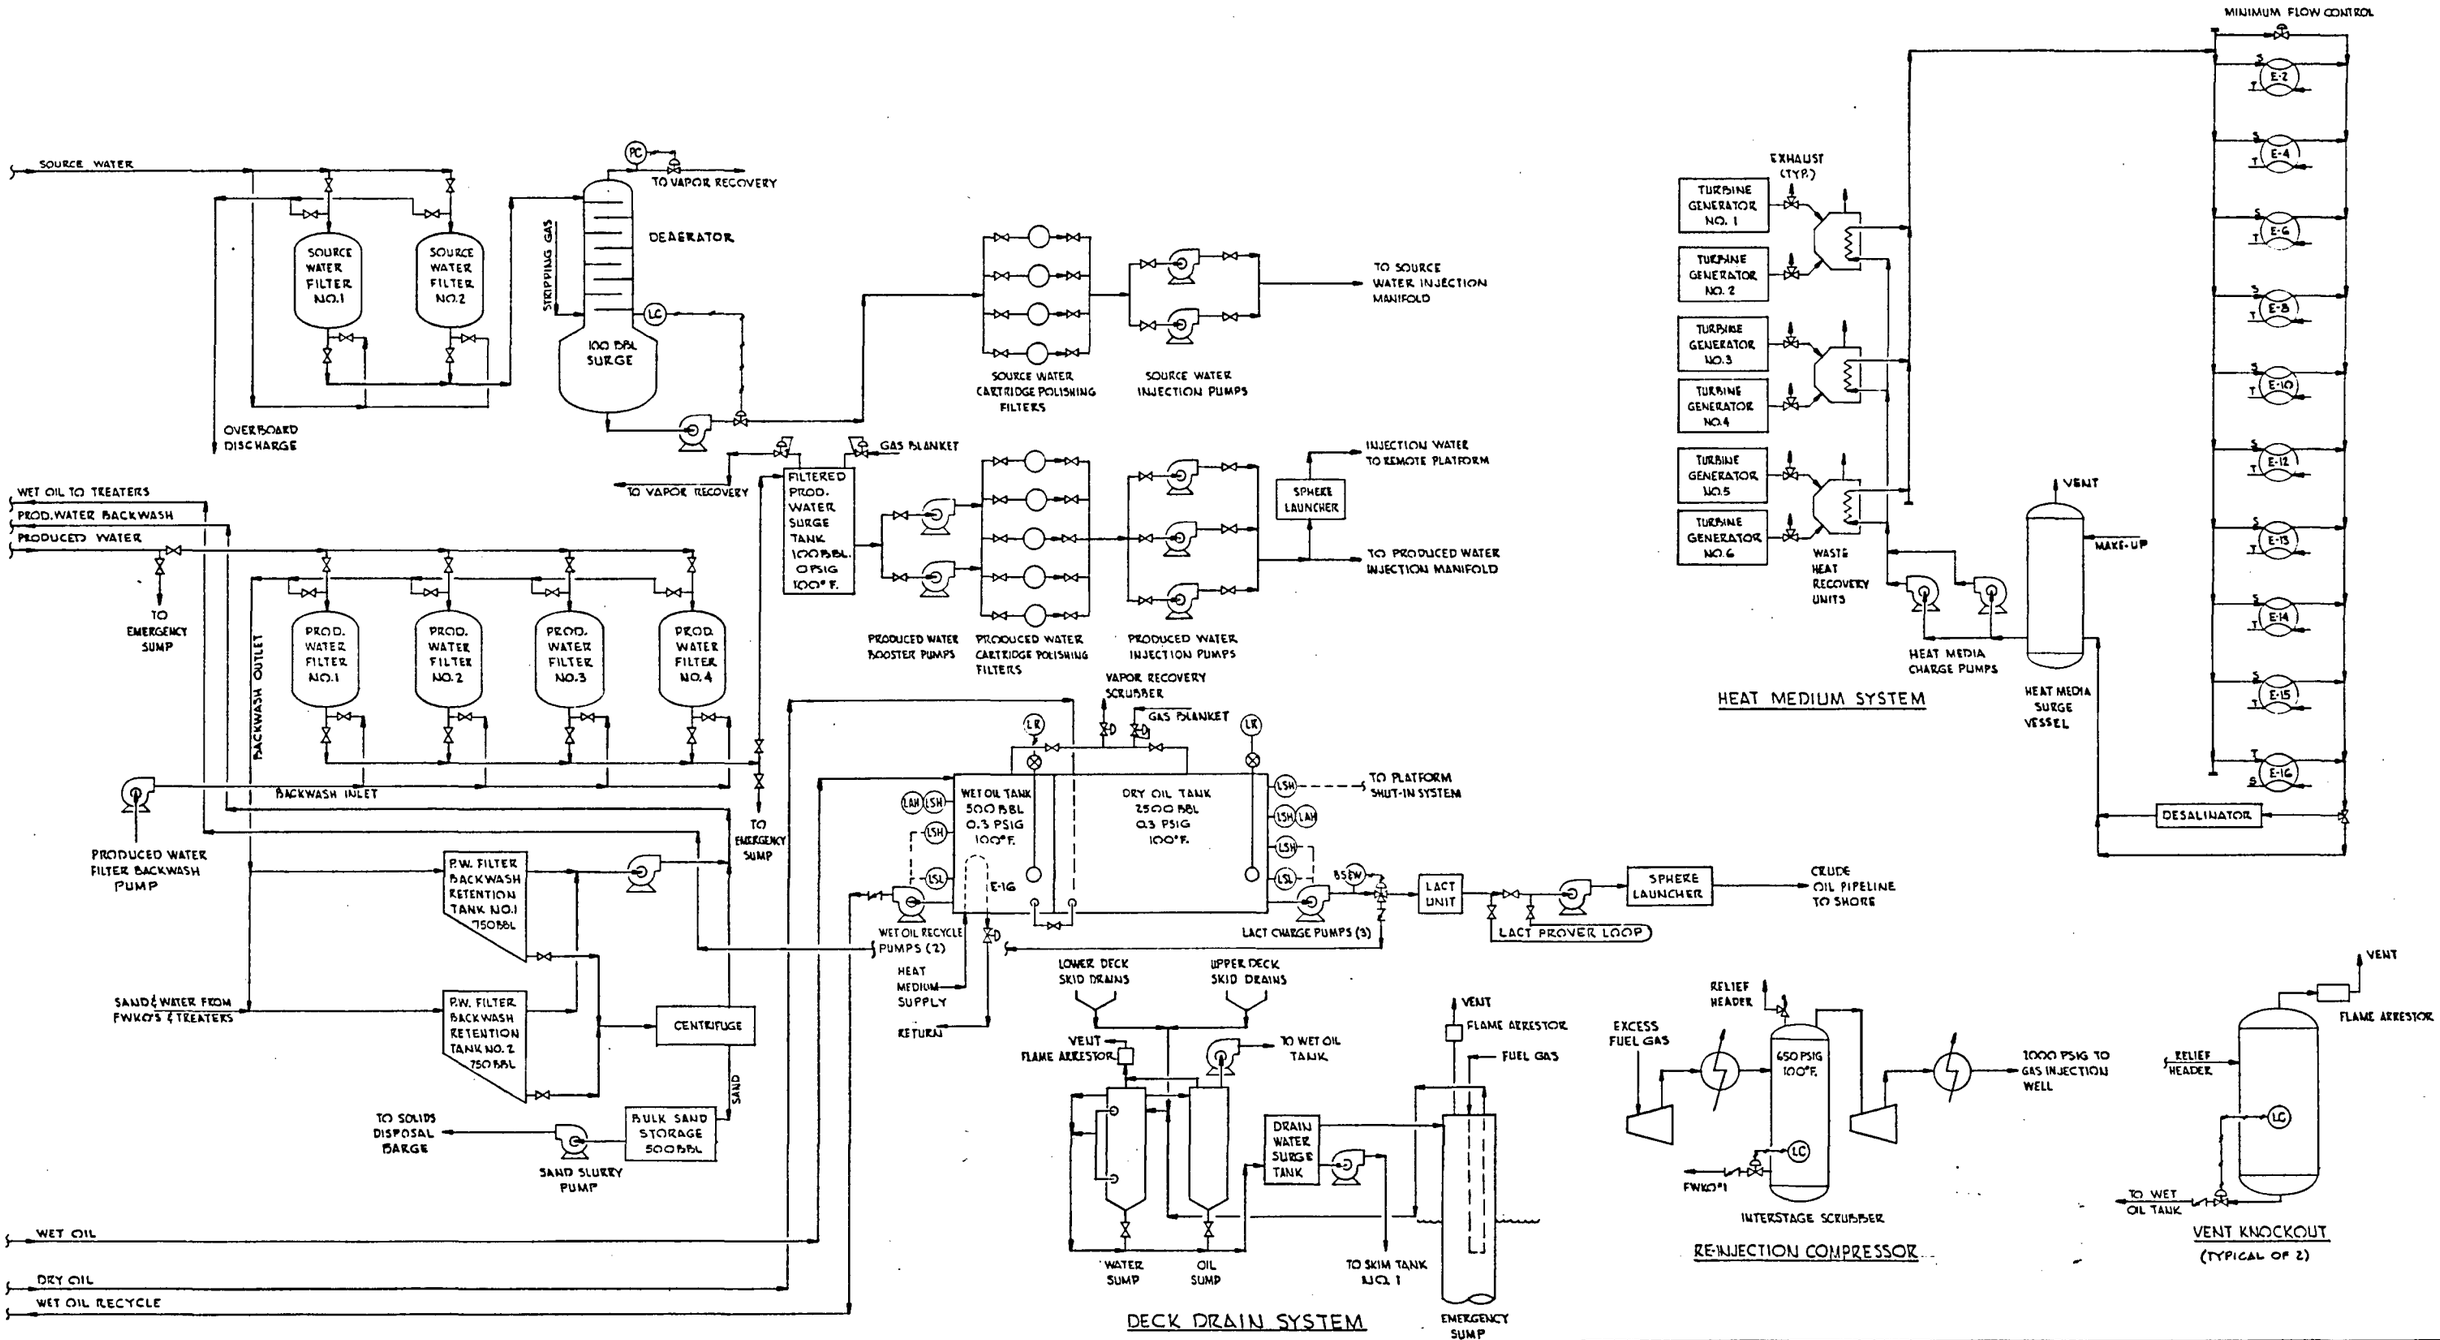

FOR PRELIMINARY ONLY

DATE: 10-4-77

REVIEWED BY:	DATE	REVISION	BY	APP'D
PROJ. ENGR.				
ENGR.				
OPR.				
CONST.				
S.E.C.				

RELEASED ONLY FOR:	GROUP LEADER	DESIGN ENGR.	DATE
CHECKING			
PRELIMINARY			
BIDDING			
FABRICATION			
ERECTION			

SHELL OIL COMPANY

PROCESS FLOW SHEET
SHEET 2
SHALLOW WATER COMPLEX
BETA PROSPECT

DATE: 8-19-76 | DWN. A. P. | DGN. F.E.G. | DIV. WESTERN
SCALE: NONE | APP'D
No. CG-1717

Well Forecast Data

Pursuant to the Freedom of Information Act (5 U.S.C. 552) and its implementing regulations (43 CFR Part 2) and as provided in 30 CFR 550.199(b), the information contained in this section is deleted from the public information copy of this submission.

Proprietary

Not for Public Release

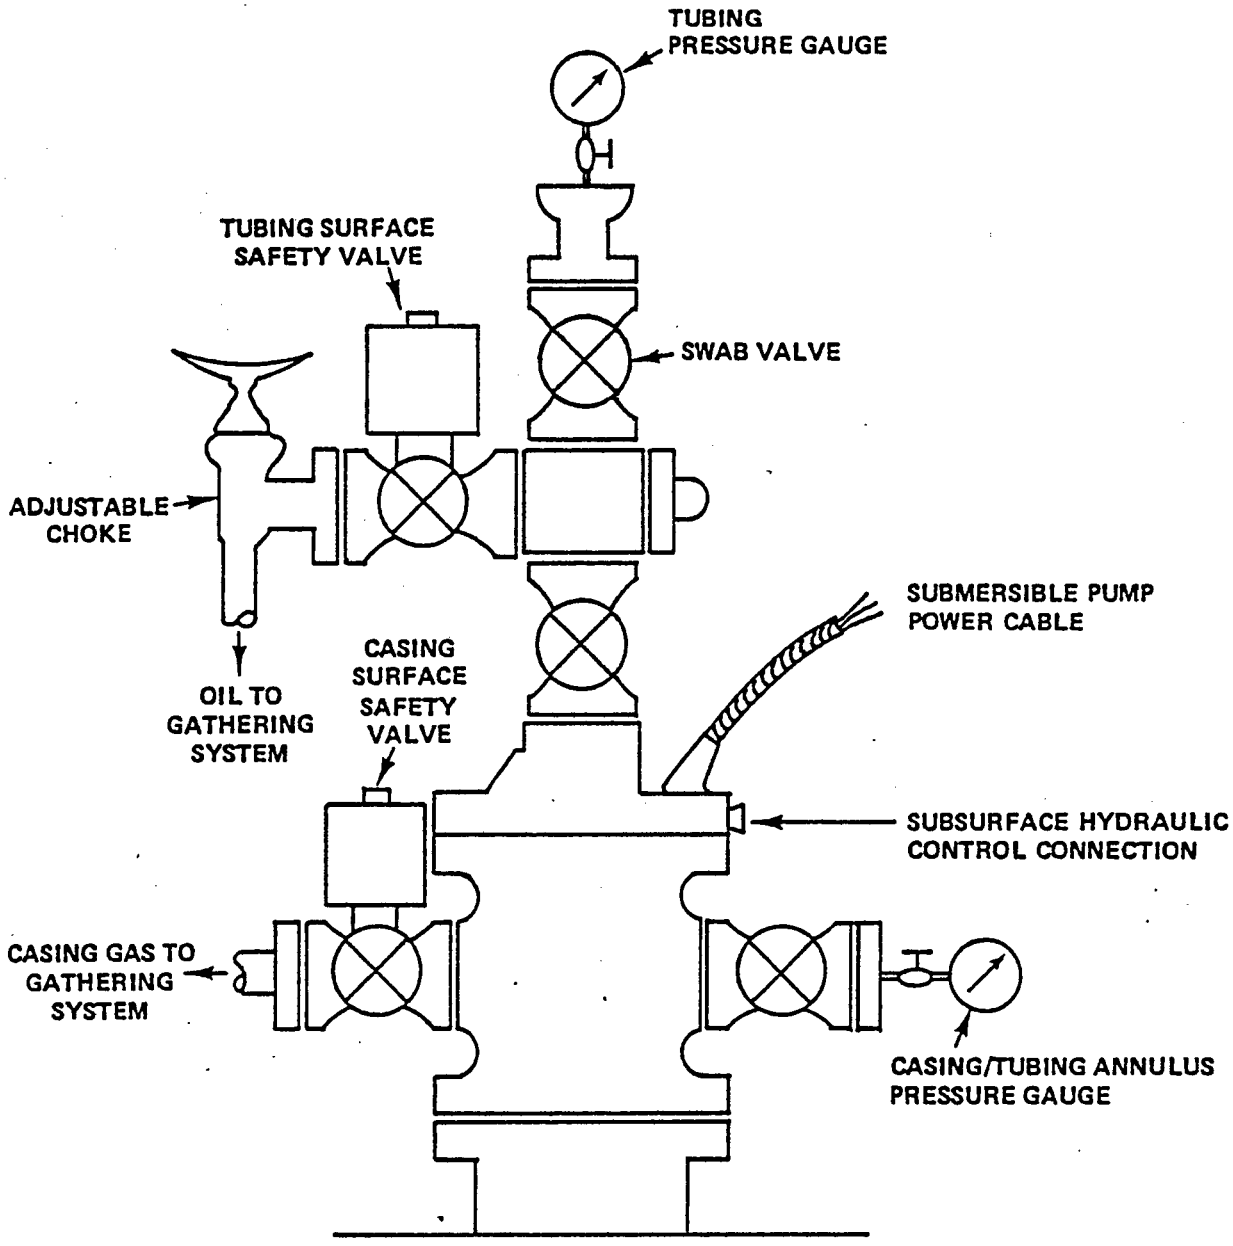

REVIEWED BY:	RELEASED ONLY FOR:				SHELL OIL COMPANY			
PROJ. ENGR.					WELLHEAD ARRANGEMENT			
ENGR.		GROUP LEADER	DESIGN ENGR.	DATE				
OPR.	CHECKING							
	PRELIMINARY							
CONST.	BIDDING				DATE: 9-8-77	DWN. RLK	DGN. GPD	DIV. WESTERN
S.E.C.	FABRICATION				SCALE:	No.	ZF 2627	
	ERECTION				APP'D.			

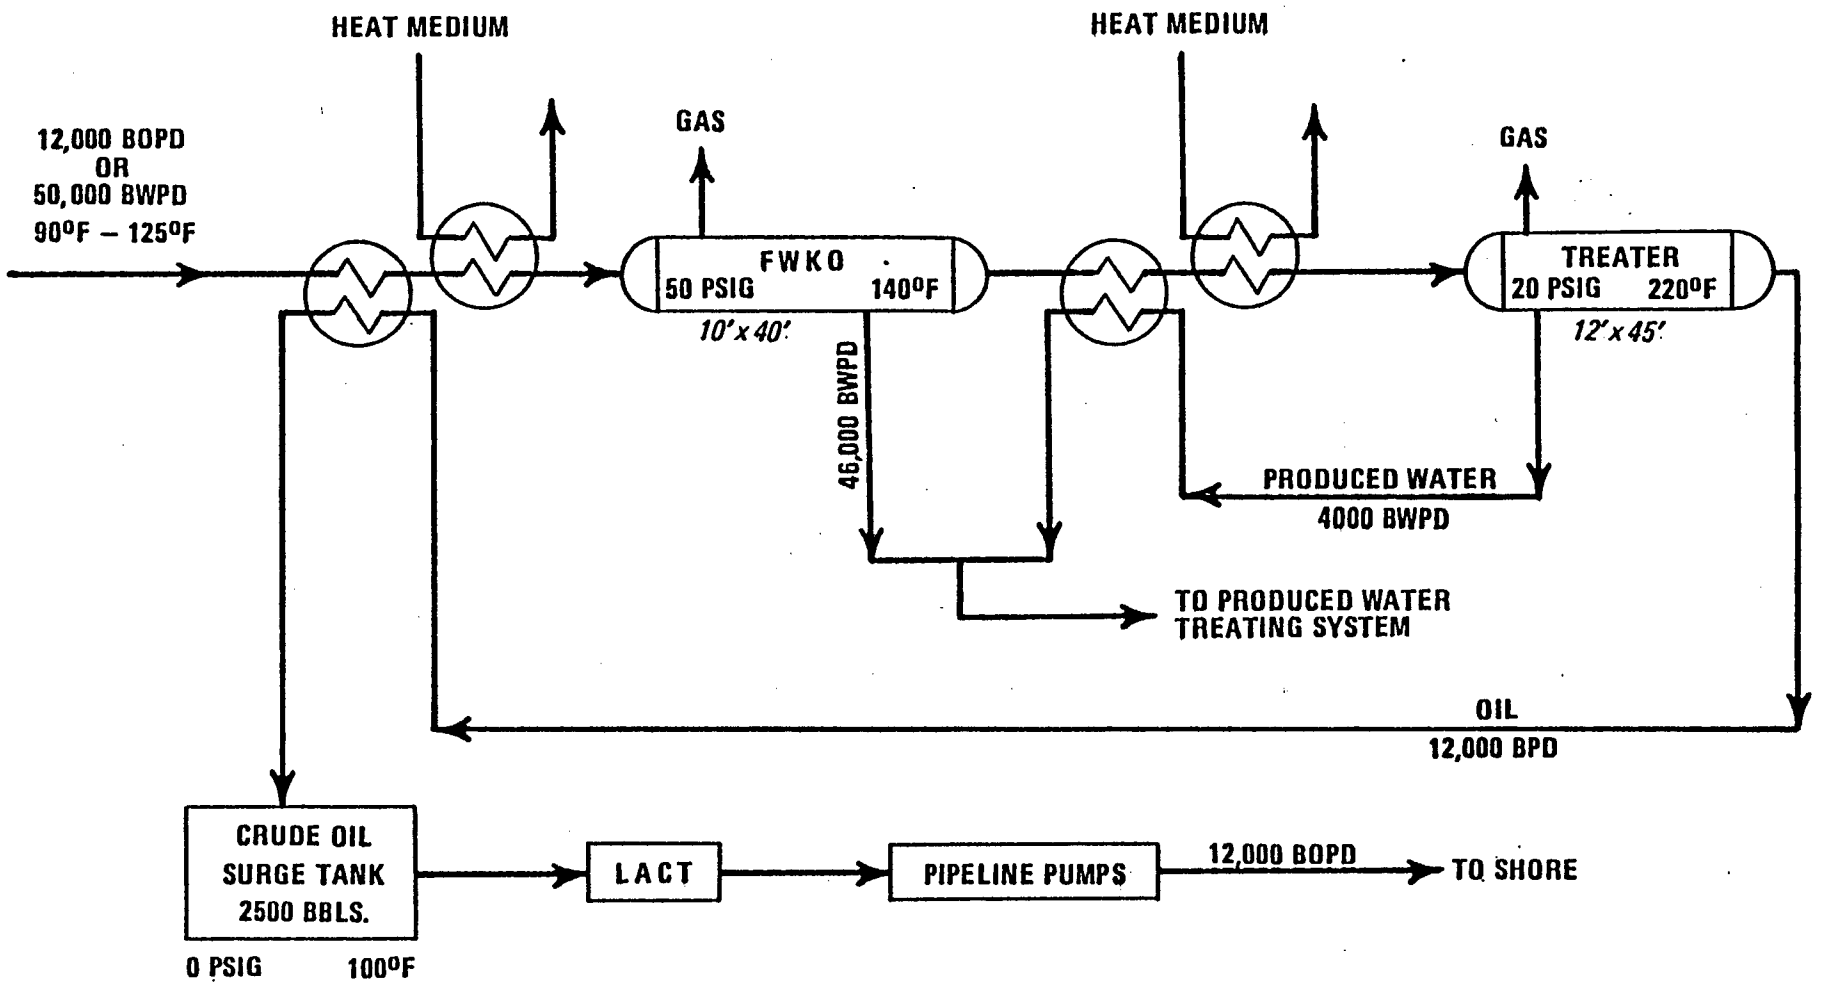

SINGLE TRAIN
OIL DEHYDRATION
PROSPECT BETA

ETB 8/2/77
Z9-499b

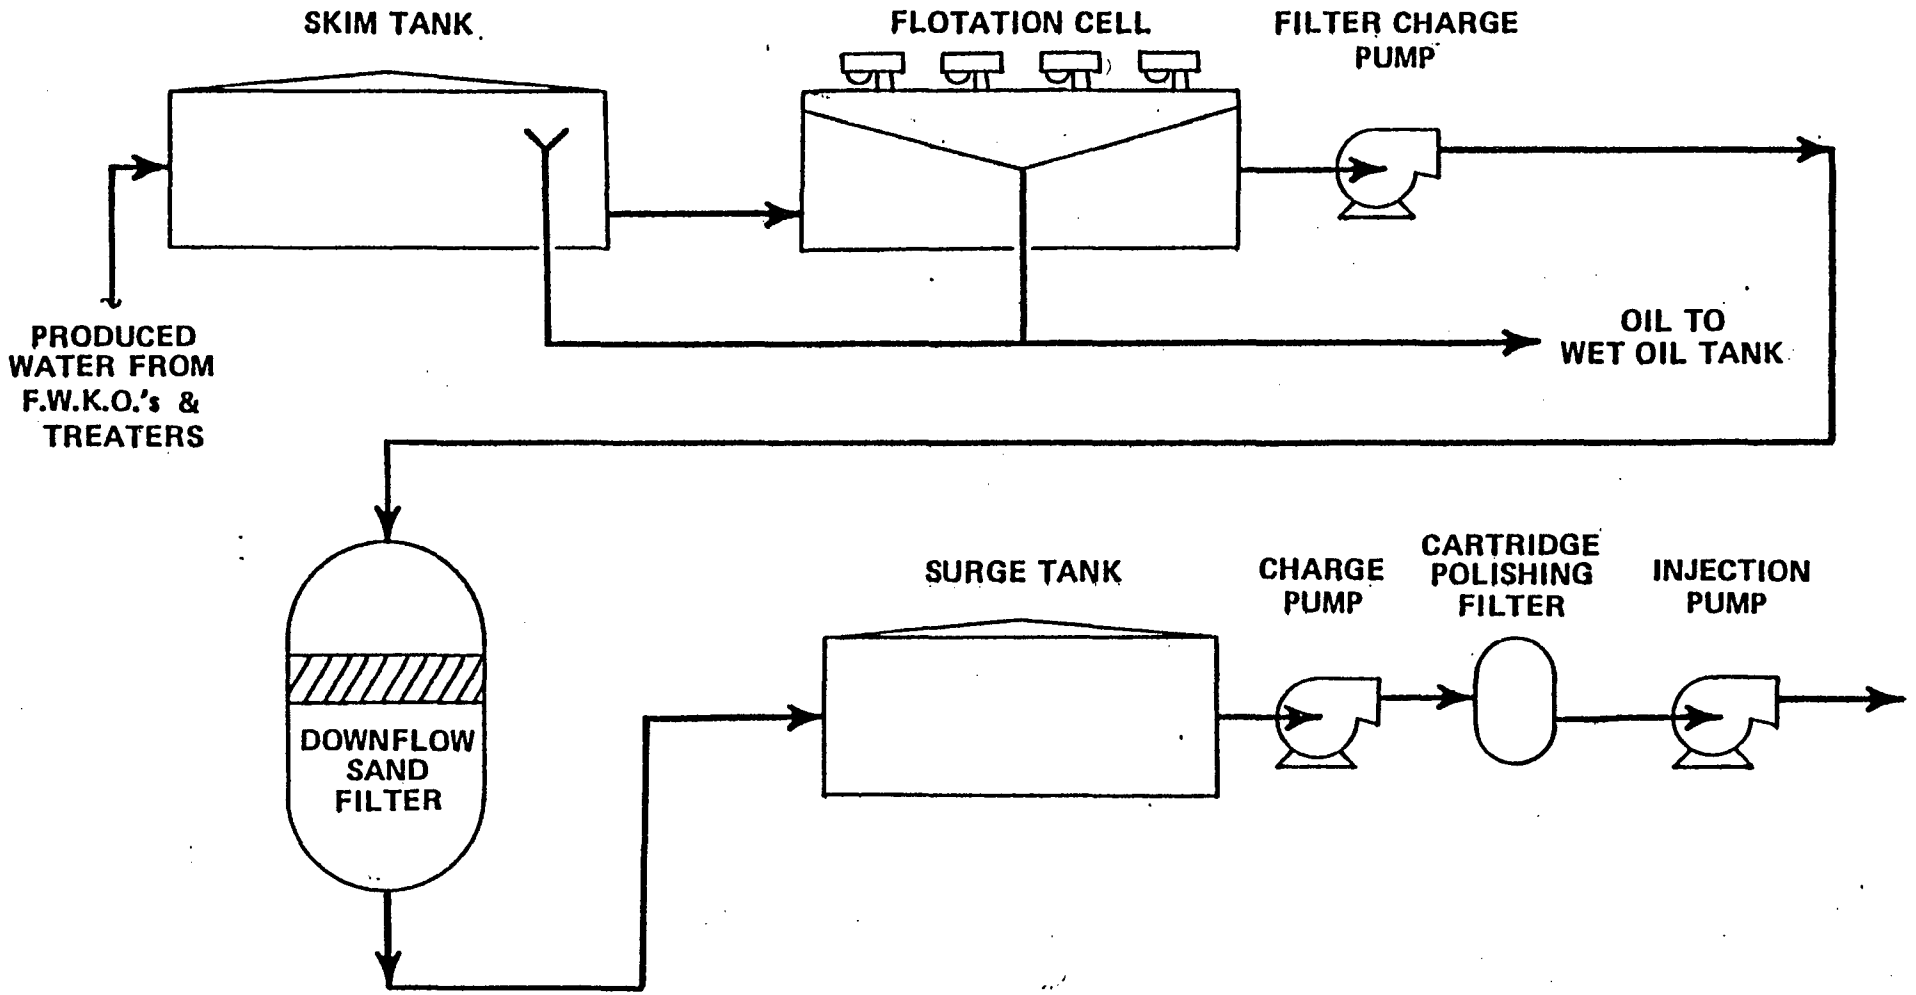

SIMPLIFIED PROCESS FLOW
PRODUCED WATER TREATMENT
PROSPECT BETA

ETB 7/29/77
Z9-499

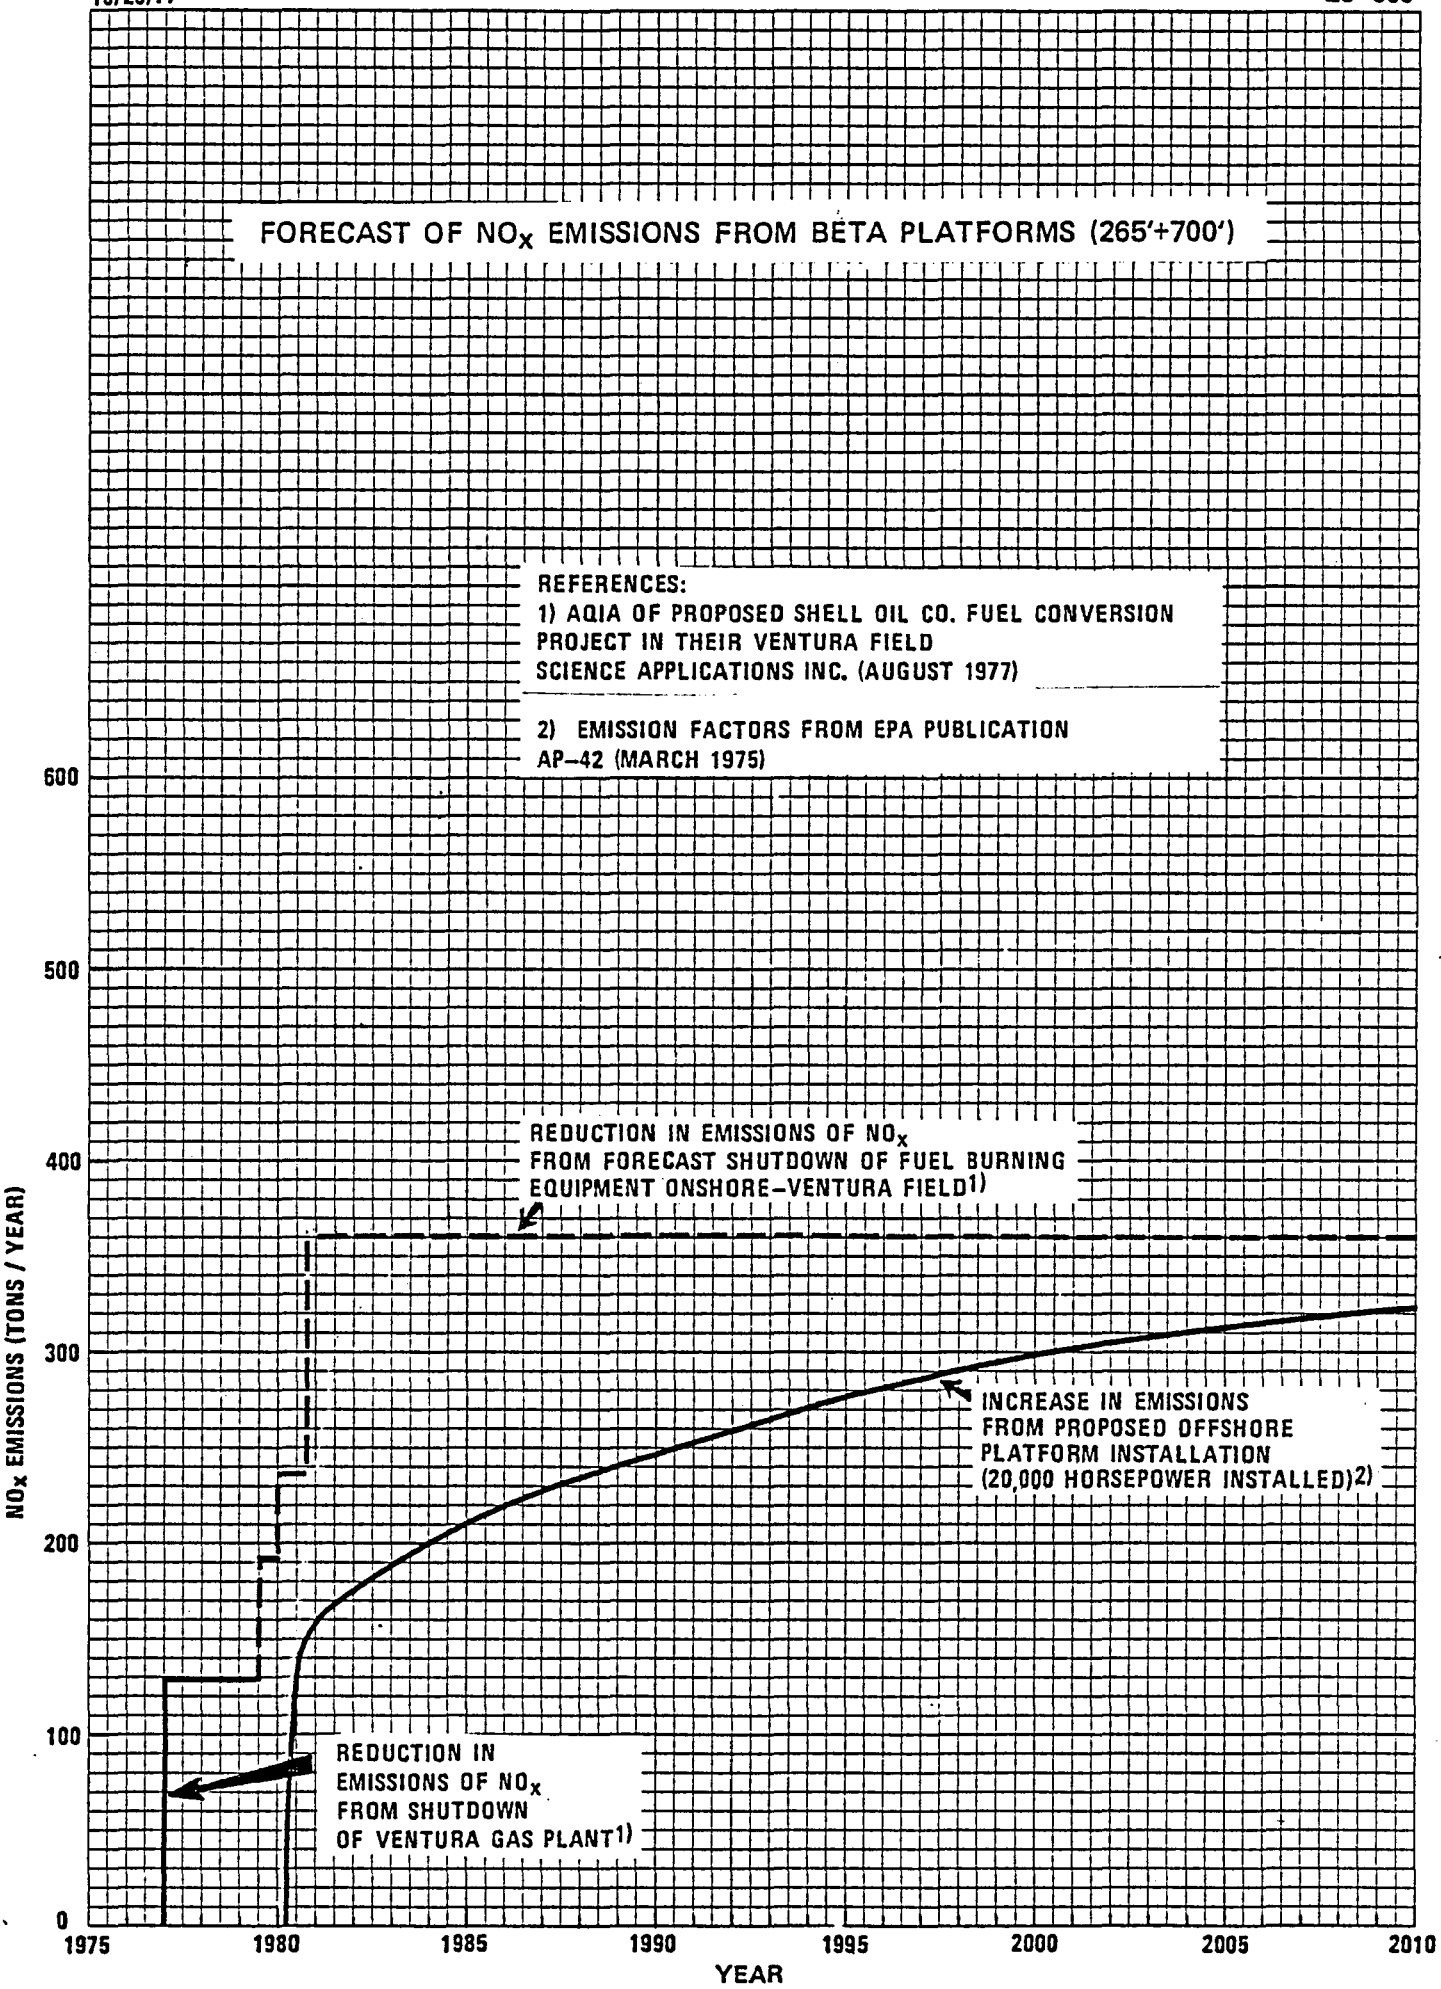
FORECAST OF NO_X EMISSIONS FROM BETA PLATFORMS (265'+700')
REFERENCES:
1) AQIA OF PROPOSED SHELL OIL CO. FUEL CONVERSION PROJECT IN THEIR VENTURA FIELD SCIENCE APPLICATIONS INC. (AUGUST 1977)
2) EMISSION FACTORS FROM EPA PUBLICATION AP–42 (MARCH 1975)
REDUCTION IN EMISSIONS OF NO_X FROM FORECAST SHUTDOWN OF FUEL BURNING EQUIPMENT ONSHORE–VENTURA FIELD 1)
INCREASE IN EMISSIONS FROM PROPOSED OFFSHORE PLATFORM INSTALLATION (20,000 HORSEPOWER INSTALLED) 2)
REDUCTION IN EMISSIONS OF NO_X FROM SHUTDOWN OF VENTURA GAS PLANT 1)
NO_X EMISSIONS (TONS / YEAR)
0
100
200
300
400
500
600
1975
1980
1985
1990
1995
2000
2005
2010
YEAR

SECTION VII

SUBSEA PIPELINE AND ONSHORE FACILITIES

TABLE OF CONTENTS

		Page
7.1	Introduction	7-1
7.2	Pipeline Routes and Facilities	7-1
7.2.1	Long Beach Route	
7.2.2	Huntington Beach Route	
7.2.3	Seal Beach Route	
7.3	Design Criteria and Objectives	7-2
7.3.1	Basis for Design	
7.3.2	Applicable Regulations and Codes	
7.3.3	Stability	
7.3.4	Maximum Operating Pressure	
7.3.5	External Pressure	
7.3.6	Other Stresses	
7.3.7	External Corrosion Protection	
7.3.8	Internal Corrosion Protection	
7.3.9	Construction Method	
7.3.10	Pipeline Operation	
7.4	Attachments	
Figure 7-1	Preferred Subsea Pipeline Routes	
Figure 7-2	Pipeline Landfall - Long Beach	

SECTION VII

SUBSEA PIPELINE AND ONSHORE FACILITIES

7.1 Introduction

A subsea pipeline to transport the clean crude from the dehydration facilities on the platform is planned for installation during late 1979 or early 1980. Pipeline capacity will be sufficient for handling production from not only the platforms in the Unit but also from other San Pedro Bay parcels which might logically be included in this system. It is expected that Unit production will peak at about 26,000 B/D oil and that the oil will be shipped to shore via pipeline.

7.1.1 Long Beach is the preferred landfall, from which the oil may be routed to various refineries. We plan to install a 16-inch line capable of transporting 40,000 B/D oil to shore with shore facilities to handle the 26,000 B/D expected maximum oil production.

7.1.2 Huntington Beach is a possible landfall, from which the oil could be routed to Chevron's Huntington Beach pipeline terminal and thence to their El Segundo Refinery. A 16" line to shore would transport 40,000 B/D oil but, even with onshore heating and blending, this volume of oil could not be moved through Chevron's pipelines.

7.1.3 Seal Beach landfall with a 16" line would require onshore installation of eleven miles of 16" or 20" pipeline to Shell's Wilmington Refinery.

7.1.4 The preferred pipeline route is shown on maps included in this section.

7.2 Pipeline Routes and Facilities

7.2.1 The subsea portion of the pipeline route to Long Beach is approximately 14 miles long. Landfall is planned on Pier J near the Queen Mary as shown on Figure 7-2. The proposed route would parallel the THUMS clean oil lines to the THUMS seven company distribution manifold about two miles inland. A site along the route, but preferably near the THUMS manifold is planned for facilities consisting of a scraper trap, meters, a tank equipped for vapor recovery, pumps and manifold. The facilities could

easily be expanded to handle larger than expected oil production.

7.2.2 The pipeline route to the Huntington Beach coast is approximately nine miles long and is the shortest distance to shore. With landfall near the foot of the bluff immediately west of the Huntington Beach city limits, a possible route would cross the beach, pass through a bore under Pacific Coast Highway, cross privately owned oilfield property west of the bluff, thence along city streets to an existing Chevron pipeline terminal about three miles inland. Acquisition of about one acre of land is required for facilities. These facilities will consist of heaters or heat exchangers for heating the crude from 55°-60°F to 110°-120°F, scraper trap, meters, a tank equipped for vapor recovery and pumps. Since other pipelines in the area are believed to be near capacity, installation of up to 38 miles of additional onshore pipeline will be required to handle crude volumes much in excess of 25-30,000 B/D.

7.2.3 The subsea pipeline route to Seal Beach is slightly more than 11 miles long, but requires installation of 11 miles or so of new land line to Shell's Wilmington Refinery. A 16" line will move 40,000 B/D oil to shore. Onshore facilities are required in or near Seal Beach which will consist of a scraper trap, meters, a tank equipped for vapor recovery, pumps, scraper launcher and about 11 miles of 16" or 20" land line. Sites along the route are needed for metering oil to other refiners.

7.3 Design Criteria and Objectives

7.3.1 Basis for Design

The oil line to shore would be designed for a maximum throughput of at least 40,000 barrels per day of sour crude. Since all gas produced will be used on the platform for power generation and oil dehydration, gas transportation facilities are not planned.

7.3.2 Applicable Regulations and Codes

The oil line will be designed in compliance with USGS, Conservation Division, Branch of Oil & Gas Operations, Pacific Region, OCS Order No. 9, dated June 1, 1971, ANSI B31.4-1974, "Liquid Petroleum Transportation Piping Systems", and Department of Transportation Regulation 49, Part 195, as amended

August 18, 1976, "Transportation of Liquids by Pipeline". Portions of the pipeline routes within the jurisdiction of the State of California would be designed in compliance with any additional State regulations in effect at that time. In addition to the above, the pipeline design and operating procedures would follow API Recommended Practice RP 1111, Design, Construction, Operation and Maintenance of Offshore Hydrocarbon Pipelines, March 1976, and the Department of Interior/Department of Transportation memorandum of understanding of June 11, 1976.

7.3.3 Stability

The offshore portions of the pipeline will be designed to resist movement under the action of on-bottom currents predicted to occur during the design 100-year storm. Stability will be achieved by proper design of submerged pipeline weight. The pipeline, appropriately protected, will be placed on the ocean bottom.

7.3.4 Maximum Operating Pressure

Maximum operating pressures of the line will be 1440 psi and be designed to withstand this maximum operating pressure under applicable codes and regulations.

7.3.5 External Pressure

The pipeline will be designed to withstand external loads, including hydrostatic pressures with the pipeline void and with its absolute internal pressure equal to one atmosphere.

7.3.6 Other Stresses

The pipeline will be designed under applicable codes and regulations to withstand stresses which result from installation, thermal and fluid expansion effects, earthquake and other dynamic effects, dead loads, and surges.

7.3.7 External Corrosion Protection

The pipeline will be protected against external corrosion by means of external coatings and cathodic protection. Choice of coating materials and cathodic protection systems, impressed current or

sacrificial anodes, will be based on detailed studies of the selected pipeline route.

7.3.8 Internal Corrosion Protection

Internal corrosion in this clean oil pipeline is not expected. However, the use of inhibitors is planned. Testing and monitoring for internal corrosion will dictate the extent of the program.

7.3.9 Construction Method

The construction technique used for the offshore portion of the pipeline is influenced by relative economics and availability of equipment at the time of installation. The use of the pull method is planned at the present time, but is subject to review.

The pipeline's near shore end would be buried in the section through the beach and surf zone to the MLL water level, excepting that all of the pipeline inside the Long Beach breakwater would be buried.

The onshore portion of the pipeline would be installed using conventional land-type pipeline construction methods and equipment. Testing and inspection of all sections of the pipeline would be in compliance with all applicable codes and regulations.

7.3.10 Pipeline Operation

The pipeline will be operated and regularly inspected in compliance with USGS and DOT regulations. Safety and monitoring devices, such as leak detectors, shut-ins, etc. will be provided in accordance with OCS Order No. 9. Recordkeeping and reporting will be in accordance with all federal and state regulations.

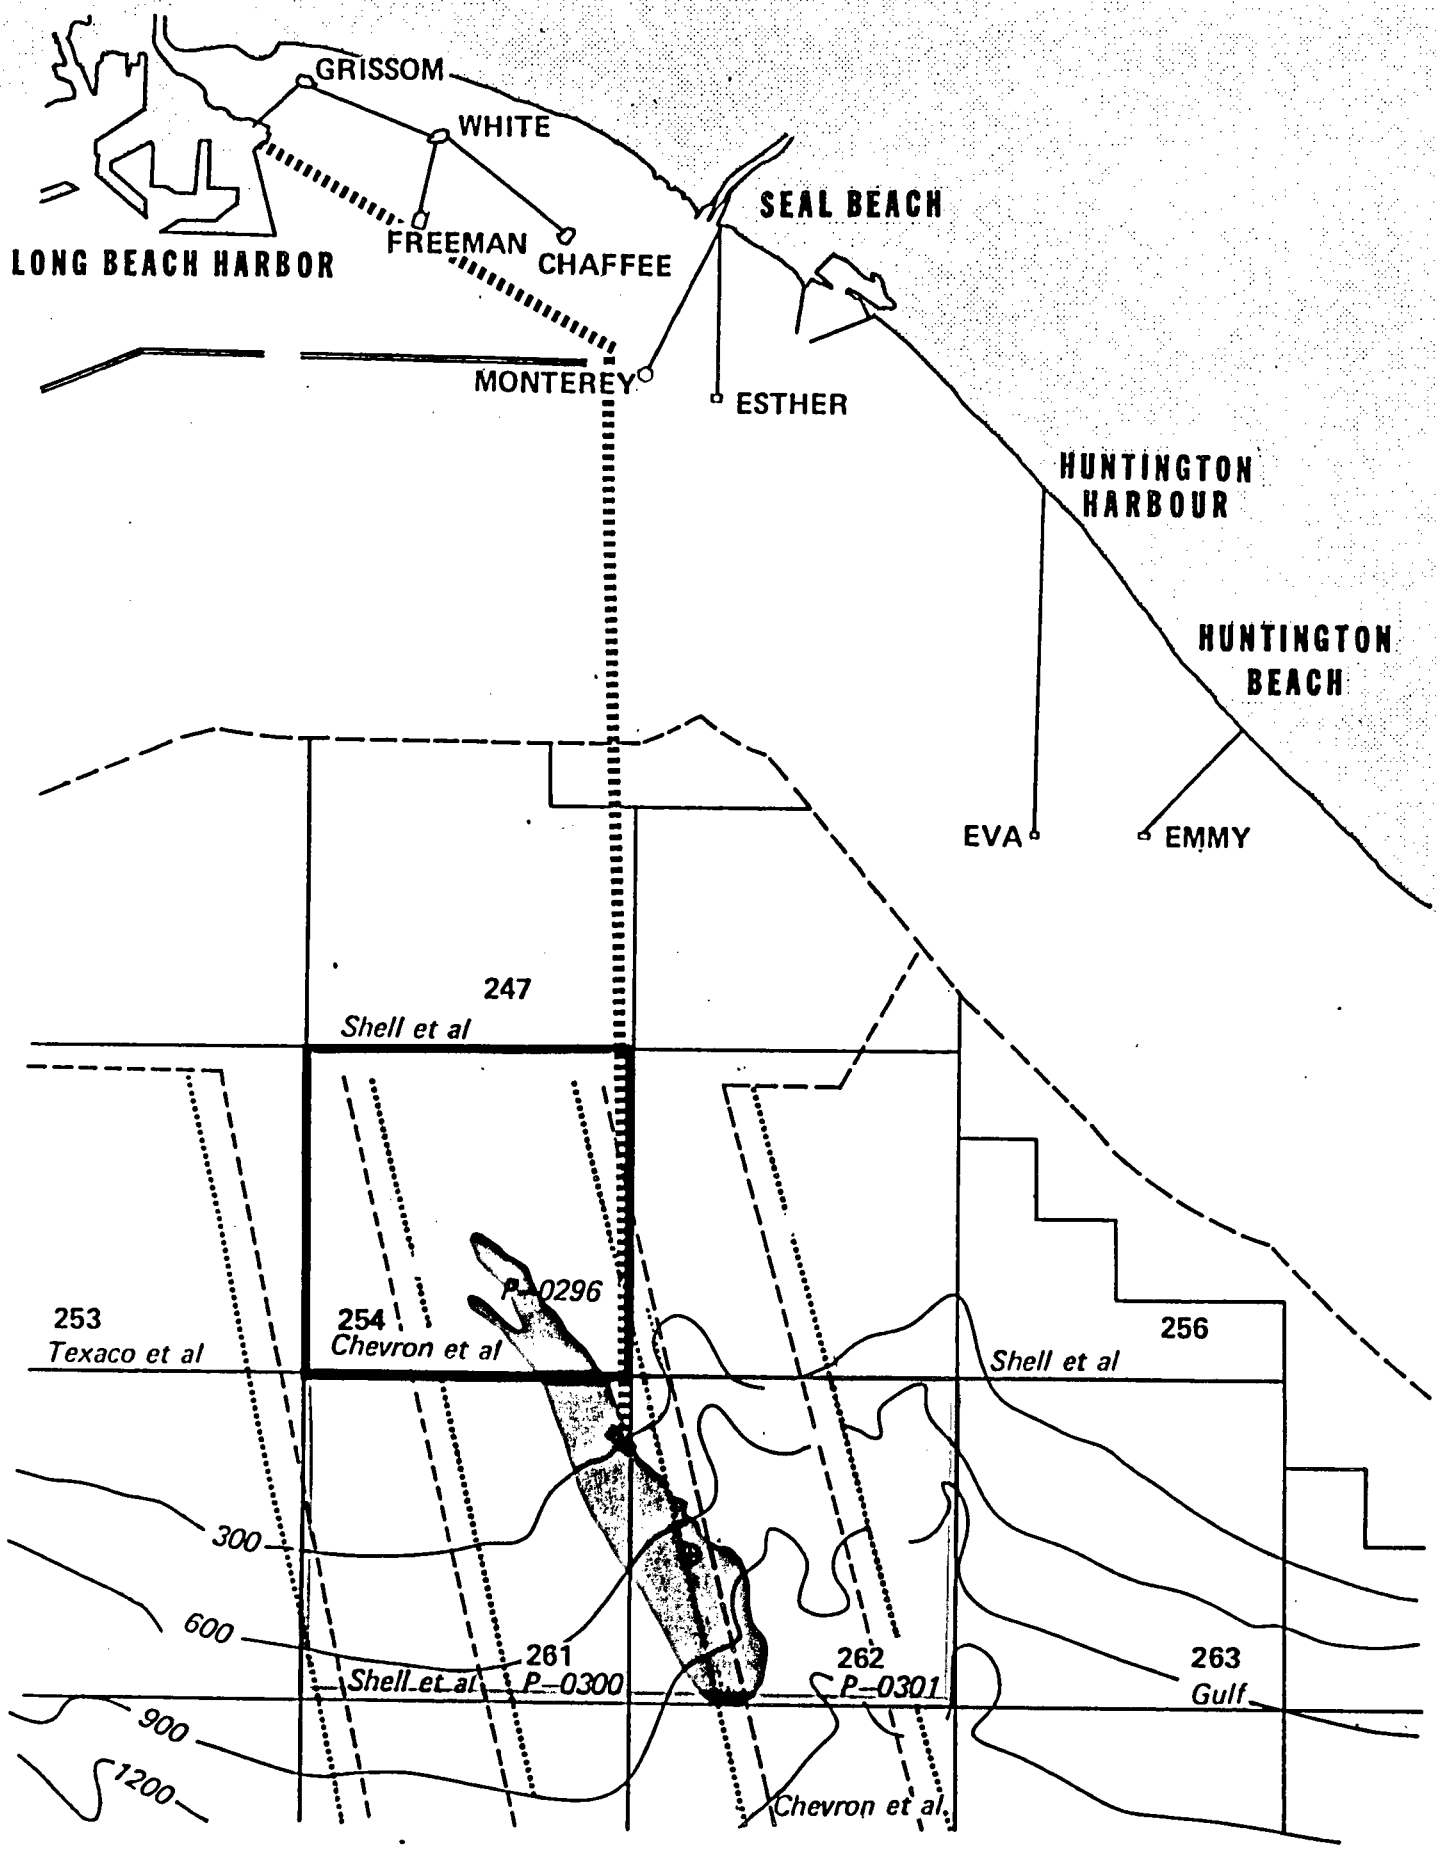
GRISSOM
WHITE
FREEMAN
CHAFFEE
LONG BEACH HARBOR
SEAL BEACH
MONTEREY
ESTHER
HUNTINGTON HARBOUR
HUNTINGTON BEACH
EVA
EMMY
247
Shell et al
253
Texaco et al
254
Chevron et al
P-0296
256
Shell et al
300
600
900
1200
261
Shell et al
P-0300
262
P-0301
263
Gulf
Chevron et al

FIGURE 7–1

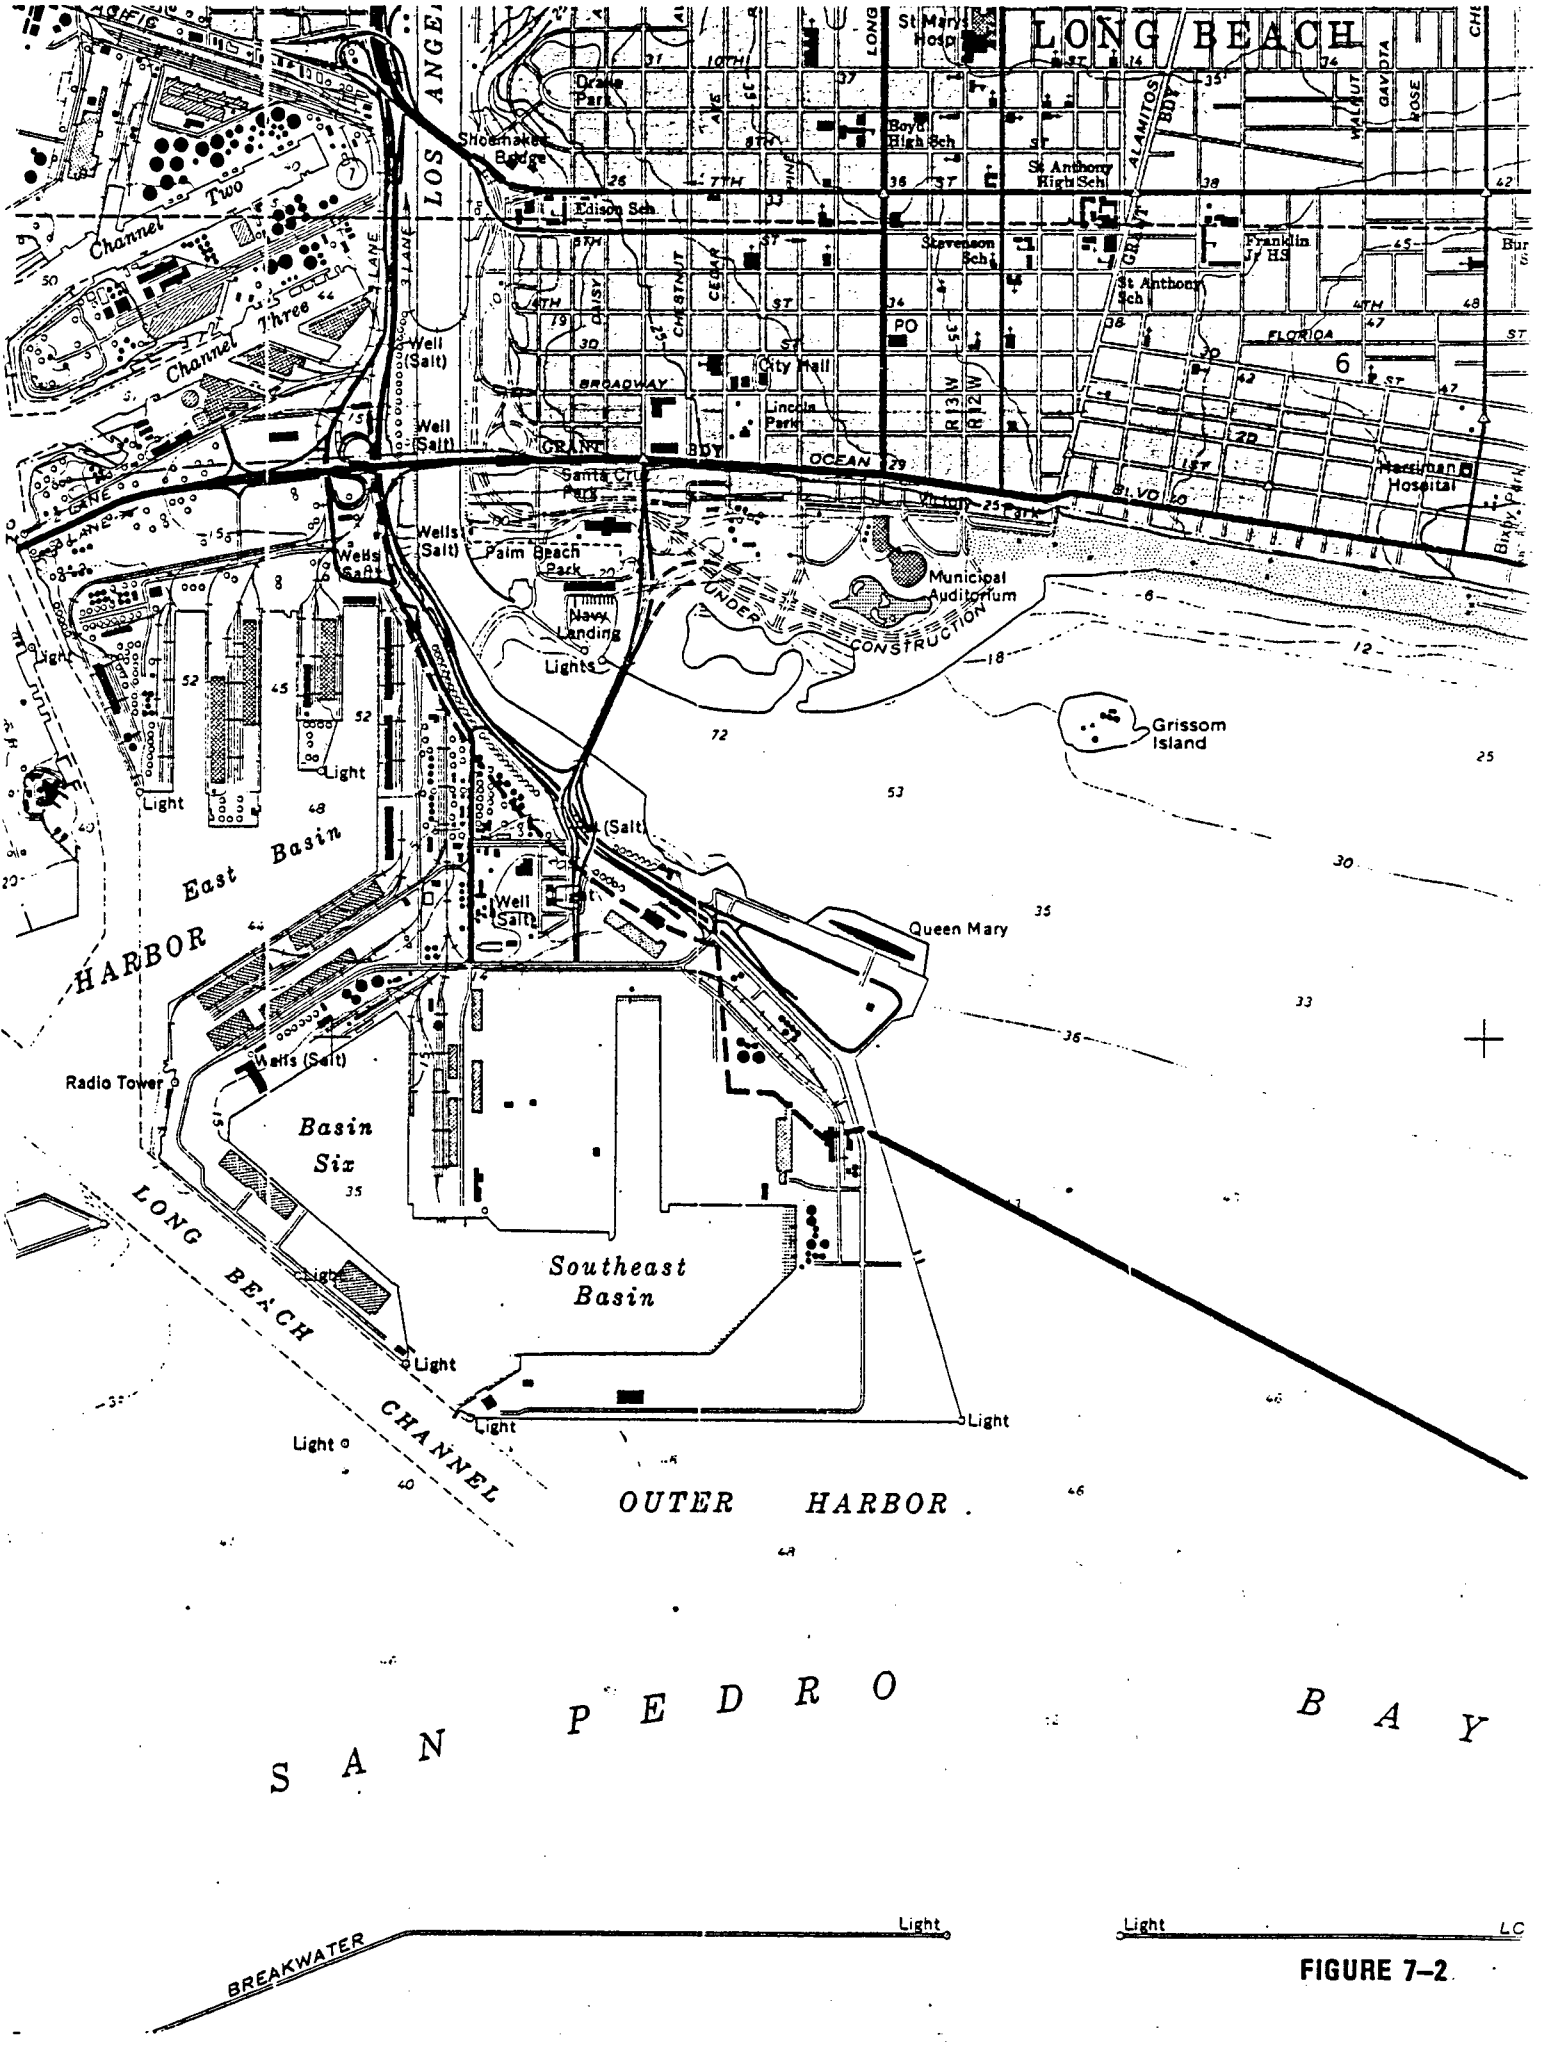
LONG BEACH
St Mary's Hosp
Drake Park
Shoemaker Bridge
Boys High Sch
St Anthony High Sch
Edison Sch
Stevenson Sch
Franklin Jr HS
St Anthony Sch
Channel Two
Channel Three
Channel
Well (Salt)
City Hall
Lincoln Park
Santa Cruz Park
Palm Beach Park
Navy Landing
Lights
Victory Park
Municipal Auditorium
UNDER CONSTRUCTION
Grissom Island
Marshman Hospital
Bixby Park
Light
East Basin
HARBOR
Queen Mary
Radio Tower
Basin Six
Southeast Basin
LONG BEACH CHANNEL
OUTER HARBOR
SAN PEDRO BAY
BREAKWATER

FIGURE 7–2

SECTION VIII

APPENDIX

The following reports, other than Governmental regulations and industry standards, were utilized and referenced in preparation of this Plan of Development:

8.1 MESA[2] (1977) Beta Platform Site Evaluations

8.2 Woodward-Clyde Consultants (1977) Soil Boring, Sampling and Laboratory Testing Program, Tract No. 261, San Pedro Bay, Offshore Southern California.

8.3 Woodward-Clyde Consultants (1977) Soil Boring, Sampling, and Laboratory Testing Program, Tract No. 262, San Pedro Bay, Offshore Southern California.

8.4 Evans-Hamilton, Inc. (1976) An Environmental Design Study for the Southern California Outer Continental Shelf.

8.5 Dames and Moore (1977) Geoseismic Investigation of the Palos Verdes Fault Zone.

8.6 Dames and Moore (1977) Pipeline Route Survey, San Pedro Shelf, California

8.7 Shell Oil Company (1977) Critical Operations and Curtailment Plan.

8.8 Shell Oil Company (1977) Oil Spill Contingency Plan for Beta Unit Development.

8.9 United States Department of the Interior, Bureau of Land Management (1975) Final Environmental Statement, Volumes 1-5; Proposed 1975 Outer Continental Shelf Oil and Gas General Lease Sale, Offshore Southern California (OCS Sale No. 35)

8.10 Greene, H. G., Clarke, S. H., Jr., Field, M. E., Linker, F. I., and Wagner, H. C., (1975) Preliminary Report on the Environmental Geology of Selected Areas of the Southern California Continental Borderland: U. S. Geological Survey open-file report, 75-596, page 50-66.

8.11 Junger, Arne and Wagner, H. C., (1977) Geology of the Santa Monica and San Pedro Basins, California Continental Borderland: U. S. Geological Survey Map MF-820.

8.12 Veder, J. G., Beyer, L.A., Junger, A., Moore, G. W., Roberts, A. E., Taylor, J. C., and Wagner, H. C. (1974) Preliminary Report on the Geology of the Continental Borderland of Southern California: U. S. Geological Survey miscellaneous Field Studies Map MF-624.

8.13 Yerkes, R. F., McCulloh, T. H., Schoellhamer, J. E., and Vedder, J. G., (1965) Geology of the Los Angeles Basin, California -- An Introduction: U. S. Geological Survey Professional Paper 420-a, page 57
